

**ELECTRICALS**GOVT. APPROVED CIVIL, EHV, HT, LT ELECTRICALS,
TELECOM WORKS & LABOUR CONTRACTORSTel : (0288) 2555750
M : 97179 09040, 93774 58805
E mail : excel19680@gmail.com
excel19680@rediffmail.com116, Siddhriath Complex,
1st Floor, Near Indian Bank
K. V. Road, Jamnagar - 361 001

Ref. No. :

Date :

TAX INVOICE

ORIGINAL FOR RECIPIENT

Excel Electrical 116, Siddhriath Complex, 1st Floor, Near Indian Bank, K. V. Road, Jamnagar-361001				NA		
TO,				Invoice No	MAY/22-23/04	
Reliance Projects And Property Management Services Limited				Invoice Date	01-05-22	
First Floor 101, Saffron, Panchwati 5 Rasta, Nr Bank of Baroda, Ambawadi, Ahmedabad- Gujarat-380006				Contract- WO No.	P21/630180228	
				Route Name	NA	
				Site ID	As Par Abstract	
				Site Name	As Par Abstract	
				Vendor Code	399452	
				Supplier's PAN No.	AADFE1348L	
				Supplier's GSTIN	24AADFE1348L1ZJ	
State - State Code as per GST : GUJARAT - 24				Period of Supply	20/03/2022 to 25/03/2022	
GSTIN / Unique ID : 24AAJCR6636B1ZJ				Nature of Supply	Solar Civil Work	
PAN No. : AAJCR6636B				Place of supply of	GUJARAT	
Sr.	SAC : Code	Service Description	Qty (A)	UOM	Rate (Rs. / UoM) (B)	Amount (Rs.) (A*B*C)
1	995428	[3343857] CHRG CVL SOLAR 2M 20-25DT 28 WT 5SBC	1.00	EA	91,901.00	91,901.00
Total Supply Value of Milestone (Basic Value)						91,901.00
Less : Basic value of Advance Paid with Service Tax						
Balance Invoice Value (Net off Advance paid with Tax)						91,901.00
Central GST @ 9%						8,271.09
State GST @ 9%						8,271.09
Total GST Payable on Balance Invoice Value (Net off Advance paid with Service Tax)						16,542.18
Total Invoice Value with GST						108,443.18
Less - Advance paid without Service Tax						
Net Payable Amount						108,443.18
Round Off Net amount						108,443.00
Amount in Words :- One Lakh Eight Thousand Four Hundred Fourty Three Rupees Only						
GST Amount in Words :- Sixteen Thousand Five Hundred Fourty Two Rupees Eighteen Paise						
For:- Excel Electricals PARESHBHAI BHIMJIBHAI LUNAGARIYA Digitally signed by PARESHBHAI BHIMJIBHAI LUNAGARIYA Date: 2022.06.13 16:31:11 +05'30' Authorised Signatory						
Declaration: a) Certified that all the particulars given above are true and correct.						



GOVT. APPROVED CIVIL, EHV - HT - LT ELECTRICALS,
TELECOM WORKS & LABOUR CONTRACTORS

Tel. : (0288) 2555750
M. : 97129 09040, 93774 58805
E-mail: excel19680@rediffmail.com
excel19680@gmail.com

116, Siddhnath Complex,
1st Floor, Near Indian Bank,
K. V. Road, Jamnagar - 361 001

NO CLAIM CERTIFICATE

WO/Contract Order and Frame Order no : P21/630180228

WO/Contract Order and Frame Order Date: 12/02/2022

Circle/State : North Gujarat

Site Name :-As Per Attached BOQ

Scope of Work :- SOLAR 40M GBT CIVIL WORK

Invoice no :- MAY/22-23/04

Invoice Date :- 01-05-2022

We hereby confirm that we have carried out above scope of work in accordance with the, w.o/Contract order and Frame Order scope, terms and instruction of EIC and RS/- (1,08,443=00) (One Lakh Eight Thousand Four Hundred Forty Three Rupees Only) as our final claim. We confirm that there is no further claim by us in respect of the above invoice site & the mention scope of work. The invoice amount will be paid 95% and balance 5% kept as retention and will be paid after defect liability period as per WO/Contract Order and Frame Order terms.

For M/s EXCEL ELECTRICALS

For, EXCEL ELECTRICALS


AUTH. SIGN.

Authorized Signatory

Quantity Certification Summary (QCS)

WO No: P21/630180228

WO Date:- 12/02/2022

Site ID Count:-AS PER BELOW MENTION

This is to certify that following Sites along with Technical Parameter pertaining to ODESC for above mentioned Work Order and of M/s. Excel Electricals being invoiced as per details attached, has been completed the following works.

A) SOLAR CIVIL WORK :- GBT

Site ID	WBS ID	Technical Parameter				
		Tower Type	KIT/NKIT	Tower Height	Building Height	SBC
I-GJ-MTAR-ENB-9023	I-GJ-MTAR-ENB-9023	GBT	NONKTD	40M	NA	5

Certified By:-

Engineer In-Charge (EIC):-

Circle Project Head (CPH):-

For, EXCEL ELECTRICALS


AUTH. SIGN.


ANIL SHAH
MPCM-VADODARA-2
Mob. No. 9374710314



Work Completion Certificate

State	Gujarat		Maintenance Point		
Project Type	93 K ☐	Infill ☐	Growth ☐	Other (Specify)	
Site Type	Own Built ☐	IP Colo ☐	RP1 ☐	BSNL ☐	MAG1 ☐
Tower type	GBT ☐	RTT ☐	RTP ☐	GBM ☐	NBT ☐
	Other (Specify) _____				

This is to certify that work has been completed as per specification given in workorder on the sites mentioned

The required ITP / Checklists are available and verified in system

Site I.D.	I-GJ-MTAR-ENB-9023	SAP ID	I-GJ-MTAR-ENB-9023
-----------	--------------------	--------	--------------------


W.O.Number	P21/630180228	Vendor Name	M/S. EXCEL ELECTRICALS
------------	---------------	-------------	------------------------

No of Sites	1	Completion Date	25-Mar-22
-------------	---	-----------------	-----------

Vendor Representative

Name ~~For, EXCEL ELECTRICALS~~
Sign 
Date _____
AUTH. SIGN.

RJIL Representative

Name 
Sign **ANIL SHAH**
MPCM-VADODARA-2
Mob. No. 9374710314
Date _____

Remarks, if any:

Note : In case of Multiple sites, please attach applicable site details with this certificate

EXCEL ELECTRICALS

SOLAR Civil Quantity Measurement Sheet

Reliance SAP I-GJ-MTAR-ENB-9023		Vendor Name:-Excel Electricals				
TOWER HEIGHT:- 40M GBT		Opco Name:- Reliance -4G				
District:- Vadodara-2		Wo No :- P21/630180228				
Circle Name:- Vadodara-2- Gujarat						
NO	Item Code	Item	Description	Quantity	UOM	Quantity
10	3343857	CHRG CVL SOLAR 2M 20-25DT 28 WT 5SBC	Charges for providing materials and services for execution of CIVIL works for solar work having 28 module at 2m height with 20-25 degree tilt and soil with water table and 5 SBC. The scope of work includes site preparation & restoration, excavation for footing, disposal of surplus earth, backfilling with selected earth, providing and fixing/ laying of steel reinforcement, shuttering, and concrete, transportation, fixing and alignment of stubs/ foundation bolts/ CIP, construction of support wall, grouting related work etc., and other site specific works as per requirement. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge.	1.00	EA	1.00
Excel Engg		AM/CDP				
Name :- For, EXCEL ELECTRICALS		Name :- JEVIN PATEL		Name :- ANIL SHAH		
Signature :- AUTH. SIGN.		Signature :- Mo. No. 9662609867		Signature :- ANIL SHAH		
Date :-		Date :-		Date :-		
		FE-Vadodara-2		Mob. No. 9374710314		

EXCEL ELECTRICALS

SOLAR Civil Quantity Abstract Sheet

Reliance SAP I-GJ-MTAR-ENB-9023				Vendor Name:-Excel Electricals			
TOWER HEIGHT:- 40M GBT				Opco Name:- Reliance -4G			
District:- Vadodara-2				Wo No :- P21/630180228			
Circle Name:- Vadodara-2- Gujarat							
NO		Item Code	Item	Description	Quantity	UNIT RATE	Amount
10		3343857	CHRG CVL SOLAR 2M 20-25DT 28 WT 5SBC	Charges for providing materials and services for execution of CIVIL works for solar work having 28 module at 2m height with 20-25 degree tilt and soil with water table and 5 SBC. The scope of work includes site preparation & restoration, excavation for footing, disposal of surplus earth, backfilling with selected earth, providing and fixing/ laying of steel reinforcement, shuttering, and concrete, transportation, fixing and alignment of stubs/ foundation bolts/ CIP, construction of support wall, grouting related work etc., and other site specific works as per requirement. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge.	1.00	91901.00	91901.00
							91901.00
Excel Engg				AM/CDP	CPH		
Name :- For, EXCEL ELECTRICALS				Name :-	Name :-		
Signature :-				Signature :-	Signature :-		
Date :-				Date :-	Date :-		

[Signature]

ANIL SHAH

MPCM-VADODARA-2

Mob. No. 9374710314

[Signature]

AUTH. SIGN.

PROJECT TITLE:	4G Project
VENDOR NAME:	Ramboll India Pvt Ltd
DOCUMENT TITLE:	Foundation drawing for Solar supporting structure (Panel area: 4x4m) Tilt: 25 deg Ground clearance-2m_SBC: 5T/m^2 (Full water Table)
VENDOR DOCUMENT NO.	15RIT-70/FD/4x4/2GC/25deg-5FWT
VENDOR REVISION NO:	0

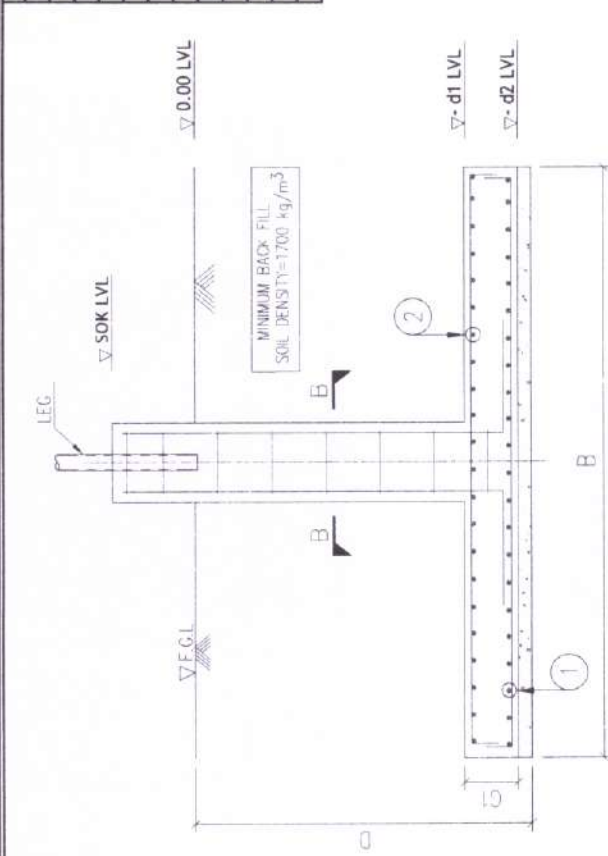
Permission to proceed does not constitute acceptance or approval of Design Detail, Calculations, Analysis, Test Methods or Materials developed OR selected by Vendor, and does NOT relieve Vendor from FULL compliance with Contractual Obligations

- By: Deepa Nail Date: 20.05.2020

Discipline:																									
Equipment No. (if applicable)																									
MR Number (if applicable)	<table border="1"> <tr> <td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td> </tr> </table>																								
Project No	PO No						Cat. Code			Seq. No.			Rev No												
10070	1	1	8	-	6	3	5	1	0	6	5	9	B	0	5	1	2	8	0	0					

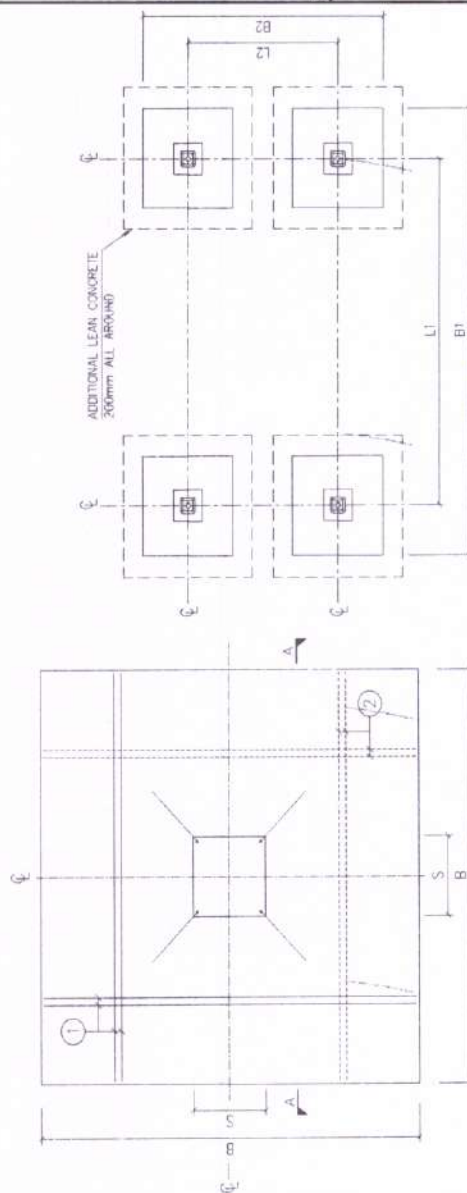
For, EXCEL ELECTRICALS
AUTH. SIGN.

Dimensions	
L1	2.900 m
L2	1.950 m
B	1.050 m
B1	3.950 m
B2	3.000 m
S	0.300 m
G1	0.200 m
SOK	0.300 m
d1	1.250 m
d2	1.450 m
D	1.500 m
Embedded depth	
	0.400 m



FOUNDATION DETAIL
(SECTION "A-A")

SECTION "B-B"



PLAN VIEW
(SHOWING REINFORCEMENT DETAILS IN F405) EXCEL ELECTRICALS

AUTH. SIGN.

General notes

1. This is a generic foundation drawing.
2. The following are the assumed parameters considered during foundation design
 Net safe bearing capacity (NSBC) = $57/\text{m}^2$
 Ground water table = At Ground level
 Depth of foundation = 1.5 m
 Dry density of soil = 1700 kg/m^3
 Angle of internal friction = 10 deg
3. Before commencement of construction work using these designs, the owner/client/civil contractor shall carry out detailed soil investigation of every site.
4. Further, the soil investigation report shall be reviewed by a consultant and certification shall be obtained to ensure conformity between assumed parameters and soil report values before start of construction.
5. The foundation design is applicable only when the considered NSBC is available at or within 1.5 m depth from FGL. In both cases the minimum foundation depth shall be 1.5 m from FGL.
 In case the required nsbc is available beyond 1.5 m depth, this foundation design does not stand applicable.
6. This foundation design shall not be used in case of organic silt, organic clay, or peat layers are found at any depths during soil investigation.
7. This foundation design shall not be adopted at sites where to ground improvement/liquefaction and in this case special foundation shall be done.
8. Any discrepancy in the drawing & site conditions shall be brought to the notice of site engineer & consultant.
9. In case top of pedestal is found to be lower than the road level/high flood level, then base plate encasement shall be taken up in site with site engineer/incharge/consultant.

Foundation Quantity	
Items	Per structure
Concrete	1.44 cum
PCC	0.22 cum
Steel	123.8 kg
Shuttering	10.80 sq.m
Excavation	12.70 cum





Refer DWG. SPS-65GT-C-01 for baseplate and anchor bolt details

Rev	Date	Prepared	Approved
0	09-03-2020	GVR	SSR

RAMBOLL

Tilt angle: 25deg
 Panel Area : 4 x 4 m
 Ground clearance : 2m
 Net SBC : $57/\text{m}^2$
 Water Table : At Ground level
 Isolated Foundation Structural drawing
 DWG No: 15RIT-70/FD/4x4/2GC/25deg-SFWT
 Sheet: 1 of 3
 Released for Construction

BAR BENDING SCHEDULE

#	Shape of Bar	Length of Bar (mm)	Dia. of Bar (mm)	Spacing (mm)	No. of Bars/ leg	No. of Bars/ structure	Unit Weight	Total Weight
1		1050	10	300	10	40	0.62	26.0
2		1050	10	300	10	40	0.62	26.0
4		2050	16	-	4	16	1.58	51.8
5	 Hook - 50mm	900	8	200	10	40	0.39	14.0

* Refer note 1.13

Weight of steel (kg)	117.9
Wastage and splices (kg)	5.9
Total Steel Quantity (kg)	123.8

For, EXCEL ELECTRICALS


AUTH. SIGN.

Rev	Date	Prepared	Approved
0	09-03-2020	GVR	SSR

RAMBOLL

Tilt angle: 25deg

Panel Area : 4 x 4 m

Ground clearance : 2m

Net SBC : 5 T/m²

Water Table : At Ground level

DWG No: 15RIT-70/FD/4x4/2GC/25deg-5FWT

Sheet 2 of 3

Released for Construction

Isolated Foundation Structural drawing

GENERAL NOTES

1. GENERAL & MATERIAL

- 1.1 ALL DIMENSIONS ARE IN "mm" U.O.S.
- 1.2 DO NOT SCALE DRAWING
- 1.3 RCC & LEAN CONCRETE SHALL BE OF GRADE M20 & M10 RESPECTIVELY
- 1.4 FOR AGGRESSIVE SOIL/EXPOSURE CONDITIONS, MINIMUM GRADE OF CONCRETE SHALL BE REFERRED AS PER IS456:2000, TABLE 3 AND 5.
- 1.5 LEAN CONCRETE SHALL BE OF GRADE M10 WITH MIX PROPORTION OF 1:3:6
- 1.6 STEEL GRADE IS F415 U.O.S. AS PER IS 1786 / IS 1159
- 1.7 IF ANY LEVEL DIFFERENCE IN EXISTING GROUND IS FOUND, THEN SOIL EXCAVATION FOR FOUNDATION SHALL BE STARTED WITH REFERENCE TO THE LOWER LEVEL AND THE SOIL SHALL BE BACK FILLED AND COMPACTED UP TO THE TOP MOST LEVEL OF NATURAL GROUND LEVEL TO AVOID SOIL EROSION.
- 1.8 VERIFY THE ADJACENT SITE FEATURES BEFORE EXCAVATION, PROPER CARE SHALL BE TAKEN TO AVOID DAMAGE TO ADJACENT STRUCTURE.
- 1.9 ANY DISCREPANCY IN THE DRAWING (VS) SITE CONDITIONS SHALL BE BROUGHT TO THE NOTICE OF SITE ENGINEER & CONSULTANT (Ramboll India Pvt. Ltd.)
- 1.10 NO FURTHER EXCAVATION/CONSTRUCTION IS ALLOWED WITHIN ZONE OF FOUNDATION AND IF ANY SHALL BE VALIDATED BY CONSULTANT.
- 1.11 REINFORCEMENT SHALL BE SUITABLY ADJUSTED AT SITE TO CLEAR POCKETS, BOLTS, OPENINGS, CUTOUT, ETC. AS APPROVED BY SITE ENGINEER UNLESS OTHERWISE SHOWN IN DRAWING.
- 1.12 THE CONTRACTOR/CLIENT SHALL VERIFY ALL QUANTITY, DIMENSION AND CONDITION WITH SITE AND NOTIFY THE ENGINEER/CONSULTANT, IF ANY DISCREPANCY IN DRAWING AND/OR SPECIFICATION BEFORE PROCEEDING THE WORK.
- 1.13 THE TOTAL LENGTH OF BARS (CUTTING LENGTH) SHALL BE CALCULATED ON THE BASIS OF THE APPROPRIATE BENDING DIMENSIONS WITH CORRECTIONS FOR BENDS AND ALLOWANCES FOR ANCHORAGES.

2. TECHNICAL SPECS

- 2.1 MINIMUM COVER TO THE MAIN REINFORCEMENT FOR COLUMN 50mm
FOR PAD(RAFT SLAB) 50mm
FOR BEAM 50mm.
- 2.2 THE LAP LENGTH/DEVELOPMENT LENGTH OF BARS SHALL BE AS PER
DOC. No.R4G-70-TWC-GEN-PR-049 OR RELEVANT IS CODE.
- 2.3 NO HONEYCOMB/GAP SHALL BE PERMITTED WHILE CONCRETING.
- 2.4 NO CONSTRUCTION JOINT SHALL BE ALLOWED OTHER THAN SPECIFIED.
- 2.5 CONSTRUCTION SHALL BE CARRIED OUT IN ACCORDANCE TO VARIOUS PROVISIONS LAID DOWN IN IS:456/IS:800 STANDARDS.
- 2.6 STRIPPING OF FORMWORK & CURING SHALL BE CARRIED OUT AS PER THE PROVISIONS OF IS:456.

3. EXCAVATION & BACKFILLING

- 3.1 THE SIDE SLOPES FOR EXCAVATION SHALL BE DIVIDED AS PER THE FOLLOWING GUIDELINES:
 - a) FOR SANDY SOILS, SLOPE 1/2H
 - b) FOR CLAYEY SOILS, SLOPE 1V:1H
 - c) FOR HARD STRATA, VERTICAL CUTALTERNATIVELY, SUFFICIENT SHEET PILES/SHORING SHALL BE USED DURING EXCAVATION TO PREVENT SIDE COLLAPSE.
- 3.2 SAND BEDDING/STONE BEDDING SHALL BE PROVIDED IN FOUNDATIONS OF MARSHY AND WET BLACK COTTON SOIL.

- 3.3 IN CASE OF NO GROUND WATER, ALL FOUNDATION PITS SHALL BE SOAKED WITH WATER FOR 24 HOURS AND COMPACTED WELL BEFORE PLACING LEAN CONCRETE.
- 3.4 LOOSE POCKETS OF SOIL (IF ANY FOUND) IN FOUNDATION PITS SHALL BE COMPLETELY REMOVED FOR LOOSE MATERIAL AND FILLED WITH LEAN CONCRETE & COMPACTED WELL BEFORE FOUNDATIONS IS LAID.
- 3.5 FOUNDATION PIT SHALL BE KEPT DRY (FREE FROM WATER) DURING LAYING OF LEAN CONCRETE & RCC AND FURTHER TO A PERIOD OF 48 HOURS (MIN.) FROM THE CONCRETE LAYING TIME
- 3.6 ALL BACK FILLING OF FOUNDATION SHOULD BE DONE WITH WELL COMPACTED MURRUM SOIL
- 3.7 THE BACK FILLING MATERIALS SHOULD BE CLEAN AND FREE FROM ORGANIC OR OTHER FOREIGN MATERIALS.
- 3.8 SOIL BACK FILL SHALL BE DONE IN LAYERS OF APPROX 150-200mm, EACH LAYERS SHALL BE DENSELY COMPACTED BY SPRINKLING MINIMUM QUANTITY OF WATER AS NECESSARY FOR PROPER COMPACTION AND MINIMUM BACKFILL SOIL DENSITY SHALL BE 1700 kg/m³
- 3.9 CARE SHALL BE TAKEN THAT THE BACK FILLING IS STARTED FROM THE CENTRE TOWARDS THE OUTER ENDS
- 3.10 AFTER BACK FILLING 50mm HIGH EARTHEN EMBANKMENT(BUND) TO BE MADE ALONG THE SIDES OF EXCAVATED PITS AND SUFFICIENT WATER WILL BE POURED OVER THE BACK FILLED EARTH FOR ATLEAST 24HRS.
- 3.11 FINISHED GROUND LEVEL AT COLUMN/CHIMNEY SHOULD BE SLOPED AWAY, WITH SLOPE OF 1:3 TO PREVENT ACCUMULATION OR PONDING OF WATER
- 3.12 SURFACE DRAINAGE OF THE PLOT SHOULD BE MADE SO AS TO AVOID WATER LOGGING IN THE PLOT, IN PARTICULAR AROUND THE FOUNDATION
- 3.13 IN CASE TOP OF PEDESTAL IS FOUND TO BE LOWER THAN THE ROAD LEVEL/HIGH FLOOD LEVEL, THEN BASE PLATE ENCASEMENT SHALL BE TAKEN UP IN CONSULTATION WITH THE SITE ENGINEER/INCHARGE/CONSULTANT
- 3.14 EXCAVATION PLAN & VOLUME SHOWN IN DRAWING IS INDICATIVE ONLY & THIS IS APPLICABLE FOR NORMAL SOIL CONDITIONS. IT MAY VARY, AS PER SITE CONDITION & STRATA ENCOUNTERED.

4. TEMPLATE ASSEMBLY/ GROUTING

- 4.1 VERIFY BOLT, NUT SIZE AND LENGTH AS PER TEMPLATE/BASE ASSEMBLY DRAWING.
- 4.2 CHECK THE INTEGRITY OF BOLT AND NUT BEFORE EXECUTION AT SITE. IF ANY PLAY FOUND, CONSULT SITE ENGINEER/CONSULTANT
- 4.3 GROUTING UNDER BASE PLATE HAS TO BE DONE WITH FREE FLOW NON SHRINK GROUT HAVING MINIMUM STRENGTH AS THAT OF CONCRETE.

LEGEND

U.O.S. - UNLESS OTHERWISE SPECIFIED

↖ - INDICATES CHAIR LOCATIONS

F.G.L - FINISHED GROUND LEVEL

E.G.L - EXISTING GROUND LEVEL

T & B + TOP AND BOTTOM

TOS - TOP OF SLAB

BOS - BOTTOM OF SLAB

For, EXCEL ELECTRICALS.

AUTH. SIGN.

Rev	Date	Prepared	Approved
0	09-03-2020	GVR	SSR

RAMBOLL

Tilt angle: 25deg

Panel Area : 4 x 4 m

Ground clearance : 2m

Net SBC : 5 T/m²

DWG No: 15RIT-70/FD/4x4/ZGC/25deg-5PWT

Sheet 3 of 3

Released for Construction

Water Table : At Ground level

Isolated Foundation Structural drawing

PROJECT TITLE:	4G Project
VENDOR NAME:	Ramboll India Pvt Ltd
DOCUMENT TITLE:	Foundation drawing for Solar supporting structure (Panel area: 4x10m) Tilt: 25 deg Ground clearance- 2m_SBC: 5T/m^2 (Full water Table)
VENDOR DOCUMENT NO.	15RIT-70/FD/4x10/2GC/25deg-5FWT
VENDOR REVISION NO:	0

Permission to proceed does not constitute acceptance or approval of Design Detail, Calculations, Analysis, Test Methods or Materials developed OR selected by Vendor, and does NOT relieve Vendor from FULL compliance with Contractual Obligations

- By: Deepa Nair Date: 21.03.2023

Discipline:																				
Equipment No. (if applicable)																				
MR Number (if applicable)																				
Project No	PO No										Cat. Code			Seq. No.		Rev No				
10070	1	1	8	-	6	3	5	1	0	6	5	9	B	0	5	1	4	0	0	0

For, EXCEL ELECTRICALS


AUTH. SIGN.

Dimensions	
L1	3.900 m
L2	1.950 m
B	1.500 m
B1	9.300 m
B2	3.450 m
S	0.300 m
G1	0.200 m
SOK	0.300 m
d1	1.250 m
d2	1.450 m
D	1.500 m
Embedded depth	0.400 m

General notes

- This is a generic foundation drawing.
- The following are the assumed parameters considered during foundation design

Net safe bearing capacity (NSBC) = $57/m^2$
 Ground water table = At Ground level
 Depth of foundation = 1.5 m
 Dry density of soil = 1700 kg/m^3
 Angle of internal friction = 10°
 Before commencement of construction work using these designs, the owner/client/civil contractor shall carry out detailed soil investigation of every site.

4. Further, the soil investigation report shall be reviewed by a consultant and certification shall be obtained to ensure conformity between assumed parameters and soil report values before start of construction.
 5. The foundation design is applicable only when the considered NSBC is available at or within 1.5 m depth from FGL. In both cases the minimum foundation depth shall be 1.5 m from FGL.
 In case the required NSBC is available beyond 1.5 m depth, this foundation design does not stand applicable.
 6. This foundation design shall not be used in case of organic silt, organic clay, or peat layers are found at any depths during soil investigation.
 7. This foundation design shall not be adopted at sites where to ground improvement/liquefaction and in this case special foundation shall be done.

8. Any discrepancy in the drawing & site conditions shall be brought to the notice of site engineer & consultant.
 9. In case top of pedestal is found to be lower than the road level/high flood level, then base plate encasement shall be taken up in site with the site engineer/incharge/consultant.

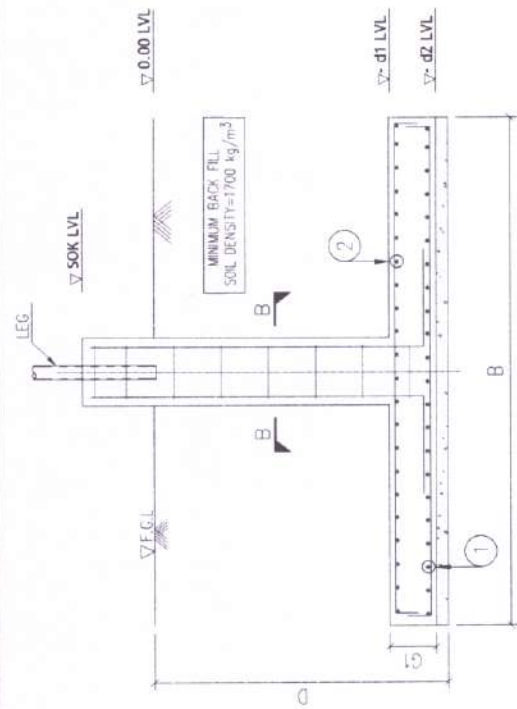
Foundation Quantity	
Items	Per structure
Concrete	3.54 cum
PCC	0.68 cum
Steel	252.3 kg
Shuttering	18.36 sq.m
Excavation	32.50 cum

Note: For excavation, 200mm extra considered over pad size
 Refer DWG. SPS-65GT-C-01 for baseplate and anchor bolt details




Rev 0
 Date 09-03-2020
 Prepared GVR
 Approved SSR

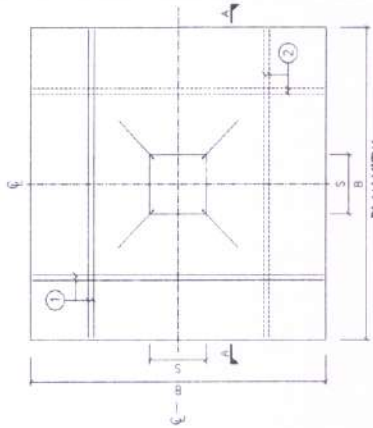
Tilt angle : 25°
 Panel Area : $4 \times 10 \text{ m}$
 Ground clearance : 2 m
 Net SBC : $57/m^2$
 Water Table : At Ground level
 Isolated Foundation Structural Drawing
 DWG No: 15RIT-70/FD/4x10/25deg/ZGC-SFWT
 Sheet 1 of 3
 Released for Construction



FOUNDATION DETAIL
 (SECTION "A-A")

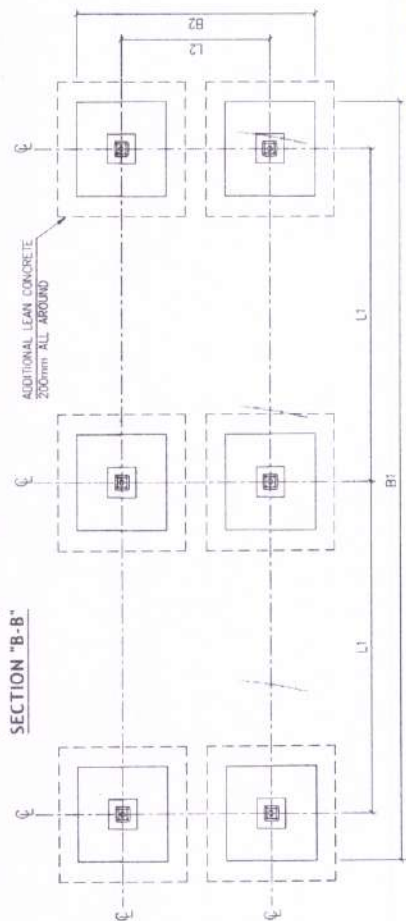


SECTION "B-B"



PLAN VIEW

(SHOWING REINFORCEMENT DETAILS IN PAD)






EXCAVATION PLAN

For, EXCEL ELECTRICALS

AUTH. SIGN.


BAR BENDING SCHEDULE

#	Shape of Bar	Length of Bar (mm)	Dia. of Bar (mm)	Spacing (mm)	No. of Bars/ leg	No. of Bars/ structure	Unit Weight	Total Weight
1		1500	10	300	12	72	0.62	67.0
2		1500	10	300	12	72	0.62	67.0
4		2250	16	-	4	24	1.58	85.3
5	 Hook - 50mm	900	8	200	10	60	0.39	21.1

* Refer note 1.13

Weight of steel (kg)	240.3
Wastage and splices (kg)	12.0
Total Steel Quantity (kg)	252.3

For, EXCEL ELECTRICALS.


AUTH. SIGN.

Rev	Date	Prepared	Approved
0	09-03-2020	GVR	SSR

RAMBOLL

Tilt angle : 25deg

Panel Area : 4 x 10 m

Ground clearance : 2 m

Net SBC : 5 T/m²

Water Table : At Ground level

DWG No: 15RIT-70/FD/4x10/25deg/2GC-5FWT

Sheet 2 of 3

Released for Construction

Isolated Foundation Structural drawing

GENERAL NOTES

1. GENERAL & MATERIAL

- 1.1 ALL DIMENSIONS ARE IN "mm" U.O.S
 - 1.2 DO NOT SCALE DRAWING
 - 1.3 RCC & LEAN CONCRETE SHALL BE OF GRADE M20 & M10 RESPECTIVELY.
 - 1.4 FOR AGGRESSIVE SOIL/EXPOSURE CONDITIONS, MINIMUM GRADE OF CONCRETE SHALL BE REFERRED AS PER IS:456-2000, TABLE 3 AND 5.
 - 1.5 LEAN CONCRETE SHALL BE OF GRADE M10 WITH MIX PROPORTION OF 1:3:6
 - 1.6 STEEL GRADE IS Fe415 U.O.S. AS PER IS:1786 / IS:1159
 - 1.7 IF ANY LEVEL DIFFERENCE IN EXISTING GROUND IS FOUND, THEN SOIL EXCAVATION FOR FOUNDATION SHALL BE STARTED WITH REFERENCE TO THE LOWER LEVEL AND THE SOIL SHALL BE BACK FILLED AND COMPACTED UP TO THE TOP MOST LEVEL OF NATURAL GROUND LEVEL TO AVOID SOIL EROSION.
 - 1.8 VERIFY THE ADJACENT SITE FEATURES BEFORE EXCAVATION, PROPER CARE SHALL BE TAKEN TO AVOID DAMAGE TO ADJACENT STRUCTURE
 - 1.9 ANY DISCREPANCY IN THE DRAWING (VS) SITE CONDITIONS SHALL BE BROUGHT TO THE NOTICE OF SITE ENGINEER & CONSULTANT (Ramboll India Pvt. Ltd.)
 - 1.10 NO FURTHER EXCAVATION/CONSTRUCTION IS ALLOWED WITHIN ZONE OF FOUNDATION AND IF ANY SHALL BE VALIDATED BY CONSULTANT.
 - 1.11 REINFORCEMENT SHALL BE SUITABLY ADJUSTED AT SITE TO CLEAR POCKETS, BOLTS, OPENINGS, CUTOUT, ETC. AS APPROVED BY SITE ENGINEER UNLESS OTHERWISE SHOWN IN DRAWING.
 - 1.12 THE CONTRACTOR/CLIENT SHALL VERIFY ALL QUANTITY, DIMENSION AND CONDITION WITH SITE AND NOTIFY THE ENGINEER/CONSULTANT. IF ANY DISCREPANCY IN DRAWING AND/OR SPECIFICATION BEFORE PROCEEDING THE WORK.
 - 1.13 THE TOTAL LENGTH OF BARS (CUTTING LENGTH) SHALL BE CALCULATED ON THE BASIS OF THE APPROPRIATE BENDING DIMENSIONS WITH CORRECTIONS FOR BENDS AND ALLOWANCES FOR ANCHORAGES
- ### 2. TECHNICAL SPECS
- 2.1 MINIMUM COVER TO THE MAIN REINFORCEMENT
FOR COLUMN 50mm
FOR PAD/RAFT SLAB) 50mm
FOR BEAM 50mm.
 - 2.2 THE LAP LENGTH/DEVELOPMENT LENGTH OF BARS SHALL BE AS PER
DOC. No.R40-70-TWC-GEN-PR-049 OR RELEVANT IS CODE.
 - 2.3 NO HONEYCOMB/GAP SHALL BE PERMITTED WHILE CONCRETING.
 - 2.4 NO CONSTRUCTION JOINT SHALL BE ALLOWED OTHER THAN SPECIFIED.
 - 2.5 CONSTRUCTION SHALL BE CARRIED OUT IN ACCORDANCE TO VARIOUS PROVISIONS LAID DOWN IN IS-456/IS:800 STANDARDS.
 - 2.6 STRIPPING OF FORMWORK & CURING SHALL BE CARRIED OUT AS PER THE PROVISIONS OF IS-456.

3. EXCAVATION & BACKFILLING

- 3.1 THE SIDE SLOPES FOR EXCAVATION SHALL BE DIVIDED AS PER THE FOLLOWING GUIDELINES.
 - a) FOR SANDY SOILS, SLOPE 1V:2H
 - b) FOR CLAYEY SOILS, SLOPE 1V:1H
 - c) FOR HARD STRATA, VERTICAL CUTALTERNATIVELY, SUFFICIENT SHEET PILES/SHORING SHALL BE USED DURING EXCAVATION TO PREVENT SIDE COLLAPSE.
- 3.2 SAND BEDDING/STONE BEDDING SHALL BE PROVIDED IN FOUNDATIONS OF MARSHLY AND WET BLACK COTTON SOIL

For, EXCEL ELECTRICALS.
AUTH. SIGN.

- 3.3 IN CASE OF NO GROUND WATER, ALL FOUNDATION PITS SHALL BE SOAKED WITH WATER FOR 24 HOURS AND COMPACTED WELL BEFORE PLACING LEAN CONCRETE.
- 3.4 LOOSE POCKETS OF SOIL (IF ANY FOUND) IN FOUNDATION PITS SHALL BE COMPLETELY REMOVED FOR LOOSE MATERIAL AND FILLED WITH LEAN CONCRETE & COMPACTED WELL BEFORE FOUNDATIONS IS LAID.
- 3.5 FOUNDATION PIT SHALL BE KEPT DRY (FREE FROM WATER) DURING LAYING OF LEAN CONCRETE & RCC AND FURTHER TO A PERIOD OF 48 HOURS (MIN.) FROM THE CONCRETE LAYING TIME
- 3.6 ALL BACK FILLING OF FOUNDATION SHOULD BE DONE WITH WELL COMPACTED MURRUM SOIL
- 3.7 THE BACK FILLING MATERIALS SHOULD BE CLEAN AND FREE FROM ORGANIC OR OTHER FOREIGN MATERIALS.
- 3.8 SOIL BACK FILL SHALL BE DONE IN LAYERS OF APPROX. 150-200mm, EACH LAYERS SHALL BE DENSELY COMPACTED BY SPRINKLING MINIMUM QUANTITY OF WATER AS NECESSARY FOR PROPER COMPACTION AND MINIMUM BACKFILL SOIL DENSITY SHALL BE 1700 kg/m³
- 3.9 CARE SHALL BE TAKEN THAT THE BACK FILLING IS STARTED FROM THE CENTRE TOWARDS THE OUTER ENDS
- 3.10 AFTER BACK FILLING 50mm HIGH EARTHEN EMBANKMENT(BUND) TO BE MADE ALONG THE SIDES OF EXCAVATED PITS AND SUFFICIENT WATER WILL BE POURED OVER THE BACK FILLED EARTH FOR ATLEAST 24-HRS.
- 3.11 FINISHED GROUND LEVEL AT COLUMN/CHIMNEY SHOULD BE SLOPED AWAY, WITH SLOPE OF 1:3 TO PREVENT ACCUMULATION OR PONDING OF WATER
- 3.12 SURFACE DRAINAGE OF THE PLOT SHOULD BE MADE SO AS TO AVOID WATER LOGGING IN THE PLOT, IN PARTICULAR AROUND THE FOUNDATION
- 3.13 IN CASE TOP OF PEDESTAL IS FOUND TO BE LOWER THAN THE ROAD LEVEL/HIGH FLOOD LEVEL, THEN BASE PLATE ENCASEMENT SHALL BE TAKEN UP IN CONSULTATION WITH THE SITE ENGINEER/INCHARGE/CONSULTANT.
- 3.14 EXCAVATION PLAN & VOLUME SHOWN IN DRAWING IS INDICATIVE ONLY & THIS IS APPLICABLE FOR NORMAL SOIL CONDITIONS. IT MAY VARY, AS PER SITE CONDITION & STRATA ENCOUNTERED.

4. TEMPLATE ASSEMBLY / GROUTING

- 4.1 VERIFY BOLT, NUT SIZE AND LENGTH AS PER TEMPLATE/BASE ASSEMBLY DRAWING.
- 4.2 CHECK THE INTEGRITY OF BOLT AND NUT BEFORE EXECUTION AT SITE. IF ANY PLAY FOUND, CONSULT SITE ENGINEER/CONSULTANT
- 4.3 GROUTING UNDER BASE PLATE HAS TO BE DONE WITH FREE FLOW NON SHRINK GROUT HAVING MINIMUM STRENGTH AS THAT OF CONCRETE.

LEGEND

U.O.S. - UNLESS OTHERWISE SPECIFIED.
→ - INDICATES CHAIR LOCATIONS

F.G.L - FINISHED GROUND LEVEL
E.G.L - EXISTING GROUND LEVEL
T & B - TOP AND BOTTOM
TOS - TOP OF SLAB
BOS - BOTTOM OF SLAB

RAMBOLL

Rev	Date	Prepared	Approved
0	09-03-2020	GVR	SSR

Tilt angle : 25deg

Panel Area : 4 x 10 m

Ground clearance : 2 m

Net SBC : 5 T/m²

Water Table : At Ground level

DWG No: 15RIT-70/FD/4x10/25deg/20C-SFWT

Sheet 3 of 3

Released for Construction

Isolated Foundation Structural drawing



Geo Technical Solutions

Om Geo Tech Services

(ISO 9001 CERTIFIED LAB)

NADIAD

CIVIL ENGINEERING CONSULTANCY & TESTING LAB

■ Civil Engineering Material Testing ■ Destructive & Non Destructive Testing ■ Pile & Load Test
■ BI & BBD in Highway Testing ■ Physical & Resistivity Survey

Test Report on Compressive Strength of Concrete Cubes

E:\OM GEO TECH\JIO\TRF 019-Excel.xlsx\CC Cube

Discipline/Group » Mechanical-Buildings Material
Sample ID No. » 01/20220424/CC Cube
Report Ref No » OGTS-2022-23/01/20220424/CC Cube

ULR-TC872622000001742F

Date of Report » 07-May-22

Customer » Reliance Jio
Name of Work » Site ID:- I-GJ-MATR-ENB-9023
Agency » Excel Electricals, Jamnagar

Witness Person » Mr. Jayeshbhai Panchal
Date of Sample Received » 25-Apr-22
Material Received » Concrete Cubes
Method of Test » IS 516-1959 RA - 2018 Clause 5.0

Element » Column

Sr. No.	Sample ID	Date of Casting **	Date of Testing	Required Age of Test (days)	Grade of Concrete **	Length (mm)	Width (mm)	Height (mm)	Max.Load at Failure, (KN)	Weight of Spec. (Kg)	Comp. Strength, (N/mm ²)	Sample Density (Kg/m ³)
1	Cube 1	24-Apr-22	07-May-22	13	M 20	150.00	150.00	150.00	717.2	8.84	31.88	2620.1
2	Cube 2					150.00	150.00	150.00	654.3	8.95	29.08	2653.0
3	Cube 3					150.00	150.00	150.00	705.3	8.98	31.35	2660.4
Average											30.77	2644.5

» **Remark :-** The Average of Three Samples Values shall be taken as the Representative of the Batch provided the individual variation is not more than $\pm 15\%$ of the Average. Otherwise repeat tests shall be made as per IS 516-Clause-5.6

Requirements as per IS 456:2000-(Reaffirmed-2016)Table No.2 (Clause 6.1, 9.2.2, 15.1.1, and 36.1)

Grade of Concrete	M10	M15	M20	M25	M30	M35	M40	M45
Accepted Strength on 28 days of curing for Nominal Mix, N/mm ²	10	15	20	25	30	35	40	45

" M-10 is a Nominal Mix Concrete

•• End of Report ••

Note :-

- The results are given only for the sample submitted by the Customer.
- The test report shall not be reproduced except in full, without written approval of the laboratory.
- Om Geo Tech Services is not responsible for any kind of interpretation of test results
- The results/report is not used for publicity.
- ** As informed by client.



Doc ID : FMT-TST-01 / Page 1/1



Nadiad - Dabhan Road,
Nr. Bhutia Bunglow, Nr. MGVC Office,
NADIAD - 387 320



omgeotech18@gmail.com



94273 16024 , 99987 89919



Geo Technical Solutions

Om Geo Tech Services

(ISO 9001 CERTIFIED LAB)

NADIAD

CIVIL ENGINEERING CONSULTANCY & TESTING LAB

■ Civil Engineering Material Testing ■ Destructive & Non Destructive Testing ■ Pile & Load Test
■ BI & BBD in Highway Testing ■ Physical & Resistivity Survey

Test Report on Compressive Strength of Concrete Cubes

FROM GEO TECH/20/23/01/20220424/CC Cube

Discipline/Group » Mechanical-Buildings Material
Sample ID No. » 01/20220424/CC Cube
Report Ref No » OGTS-2022-23/01/20220424/CC Cube

ULR-TC872622000001741F

Date of Report » 07-May-22

Customer » Reliance Jio
Name of Work » Site ID:- I-GJ-MATR-ENB-9023
Agency » Excel Electricals, Jamnagar

Witness Person » Mr. Jayeshbhai Panchal
Date of Sample Received » 25-Apr-22
Material Received » Concrete Cubes
Method of Test » IS 516-1959 RA - 2018 Clause 5.0

Element » Raft

Sr. No.	Sample ID	Date of Casting **	Date of Testing	Required Age of Test (days)	Grade of Concrete **	Length (mm)	Width (mm)	Height (mm)	Max.Load at Failure, (KN)	Weight of Spec. (Kg)	Comp. Strength, (N/mm ²)	Sample Density (Kg/m ³)
1	Cube 1	24-Apr-22	07-May-22	13	M 20	150.00	150.00	150.00	442.2	8.67	19.65	2568.3
2	Cube 2					150.00	150.00	150.00	674.3	8.82	29.97	2612.7
3	Cube 3					150.00	150.00	150.00	648.3	8.63	28.81	2557.0
Average											26.15	2579.4

» **Remark :-** The Average of Three Samples Values shall be taken as the Representative of the Batch provided the individual variation is not more than $\pm 15\%$ of the Average. Otherwise repeat tests shall be made as per IS 516-Clause-5.6

Requirements as per IS 456:2000-(Reaffirmed-2016)Table No.2 (Clause 6.1, 9.2.2, 15.1.1, and 36.1)

Grade of Concrete	M10	M15	M20	M25	M30	M35	M40	M45
Accepted Strength on 28 days of curing for Nominal Mix, N/mm ²	10	15	20	25	30	35	40	45

** M-10 is a Nominal Mix Concrete

•• End of Report ••

Note :-

- The results are given only for the sample submitted by the Customer.
- The test report shall not be reproduced except in full, without written approval of the laboratory.
- Om Geo Tech Services is not responsible for any kind of interpretation of test results
- The results/report is not used for publicity.
- ** As informed by client



Doc ID : FMT-TST-01 / Page 1/1



Nadiad - Dabhan Road,
Nr. Bhutia Bunglow, Nr. MGVC Office,
NADIAD - 387 320



omgeotech18@gmail.com



94273 16024 , 99987 89919



Geo Technical Solutions

Om Geo Tech Services

(ISO 9001 CERTIFIED LAB)

NADIAD

CIVIL ENGINEERING CONSULTANCY & TESTING LAB

■ Civil Engineering Material Testing ■ Destructive & Non Destructive Testing ■ Pile & Load Test
■ BI & BBD in Highway Testing ■ Physical & Resistivity Survey

Test Report on Compressive Strength of Concrete Cubes

E:\OM GEO TECH\2022\TST 04-Jun-22\CC Cube

Discipline/Group » Mechanical-Buildings Material
Sample ID No. » 01/20220424/CC Cube
Report Ref No » OGTS-2022-23/01/20220424/CC Cube

ULR-TC872622000002160F

Date of Report » 04-Jun-22

Customer » Reliance Jio
Name of Work » Site ID:- I-GJ-MATR-ENB-9023
Agency » Excel Electricals, Jamnagar

Witness Person » Mr. Jayeshbhai Panchal
Date of Sample Received » 25-Apr-22
Material Received » Concrete Cubes
Method of Test » IS 516-1959 RA - 2018 Clause 5.0

Element » Column

Sr. No.	Sample ID	Date of Casting	Date of Testing	Required Age of Test (days)	Grade of Concrete **	Length (mm)	Width (mm)	Height (mm)	Max.Load at Failure, (KN)	Weight of Spec. (Kg)	Comp. Strength, (N/mm ²)	Sample Density (Kg/m ³)
1	Cube 1	24-Apr-22	04-Jun-22	41	M 20	150.00	150.00	150.00	830.1	8.93	36.89	2645.9
2	Cube 2					150.00	150.00	150.00	653.2	8.89	29.03	2634.7
3	Cube 3					150.00	150.00	150.00	587.2	8.82	26.10	2614.5
Average											30.67	2631.7

» **Remark :-** The Average of Three Samples Values shall be taken as the Representative of the Batch provided the individual variation is not more than $\pm 15\%$ of the Average. Otherwise repeat tests shall be made as per IS 516-Clause-5.6

Requirements as per IS 456:2000-(Reaffirmed-2016) Table No.2 (Clause 6.1, 9.2.2, 15.1.1, and 36.1)

Grade of Concrete	M10	M15	M20	M25	M30	M35	M40	M45
Accepted Strength on 28 days of curing for Nominal Mix, N/mm ²	10	15	20	25	30	35	40	45

** M-10 is a Nominal Mix Concrete

•• End of Report ••

Note :-

- The results are given only for the sample submitted by the Customer.
- The test report shall not be reproduced except in full, without written approval of the laboratory.
- Om Geo Tech Services is not responsible for any kind of interpretation of test results
- The results/report is not used for publicity.
- ** As informed by client



Doc-ID: FMT-TST-01 / Page 1/1



Nadiad - Dabhan Road,
Nr. Bhutia Bunglow, Nr. MGVL Office,
NADIAD - 387 320



omgeotech18@gmail.com



94273 16024 , 99987 89919



Test Report on Compressive Strength of Concrete Cubes

ENOM GEO TECH (TIF) (NFI-Exot-Id) CC Cube

Discipline/Group » Mechanical-Buildings Material
Sample ID No. » 01/20220424/CC Cube
Report Ref No » OGTS-2022-23/01/20220424/CC Cube

ULR-TC872622000002159F

Date of Report » 04-Jun-22

Customer » Reliance Jio
Name of Work » Site ID:- I-GJ-MATR-ENB-9023
Agency » Excel Electricals, Jamnagar

Witness Person » Mr. Jayeshbhai Panchal
Date of Sample Received » 25-Apr-22
Material Received » Concrete Cubes
Method of Test » IS 516-1959 RA - 2018 Clause 5.0

Element » Raft

Sr. No.	Sample ID	Date of Casting	Date of Testing	Required Age of Test (days)	Grade of Concrete **	Length (mm)	Width (mm)	Height (mm)	Max.Load at Failure, (KN)	Weight of Spec. (Kg)	Comp. Strength, (N/mm ²)	Sample Density (Kg/m ³)
1	Cube 1	24-Apr-22	04-Jun-22	41	M 20	150.00	150.00	150.00	836.8	8.81	37.19	2611.6
2	Cube 2					150.00	150.00	150.00	899.2	8.67	39.96	2567.4
3	Cube 3					150.00	150.00	150.00	756.6	8.95	33.63	2651.3
Average											36.93	2610.1

» Remark :- The Average of Three Samples Values shall be taken as the Representative of the Batch provided the individual variation is not more than $\pm 15\%$ of the Average. Otherwise repeat tests shall be made as per IS 516-Clause-5.6

Requirements as per IS 456:2000-(Reaffirmed-2016) Table No.2 (Clause 6.1, 9.2.2, 15.1.1, and 36.1)

Grade of Concrete	M10	M15	M20	M25	M30	M35	M40	M45
Accepted Strength on 28 days of curing for Nominal Mix, N/mm ²	10	15	20	25	30	35	40	45

** M-10 is a Nominal Mix Concrete

** End of Report **

Note :-

- The results are given only for the sample submitted by the Customer.
- The test report shall not be reproduced except in full, without written approval of the laboratory.
- Om Geo Tech Services is not responsible for any kind of interpretation of test results
- The results/report is not used for publicity.
- ** As informed by client



Doc ID : FMT-TST-01 / Page 1/1



Nadiad - Dabhan Road,
Nr. Bhutia Bunglow, Nr. MGVC Office,
NADIAD - 387 320



omgeotech18@gmail.com



94273 16024 , 99987 89919

Solar Foundation

Site Information	
Sap Id	I-GJ-MTAR-ENB-9023
Candidate Id	C1
Form No	R4G-70-CQM-FMT-PR-041
Site Name	Valotri
Site Location	Open Plot of Gram Panchayat, Tarapur Bypass Road, Village - Valotri, Ta - Matar, Dist - Kheda, MATAR, Gujarat
City	MATAR
Latitude	22.690208
Longitude	72.867269
R4G State	Gujarat
Contractor	excel
Date	06 May 2022

For, EXCEL ELECTRICALS

AUTH. SIGN.

Inspection Report- Solar Foundation

Sr.No.	Description	Specifications	Observations	Remarks
Preliminary Checks				
1.1	Layout	As per Drawing	Ok	
1.2	Latest IFC	Availability	Yes	
Materials				
2.1	Steel Re-bar	Test Certificate/no rust/no cracks/Mark	no rust and cracks	
2.2	Grade of concrete	As per Drawing	M20	
2.3	Cover blocks	As per Drawing	50mm	
Raft Foundation				
3.1	Check the size of excavated pit as per drawing with limits of excavation	L * B * D	8.8*5*1.5	
3.2	Concrete- RMC/Machine Mix	RMC/Manual	manual machine mix	
3.3	Reinforcement laying as per drawing	As per BBS mentioned in drawing	as per BBS	
3.4.1	Check spacing of rebars	As per Drawing	as per drawing	
3.4.2	Diameter of re-bars	As per Drawing	10mm	

3.5	Check for Cover	As per Drawing	50mm	
3.6	Application of shuttering oil	Visual	Ok	
3.7	Check raft dimension and its shuttering/supporting system	As per Drawing(L*B*D)	1.5*1.5*0.2	
3.8	Check Column dimension and its supporting system	As per Drawing(L*B*D)	0.3*0.3*1.6	
3.9	Concrete Activity	As per Drawing & Specifications	Manual	
3.9.1	Grade of concrete	M20/M25/M30	M20	
3.10	Use of chute if applicable and height limit 1.7 mtr	Ht- Max.1.7 mtr	1mtr	
3.11	Use of vibrator	Needle size	60mm	
3.12	Cubes taken for test	06 Number of Cubes with Site ID on Cube	06 nos	
3.13	Ensure Curing	7 Days by water/Curing Compound	by water	

Pedestal/Column

4.1.1	Reinforcement binding as per drawing	As per BBS mentioned in drawing	As per BBS	
4.1.2	Main Bar, Spacing of rings, stirrups, hooks	As per Drawing	200mm	
4.1.3	Cover	50mm	50mm	
4.1.4	Application of shuttering oil	Visual	Ok	

4.1.5	Column dimension (L*B*D) and its supporting system	As per Drawing	0.3*0.3	
4.1.6.1	Concreting- Grade-M20/M25/M30	As per Drawing & Specification	M20	
4.1.6.2	Concrete with-RMC/Machine Mix	As per Drawing & Specification	Machine Mix	
4.1.7	Cubes taken for test	6 Nos. Of Cubes with Site ID on cube	06 nos cubes	
4.1.8	Ensure Curing	7 Days by water/Curing Compound	7 days by water	
4.1.9	Ensure Proper Backfilling with compaction after ensuring 3 days of Curing or application of Curing Compound	As per Guideline	ok	
4.2.1	Stub projection from top of concrete & its alignment	As per Drawing	200mm	
4.2.2.1	Top level of Foundation Stub of all pedestals	Check with water level Lvl-P1	1mm	
4.2.2.2	Top level of Foundation Stub of all pedestals	Check with water level Lvl-P2	0mm	
4.2.2.3	Top level of Foundation Stub of all pedestals	Check with water level Lvl-P3	1mm	


Post Casting

5.1	Visual check for cracks,bulging,honeycombing & exposed steel etc. in foundation	No Damages	no damages	
5.2	Check the c/c distance between foundation bolts	As per Drawing	na	
5.3	Ensure proper backfilling has been done with compaction	As per Specification	ok	

5.4.1	7 days Cube Strength(Raft)	67% & Above	to be done	
5.4.2	7 days Cube Strength(Pedestal)	67% & Above	to be done	
5.5.1	28 Days Cube Strength(Raft)	100% & Above	to be done	
5.5.2	28 Days Cube Strength(Pedestal)	100% & Above	to be done	
5.6	Curing of Foundation and Pedestal/Apply curing compound	7 days curing by water/Curing Compound	7 by water	

Observations and Comments:

ok

For, EXCEL ELECTRICALS

 AUTH. SIGN.

CFQ details			
	Contractor's representative	Field Engineer	QC Engineer
Signature			
Name	BHAVESH	Abhijit	
Date	06 May 2022	06 May 2022	--


ANIL SHAH
 MPCM-VADODARA-2
 Mob. No. 9374710314

For, EXCEL-ELECTRICALS

 AUTH. SIGN.



HH28+7WV, Valotri, Gujarat 387520, India



	Decimal	DMS
Latitude	22.549275	22°32'57" N
Longitude	72.56752	72°34'3" E

42°C

108°F

2022-04-25(Mon) 15:43

J. madh
JEVIN PATEL
Mo. No. 9662609867
FE-Vadodara-2

Swatol Ma
Temple Valotri
Gujarat

For, EXCEL ELECTRICALS.

AUTH. SIGN.

From: Hardik1.Suthar@ril.com

To: project.gujarat@excelelectricals.com

Date: 5/9/2022 11:05:16 PM

Subject: RE: [External]RE: Material Reconciliation _ Excel Electricals

Attachments: RICCO-630186908_MAY-14 Electrical.pdf
RICCO-630150746_MAY-08 Electrical.pdf
RICCO-630150746_MAY-09 Electrical.pdf
RICCO-630163294_MAY-15 Electrical.pdf
RICCO-630164230_MAY-13 Electrical.pdf
RICCO-630170811_MAY-01 Electrical.pdf
RICCO-630170811_MAY-06 Electrical.pdf
RICCO-630170811_MAY-07 Electrical.pdf
RICCO-630180228_MAY-04 Civil.pdf
RICCO-630180228_MAY-05 Civil.pdf
RICCO-630186905_MAY-12 Civil.pdf

QTY in your Ricco found ok As per issued qty.

Pls validate Ricco Site material consumption qty through MPCM/PMO/SITE engineer for billing.

Thanks & Regards
Hardik Suthar
7043055098

From: Bhavesh Sadhu <project.gujarat@excelelectricals.com>

Sent: 05 May 2022 12:11

To: Akash Gandhi <Akash.Gandhi@ril.com>; Subhash1 Khimaniya <Subhash1.Khimaniya@ril.com>

Cc: ilesh.soni@excelelectricals.com; Hardik1 Suthar <Hardik1.Suthar@ril.com>; Chirag M Shah <Chirag.M.Shah@ril.com>

Subject: [External]RE: Material Reconciliation _ Excel Electricals

Caution: The e-mail below is from an external source. Please do not open attachments or click links unless this email comes from a known sender and you know the content is safe.

Dear Sir,

Please find attached Reco. for below sites for validation.

Kindly check & validate for further approval.

SR NO	MP	SAP ID	PROJECT	Material Reconciliation			SITE RFE1 DATE
				Civil	Erection	Electrical	

For, EXCEL ELECTRICALS


AUTH. SIGN.

1	Ahmedabad-1	I-GJ-AMBD-ENB-0498	5G	No	No	Yes	30-Apr-22
2	Ahmedabad-1	I-GJ-AMBD-ENB-0041	5G	No	No	Yes	21-Apr-22
3	Ahmedabad-2	I-GJ-BVLA-ESC-0024	ESC	No	Yes	Yes	28-Feb-22
4	Vadodara-2	I-GJ-KLAL-ESC-0025	ESC	No	Yes	Yes	8-Apr-22
5	Ahmedabad-1	I-GJ-AMBD-ENB-0871	5G	No	No	Yes	30-Apr-22
6	Ahmedabad-1	I-GJ-AMBD-ENB-0725	5G	No	No	Yes	30-Apr-22
7	Ahmedabad-1	I-GJ-AMBD-ENB-1109	5G	No	No	Yes	29-Mar-22
8	Vadodara-2	I-GJ-MTAR-ENB-9023	SOLAR	Yes	No	No	
9	Vadodara-2	I-GJ-VASO-ENB-9001	SOLAR	Yes	No	No	
10	Vadodara-2	I-GJ-SAQE-ESC-0002	ESC	Yes	No	No	28-Apr-22

Regards,
Bhavesh Sadhu
Excel Electricals
9979130791

From: Bhavesh Sadhu <project.gujarat@excelelectricals.com>

Sent: Monday, May 02, 2022 9:07 PM

To: 'Akash.Gandhi@ril.com' <akash.gandhi@ril.com>; 'Subhash1.Khimaniya@ril.com' <Subhash1.Khimaniya@ril.com>

Cc: 'ilesh.soni@excelelectricals.com' <ilesh.soni@excelelectricals.com>; 'Hardik1.Suthar@ril.com'

<Hardik1.Suthar@ril.com>; 'Chirag.M.Shah@ril.com' <Chirag.M.Shah@ril.com>

Subject: Material Reconciliation _ Excel Electricals

Dear Sir,

Please find attached Reco. for below sites for validation.

Kindly check & validate for further approval.

SR NO	MP	SAP ID	PROJECT	Material Reconciliation			SITE RFE1 DATE
				Civil	Erection	Electrical	
1	Ahmedabad-1	I-GJ-AMBD-ENB-0498	5G	No	No	Yes	30-Apr-22
2	Ahmedabad-1	I-GJ-AMBD-ENB-0041	5G	No	No	Yes	21-Apr-22
3	Ahmedabad-2	I-GJ-BVLA-ESC-0024	ESC	No	Yes	Yes	28-Feb-22
4	Vadodara-2	I-GJ-KLAL-ESC-0025	ESC	No	Yes	Yes	8-Apr-22
5	Ahmedabad-1	I-GJ-AMBD-ENB-0871	5G	No	No	Yes	30-Apr-22
6	Ahmedabad-1	I-GJ-AMBD-ENB-0725	5G	No	No	Yes	30-Apr-22
7	Ahmedabad-1	I-GJ-AMBD-ENB-1109	5G	No	No	Yes	29-Mar-22
8	Vadodara-2	I-GJ-MTAR-ENB-9023	SOLAR	Yes	No	No	
9	Vadodara-2	I-GJ-VASO-ENB-9001	SOLAR	Yes	No	No	
10	Vadodara-2	I-GJ-SAQE-ESC-0002	ESC	Yes	No	No	28-Apr-22

Regards,
Bhavesh Sadhu

For, EXCEL ELECTRICALS

AUTH. SIGN.

Excel Electricals

9979130791

"Confidentiality Warning : This message and any attachments are intended only for the use of the intended recipient(s), are confidential and may be privileged. If you are not the intended recipient, you are hereby notified that any review, re-transmission, conversion to hard copy, copying, circulation or other use of this message and any attachments is strictly prohibited. If you are not the intended recipient, please notify the sender immediately by return email and delete this message and any attachments from your system.

Virus Warning: Although the company has taken reasonable precautions to ensure no viruses are present in this email. The company cannot accept responsibility for any loss or damage arising from the use of this email or attachment."

For, EXCEL ELECTRICALS


AUTH. SIGN.

Material Reconciliation Statement

Contractor Name : M/s. Excel Electricals
Circle Name : Gujarat North
Site ID & Name :
Site Count Billed : 01

WO No. : 630180228
Invoice No. : MAY/22-23/04
Invoice Date: 01-May-22

A	B	C	D	E	F	G	H	I	J	K
Material No	Material Description	UOM	Material Received from WH	Received BTN (IN)	Transfer BTN (OUT)	Material Return To WH (MRN)	Consumed & Invoiced Earlier	Consumed & Invoiced Currently	Total Consumption Till Date	Balance with Contractor / WIP
2002159304	CIP F 20 PANEL, 4X10 SOLAR PANEL STRUCTR	EA	4	0	0	0	1	2	3	1

Remarks if Any:-

>Material Net issuance verified by Material Coordinator(Column NO- "D" TO "G".)
>Site ID, Inv No + Previous and current bill quantities booking verify by MPCM/PMO

Verified & Signed By:-

MPCM :-

Anil Shah
ANIL SHAH
MPCM-VADODARA-2
Mob. No. 9374710314



Material Coordinator:-

Hardik suthar
Date : 10-05-2022

Contractor :-

For, EXCEL ELECTRICALS
[Signature]
AUTH. SIGN.

For, EXCEL ELECTRICALS
[Signature]
AUTH. SIGN.

Site Wise Consumption				
Contractor Name : M/s. Excel Electricals Circle Name : Gujarat North Site Count in Contract : Site Count Billed : 01				
WO No. : 630180228 Invoice No. : MAY/22-23/04 Invoice Date: 01-May-2022				
Material No	Material Description	UOM	I-GJ-MTAR-ENB-9023	Total
2002159304	CIP F 20 PANEL, 4X10 SOLAR PANEL STRUCTR	EA	2	2
Remarks If Any :-				
>Material Net issuance verified by Material Coordinator >Site wise consumption QTY verify by MPCM/PMO.				
Verified & Signed By :-				
MPCM:-  ANIL SHAH MPCM-VADODARA-2 Mob. No. 9374710314		Material Coordinator:- :- Hardik suthar Date : 10-05-2022		
		Contractor :- For, EXCEL ELECTRICALS  AUTH. SIGN.		

For, EXCEL ELECTRICALS

 AUTH. SIGN.



GOVT. APPROVED CIVIL, EHV - HT - LT ELECTRICALS,
TELECOM WORKS & LABOUR CONTRACTORS

Tel. : (0288) 2555750
M. : 97129 09040, 93774 58805
E-mail: excel19680@rediffmail.com
excel19680@gmail.com

116, Siddhnath Complex,
1st Floor, Near Indian Bank,
K. V. Road, Jamnagar - 361 001

This is to inform and certify that **M/S. Excel Electricals** will not be deploying 20 or more contract workmen/labour on any day during the execution of the contract work in the allotted vide Work Order No. P21/630180228

However, in future, if ever the number of contract workmen to be deployed exceeds the stipulated statutory number of 20 or more workmen, the contractor will immediately apply and obtain labour license for the required capacity from the concerned Licensing Authority under CL(R&A) Act, 1970/Central Rules, 1971.

Thanking You,

For, EXCEL ELECTRICALS


AUTH. SIGN.



GOVT. APPROVED CIVIL, EHV - HT - LT ELECTRICALS,
TELECOM WORKS & LABOUR CONTRACTORS

Tel. : (0288) 2555750
M. : 97129 09040, 93774 58805
E-mail: excel19680@rediffmail.com
excel19680@gmail.com

116, Siddhnath Complex,
1st Floor, Near Indian Bank,
K. V. Road, Jamnagar - 361 001

To,

Reliance Projects and Property Management Services Limited
5, TTS Industrial Area, Thane Belapur Road,
Ghansoli, Navi Mumbai - 400701

I/We/M/s. **EXCEL ELECTRICALS**. Hereby declare that we will not engage any child labour or Inter State Migrant Workmen on any day during the period of contract in the establishment of **M/s Reliance Digital Platform & Project Services Limited** for execution of the work awarded to us vide WO No. **P21/630180228**

We hereby indemnify M/s Reliance Corporate IT Park Limited against any legal hassles arising due to lapses on our part under **The Child Labour (Prohibition & Regulation) Act 1986 and Inter State Migrant Workmen (Regulation of Employment and Conditions of Services) Act, 1979.**

Thanking You,

(Authorized Signatory)

For, EXCEL ELECTRICALS

AUTH. SIGN.

Serial No. 454/2021

INDIA NON JUDICIAL NOTARY


Government of Gujarat

Certificate of Stamp Duty



सत्यमेव जयते

Certificate No.	IN-GJ26100522199170T
Certificate Issued Date	23-Sep-2021 05:36 PM
Account Reference	IMPACC (AC)/ gj13336711/ GULBAI TEKRA/ GJ-AH
Unique Doc. Reference	SUBIN-GJGJ1333671186961021756150T
Purchased by	EXCEL ELECTRICAL
Description of Document	Article 14 Bond
Description	Not Applicable
Consideration Price (Rs.)	0 (Zero)
First Party	EXCEL ELECTRICAL
Second Party	Not Applicable
Stamp Duty Paid By	EXCEL ELECTRICAL
Stamp Duty Amount(Rs.)	500 (Five Hundred only)



Signature

0015322762

For, EXCEL ELECTRICALS
AUTH. SIGN.

P131

Last Updationon :25.11.16

DECLARATION CUM INDEMNITY BOND

THIS DECLARATION CUM INDEMNITY BOND made at by M/s Excel Electrical their registered Office at 116, Siddhnath Complex, K.V. Road, Near Indian Bank, Jamnagar-361001 (hereinafter referred to as "**Contractor**") which expression shall unless it be repugnant to the context or meaning thereof, be deemed to mean and include their respective assigns, successors, executors and/or administrators) of the ONE PART in favor of the Company M/s. Reliance Projects And Property Management Service Limited

Registered under the Companies Act, 1956, and having its registered office at Auda TP Scheme, Bodakdev No 1/A F P No.5 2nd Floor, Opp. Drive-in Cinema, Drive-in Road Ahemdabad-380054 (hereinafter referred to as the "**Company**", which expression shall unless it be repugnant to the context or meaning thereof be deemed to mean and include its assigns, successors,) of the OTHER PART.

WHEREAS the Company has entered into a contract by issuing Work Order(s) to the Contractor for the

P21/54023589	P21/630132499	P21/630144520	P21/630144516
P21/630150017	P21/630150100	P21/630149196	P21/630149213
P21/630147145	P21/630143718	P21/630143719	P21/630152402
P21/630152403	P21/630150746	P21/630155636	P21/630155637
P21/630155650	P21/630155651	P21/630157110	P21/630157111
P21/630159071	P21/630159081	P21/630160651	P21/630160652
P21/630161205	P21/630162363	P21/630163207	P21/630163602
P21/630163292	P21/630163294	P21/630163603	P21/630163680
P21/630163207	P21/630162369	P21/630164228	P21/630164230
P21/630164338	P21/630164360	P21/630165881	P21/630165883
P21/630166047	P21/630166913	P21/630168426	P21/630168427
P21/630170776	P21/630169751	P21/630169585	P21/630169584
P21/630170205	P21/630170206	P21/630170809	P21/630170811
P21/630171733	P21/630173004	P21/630173001	P21/630172817
P21/630174759	P21/630174215	P21/630174208	P21/630173920
P21/630177304	P21/630177299	P21/630177208	P21/630177206
P21/630176190	P21/630174761	P21/630174759	P21/630177302
P21/630177300	P21/630179113	P21/630179110	P21/630178361
P21/630186317	P21/630186315	P21/630184297	P21/630180929
P21/630180926	P21/630180228		

For, EXCEL ELECTRICALS
AUTH. SIGN.

(Hereinafter called the "**Contract**")

PI31

Last Updationon :25.11.16

(Hereinafter called the "Contract")


AND WHEREAS it is one of these essential conditions of the Contract that the Contractor shall comply with all the provisions of the Labor & Industrial Laws, as may be applicable from time to time for the discharge and completion of the Works and/or Services covered under said Contract by the Contractor including but not limited to the observance and compliance of The Contract Labor (R & A) Act 1970, Child Labor (Prohibition and Regulation) Act 1986, The Employees Provident Funds & Miscellaneous Provisions Act, 1952, Employees State Insurance Act 1948, Minimum Wages Act, 1948, Payment of Bonus Act, 1965, Payment of Wages Act, 1936, Employees Compensation Act, 1923, and other Labor Laws applicable to the contractor (hereinafter referred as the 'Laws').

AND WHEREAS the Contractor has agreed to execute this Declaration cum Indemnity Bond to this effect and has agreed to indemnify and keep the Company, its directors and employees and representatives indemnified and hold harmless against all third party claims, charges, penalties, fines, expenses, losses, damages, costs, suits or any other levy against the Company and/or the management due to the failure of the Contractor to observe or follow any Laws.

NOW THIS DEED WITNESSETH AS UNDER:

1. In consideration of the Company awarding the Contract/ Work Order to the Contractor subject to the condition of execution of this Declaration cum Indemnity bond, the Contractor declares and represents to the Company that the Contractor has obtained all statutory registrations, certificates, licenses and approvals required under the Laws enabling the Contractor to execute the Contract in a legal and lawful manner.
2. That in the event of any liability arising out of non-compliance of any such 'Laws' by the Contractor in connection with the execution of the Contract, the Contractor shall bear all the resultant whatsoever liability(IES), if any arising out thereof and that the Company, its directors, employees, representatives, shall not be liable for any such liability(IES). The Contractor agrees to indemnify and keep the Company and its directors, employees, representatives indemnified, defend and hold harmless, against all losses, costs, damages, claims, penalties, interest, expenses, demands, fines, legal liability, causes of action, injury to persons suites which may be suffered, incurred, undergone and / or sustained by the Company including the costs and expenses that may be incurred in defending any such liability(ies) claim(s), proceeding(s) etc. that may be made or taken or arise on the same by any person, body, authority, government, judicial / quasi-judicial authority due to the failure or noncompliance of any such laws and rules there under (including any amendments in acts, laws, statutes & rules there under) of whatsoever kind and nature arising out of or in any way connected with, whether or not such acts or omissions are actual or alleged, active or passive with regard to the discharge of the said Contract.
3. The Contractor hereby agrees and undertakes to make good any loss, damage, penalties, interests, claims, suits, demands, decrees, expenses that the Company may suffer to the fullest satisfaction of the Company and if the Contractor fails to make good the same then the Company shall have the right to recover the same and or any other loss sustained, without any restriction or limitation, together with any other incidental expenses, costs, and all incidental logistic expenses etc. that may be suffered by the Company, from the Contractor.

For, EXCEL ELECTRICALS


AUTH. SIGN.

P131

Last Updationon :25.11.16

4. The Contractor hereby further confirms and declares that this Declaration cum Indemnity Bond, is irrevocable and shall be final and binding on it / him heirs, executors, administrators, legal representatives, successors and assigns, wherever the context applies. Any claims, demands, shall be adjusted against any amount due and payable to the Contractor and the Company shall have the right to withhold any amounts due and payable to the Contractor, till the settlement of such claims, disputes to the satisfaction of the Company or alternatively make demand sufficient security from the Contractor towards discharge of such claims, obligations etc.
5. The Declaration cum Indemnity Bond shall be applicable for any and all Work Orders issued to the Contractor in this regard.
6. This Declaration cum indemnity bond shall be in accordance with the laws of India and any dispute between the parties with regard to this Declaration cum Indemnity Bond shall be resolved through the dispute resolution process mentioned in the General Conditions of the Contract (GCC).
7. Any terms used in this indemnity bond, but not expressly defined herein shall have the meaning assigned to it in the General terms and Conditions (GTC) forming part of the Work Orders issued.


IN WITNESS WHEREOF, the said Contractor has hereunto set their hand the day and year first hereinabove written.

SIGNED SEALED AND DELIVERED
By the within named "CONTRACTOR")

For, EXCEL ELECTRICALS

AUTH. SIGN.
(Authorized Signatory)
Rubber Stamp of Firm/Company
Name:
Designation:
Date:

Contract signed
BEFORE ME
Signature
A. M. UJJAINI
NOTARY
GOVT. OF INDIA
23/9/21



For, EXCEL ELECTRICALS
Signature
AUTH. SIGN.

RELIANCE PROJECTS & PROPERTY MANAGEMENT SERVICES LIMITED

(FORMERLY RELIANCE DIGITAL PLATFORM & PROJECT SERVICES LTD)

AUDA TP SCHEME, BODAKDEV NO: 1/A,, F P NO.: 5, 2ND FLOOR,

OPP. DRIVE IN CINEMA, DRIVE IN ROAD, AHMEDABAD-380054, GUJARAT, INDIA

Telephone : +91 79 -8879387831/40014190

Email: SUNILKUMAR.LIMBACHIA@RIL.COM

**WORK ORDER**

To 399452 EXCEL ELECTRICALS 116, SIDDHNATH COMPLEX, K. V. ROAD, NR. INDIAN BANK JAMNAGAR GUJARAT Pin Code : 361001 INDIA Phone : +91-288-2555750 Fax : E-Mail : EXCEL19680@GMAIL.COM Attention : PARESH LUNAGARIYA	Work Order No. : P21/630180228 Date : 12.02.2022 Contractor's Quot. Ref : Date : Our Ref : 6011 GSTN Of Biller : 24AADFE1348L1ZJ Bill From State : Gujarat Bill From : 399452
--	---

This WORK ORDER, the SPECIAL CONDITIONS OF CONTRACT, the GENERAL CONDITIONS OF CONTRACT, the annexures enclosed to each of the foregoing, including any other document forming part of CONTRACT DOCUMENTS contain all the express terms and conditions of contract of supply of SERVICES ordered pursuant to this WORK ORDER and confirms and supersedes the LETTER OF COMMITMENT (if any) issued by COMPANY. CONTRACTOR agrees to supply the SERVICES, including all DELIVERABLES in full accordance with the foregoing terms and conditions. Capitalized terms used in this WORK ORDER but not defined in the WORK ORDER shall have the meaning ascribed to such terms in the foregoing SPECIAL CONDITIONS OF CONTRACT and GENERAL CONDITIONS OF CONTRACT. CONTRACTOR shall sign and return this WORK ORDER acknowledging the acceptance of this WORK ORDER within three (3) days of receipt at the communication address mentioned in this WORK ORDER. If acknowledgement is not received within three (3) days, this WORK ORDER will be deemed accepted by the CONTRACTOR. No other form of acceptance shall be binding on the PARTIES. For all future correspondence please quote this WORK ORDER NUMBER.

WO Period From DT : 12.02.2022 To DT : 30.04.2022	Value of Work CGST SGST	INR INR INR	315,590.00 28,403.10 28,403.10
TOTAL ORDER VALUE		INR	372,396.20
Value in Words : (Rs. Three Lakh Seventy Two Thousand Three Hundred Ninety Six and Paise Twenty only) For other details, please refer line items.			
Delivery Terms : N/A Engineer in Charge : Anil Shah			
Payment Terms : See Page Inside			
BUYER : Pandey	for RELIANCE PROJECTS & PROPERTY MANAGEMENT SERVICES LIMITED (FORMERLY RELIANCE DIGITAL PLATFORM & PROJECT SERVICES LTD) This is a computer generated document not requiring any signature	CONTRACTOR'S Acceptance Signature Title Date	

REGISTERED OFFICE : Office-101,Saffron, Nr.Centre Point Panchwati 5 Rasta,Ambawadi Ahmedabad -380006

Anil Shah
ANIL SHAH
MPCM-VADODARA-2
Mob. No. 9374710314

For, EXCEL ELECTRICALS
[Signature]
AUTH. SIGN.



WORK ORDER

W.O.Number P21 / 630180228 Dt.12.02.2022
Page No: 1

WORK ORDER ISSUED FOR SOLAR PANEL INSTALLATION WORK_ 3 SITES AT NORTH GUJARAT
(Including Digital Conditions)

1. FIM - Applicable - Applicable
2. Indemnity Clause - Applicable
3. Performance Bank Guarantee(BG)- Applicable
4. Retention Clause - Applicable
5. DLP - 12 Months

No	Item Code	Material/Work Description	Quantity	UOM	Price Details	Unit Rate	Amount (INR)
1	I-GJ-VASO-ENB-9001_C I-GJ-VASO-ENB-9001		1	AU			
		Service Accounting Number: 995428			Value of Work CGST SGST	INR/AU % %	91,901.00 8,271.09 8,271.09

The item covers the following Work :

- 10 3343857 CHRG CVL SOLAR 2M 20-25DT 28 WT 5SBC

Charges for providing materials and services for execution of CIVIL works for solar work having 28 module at 2m height with 20-25 degree tilt and soil with water table and 5 SBC. The scope of work includes site preparation & restoration, excavation for footing, disposal of surplus earth, backfilling with selected earth, providing and fixing/ laying of steel reinforcement, shuttering, and concrete, transportation, fixing and alignment of stubs/ foundation bolts/ CIP, construction of support wall, grouting related work etc., and other site specific works as per requirement. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge.

- 2 I-GJ-MTAR-ENB-9023_C
I-GJ-MTAR-ENB-9023

			1	AU			
		Service Accounting Number: 995428			Value of Work CGST SGST	INR/AU % %	91,901.00 8,271.09 8,271.09

The item covers the following Work :

- 10 3343857 CHRG CVL SOLAR 2M 20-25DT 28 WT 5SBC

Charges for providing materials and services for execution of CIVIL works for solar work having 28 module at 2m height with 20-25 degree tilt and soil with water table and 5 SBC. The scope of work includes site preparation & restoration, excavation for footing, disposal of surplus earth, backfilling with selected earth, providing and fixing/ laying of steel reinforcement, shuttering, and concrete, transportation, fixing and alignment of stubs/ foundation bolts/ CIP, construction of support wall, grouting related work etc., and other site specific works as per requirement. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge.

For, EXCEL ELECTRICALS

AUTH. SIGN.



WORK ORDER

W.O.Number P21 / 630180228 Dt.12.02.2022
Page No: 4

Total Value of Work	INR	315,590.00
Total CGST	INR	28,403.10
Total SGST	INR	28,403.10

Total Order Value:	INR	372,396.20
--------------------	-----	------------

Terms of payment :

Payment shall be made as per Detailed Payment Terms specified in the purchasing document.

Vendor Bank Details:

Bank Account No. : 917030011070652
Bank Name : AXIS BANK LTD
City : JAMNAGAR

Liquidated Damages :

0.5 % PER WEEK TO MAX OF 5%

Engineer-In-charge :

Anil Shah
Ankur Shah
Arvind Pipaliya
Chandrajeet Yadav
Girish Modi
Pavan Pandey
Nayan Patel
Saurabh Desai
Rakesh Shah
Kamal Patel
Pitar Simon
Ravi k verma
Satish Padhiyar
Kapil Gurubaxani
Alex Rao
Chirag Shah

Document Submission Bank:

Note(S): 1. It is essential that the Contractor shall mention ItemNo. & Item code along with corresponding Material/Work Description and W.O.No. as mentioned above, in the Delivery challan (On-Shore Order), Measurement sheet and invoice for ease of material Inwarding, Certification of work and Bill Processing. Failure to do so may be the grounds for the rejections(s) or delay in release of payment(s).

PLANT REGISTRATION NO. : 24AAJCR6636BIZI

For, EXCEL ELECTRICALS

AUTH. SIGN.
