

GOVT. APPROVED CIVIL, EHV, HT, LT ELECTRICALS,  
TELECOM WORKS & LABOUR CONTRACTORS


Tel : (0288) 2555750  
M. : 97129 09040, 93774 58805  
E mail: excel19680@gmail.com  
excel19680@rediffmail.com

116, Siddhnath Complex,  
1st Floor, Near Indian Bank  
K. V. Road, Jamnagar - 361 001

Ref. No. :

Date :

| TAX INVOICE                                                                                                                                                                                                                                                                          |                   |                                                       |                |            |                             |                                 |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-------------------------------------------------------|----------------|------------|-----------------------------|---------------------------------|
| ORIGINAL FOR RECIPIENT                                                                                                                                                                                                                                                               |                   |                                                       |                |            |                             |                                 |
| <b>Excel Electrical</b><br><b>116, Siddhnath Complex, 1st Floor, Near Indian Bank, K. V. Road, Jamnagar-361001</b>                                                                                                                                                                   |                   |                                                       |                |            | <b>NA</b>                   |                                 |
| <b>TO,</b><br><b>Reliance Projects And Property Management Services Limited</b><br><b>First Floor 101, Saffron, Panchwati 5 Rasta, Nr Bank of Baroda, Ambawadi, Ahmedabad- Gujarat- 380006</b>                                                                                       |                   |                                                       |                |            | <b>Invoice No</b>           | <b>MAY/22-23/05</b>             |
|                                                                                                                                                                                                                                                                                      |                   |                                                       |                |            | <b>Invoice Date</b>         | <b>01-05-22</b>                 |
|                                                                                                                                                                                                                                                                                      |                   |                                                       |                |            | <b>Contract- WO No.</b>     | <b>P21/630180228</b>            |
|                                                                                                                                                                                                                                                                                      |                   |                                                       |                |            | <b>Route Name</b>           | <b>NA</b>                       |
|                                                                                                                                                                                                                                                                                      |                   |                                                       |                |            | <b>Site ID</b>              | <b>As Par Abstract</b>          |
|                                                                                                                                                                                                                                                                                      |                   |                                                       |                |            | <b>Site Name</b>            | <b>As Par Abstract</b>          |
|                                                                                                                                                                                                                                                                                      |                   |                                                       |                |            | <b>Vendor Code</b>          | <b>399452</b>                   |
|                                                                                                                                                                                                                                                                                      |                   |                                                       |                |            |                             |                                 |
|                                                                                                                                                                                                                                                                                      |                   |                                                       |                |            | <b>Supplier's GSTIN</b>     | <b>24AADFE1348L1ZJ</b>          |
| <b>State - State Code as per GST : GUJARAT - 24</b>                                                                                                                                                                                                                                  |                   |                                                       |                |            | <b>Period of Supply</b>     | <b>20/03/2022 to 25/03/2022</b> |
| <b>GSTIN / Unique ID : 24AAJCR6636B1ZJ</b>                                                                                                                                                                                                                                           |                   |                                                       |                |            | <b>Nature of Supply</b>     | <b>Solar Civil Work</b>         |
| <b>PAN No. : AAJCR6636B</b>                                                                                                                                                                                                                                                          |                   |                                                       |                |            | <b>Place of supply of</b>   | <b>GUJARAT</b>                  |
| <b>Sr.</b>                                                                                                                                                                                                                                                                           | <b>SAC : Code</b> | <b>Service Description</b>                            | <b>Qty (A)</b> | <b>UOM</b> | <b>Rate (Rs. / UoM) (B)</b> | <b>Amount (Rs.) (A*B*C)</b>     |
| <b>1</b>                                                                                                                                                                                                                                                                             | <b>995428</b>     | <b>[3343857] CHRG CVL SOLAR 2M 20-25DT 28 WT 5SBC</b> | <b>1.00</b>    | <b>EA</b>  | <b>91,901.00</b>            | <b>91,901.00</b>                |
| <b>Total Supply Value of Milestone (Basic Value)</b>                                                                                                                                                                                                                                 |                   |                                                       |                |            |                             | <b>91,901.00</b>                |
| <b>Less : Basic value of Advance Paid with Service Tax</b>                                                                                                                                                                                                                           |                   |                                                       |                |            |                             |                                 |
| <b>Balance Invoice Value (Net off Advance paid with Tax)</b>                                                                                                                                                                                                                         |                   |                                                       |                |            |                             | <b>91,901.00</b>                |
| <b>Central GST @ 9%</b>                                                                                                                                                                                                                                                              |                   |                                                       |                |            |                             | <b>8,271.09</b>                 |
| <b>State GST @ 9%</b>                                                                                                                                                                                                                                                                |                   |                                                       |                |            |                             | <b>8,271.09</b>                 |
| <b>Total GST Payable on Balance Invoice Value (Net off Advance paid with Service Tax)</b>                                                                                                                                                                                            |                   |                                                       |                |            |                             | <b>16,542.18</b>                |
| <b>Total Invoice Value with GST</b>                                                                                                                                                                                                                                                  |                   |                                                       |                |            |                             | <b>108,443.18</b>               |
| <b>Less - Advance paid without Service Tax</b>                                                                                                                                                                                                                                       |                   |                                                       |                |            |                             | <b>-</b>                        |
| <b>Net Payable Amount</b>                                                                                                                                                                                                                                                            |                   |                                                       |                |            |                             | <b>108,443.18</b>               |
| <b>Round Off Net amount</b>                                                                                                                                                                                                                                                          |                   |                                                       |                |            |                             | <b>108,443.00</b>               |
| <b>Amount in Words :- One Lakh Eight Thousand Four Hundred Fourty Three Rupees Only</b>                                                                                                                                                                                              |                   |                                                       |                |            |                             |                                 |
| <b>GST Amount in Words :- Sixteen Thousand Five Hundred Fourty Two Rupees Eighteen Paise</b>                                                                                                                                                                                         |                   |                                                       |                |            |                             |                                 |
| <div style="text-align: right;"> <b>For:- Excel Electricals</b><br/> <b>PARESHBHAI BHIMJIBHAI LUNAGARIYA</b><br/>           Digitally signed by PARESHBHAI BHIMJIBHAI LUNAGARIYA<br/>           Date: 2022.06.13 16:31:52 +05'30'<br/>           Authorised Signatory         </div> |                   |                                                       |                |            |                             |                                 |
| <b>Declaration:</b><br><b>a) Certified that all the particulars given above are true and correct.</b>                                                                                                                                                                                |                   |                                                       |                |            |                             |                                 |



GOVT. APPROVED CIVIL, EHV - HT - LT ELECTRICALS,  
TELECOM WORKS & LABOUR CONTRACTORS

Tel. : (0288) 2555750  
M. : 97129 09040, 93774 58805  
E-mail : excel19680@rediffmail.com  
excel19680@gmail.com

116, Siddhnath Complex,  
1st Floor, Near Indian Bank,  
K. V. Road, Jamnagar - 361 001

## **NO CLAIM CERTIFICATE**

WO/Contract Order and Frame Order no : P21/630180228

WO/Contract Order and Frame Order Date: 12/02/2022

Circle/State : North Gujarat

Site Name :-As Per Attached BOQ

Scope of Work :- SOLAR 40M GBT CIVIL WORK

Invoice no :- MAY/22-23/05

Invoice Date :- 01-05-2022

We hereby confirm that we have carried out above scope of work in accordance with the, w.o/Contract order and Frame Order scope, terms and instruction of EIC and RS/- (1,08,443=00) (One Lakh Eight Thousand Four Hundred Fourty Three Rupees Only) as our final claim. We confirm that there is no further claim by us in respect of the above invoice site & the mention scope of work. The invoice amount will be paid 95% and balance 5% kept as retention and will be paid after defect liability period as per WO/Contract Order and Frame Order terms.

For M/s EXCEL ELECTRICALS

For, EXCEL ELECTRICALS

  
AUTH. SIGN.

Authorized Signatory

# BOQ CIVIL / SITE I.D. WISE ABSTRACT SHEET

| 1 Contractor Name:          |                    | EXCEL ELECTRICALS    |            |                     |                 |                     |     |                     |                             |                             |              |
|-----------------------------|--------------------|----------------------|------------|---------------------|-----------------|---------------------|-----|---------------------|-----------------------------|-----------------------------|--------------|
| 2 Invoice No.:              |                    | MAY/22-23/05         |            |                     |                 |                     |     |                     |                             |                             |              |
| 3 Invoice Dt.:              |                    | 01-May-22            |            |                     |                 |                     |     |                     |                             |                             |              |
| 4 WO No.:                   |                    | P21/630180228        |            |                     |                 |                     |     |                     |                             |                             |              |
| 5 Service Period From Date: |                    | 20-Mar-22            |            |                     |                 |                     |     |                     |                             |                             |              |
| 6 Service Period To Date:   |                    | 25-Mar-22            |            |                     |                 |                     |     |                     |                             |                             |              |
|                             |                    |                      |            |                     |                 |                     |     |                     |                             |                             |              |
| Sr.                         | Site ID            | WBS ID               | Tower Type | NON KTD             | Building Height | Tower Height        | SBC | Quantity            | Civil Service & Provide Mat | Civil Service & Provide Mat | Total Amount |
| 1                           | I-GJ-VASO-ENB-9001 | I-GJ-VASO-ENB-9001   | GBT        | YES                 | NA              | 40M                 | 5   | 1                   | 91,901.00                   | 91,901.00                   | 91,901.00    |
|                             |                    | Total Abstract Value |            |                     |                 |                     |     |                     |                             |                             |              |
|                             |                    |                      |            |                     |                 |                     |     |                     |                             |                             |              |
|                             |                    |                      |            |                     |                 |                     |     |                     |                             |                             |              |
| CONTRACTOR                  |                    |                      |            |                     |                 |                     |     |                     |                             |                             |              |
| Name                        |                    | Name                 |            | Name                |                 | Name                |     | Name                |                             | Name                        |              |
| Sign                        |                    | Sign                 |            | Sign                |                 | Sign                |     | Sign                |                             | Sign                        |              |
| Stamp                       |                    | Stamp                |            | Stamp               |                 | Stamp               |     | Stamp               |                             | Stamp                       |              |
| Date                        |                    | Date                 |            | Date                |                 | Date                |     | Date                |                             | Date                        |              |
| For, EXCEL ELECTRICALS      |                    | ANIL SHAH            |            | ANIL SHAH           |                 | ANIL SHAH           |     | ANIL SHAH           |                             | ANIL SHAH                   |              |
| AUTH. SIGN.                 |                    | MPCM-VADODARA-2      |            | MPCM-VADODARA-2     |                 | MPCM-VADODARA-2     |     | MPCM-VADODARA-2     |                             | MPCM-VADODARA-2             |              |
|                             |                    | Mob. No. 9374710314  |            | Mob. No. 9374710314 |                 | Mob. No. 9374710314 |     | Mob. No. 9374710314 |                             | Mob. No. 9374710314         |              |

## Quantity Certification Summary (QCS)

WO No: P21/630180228

WO Date:- 12/02/2022

Site ID Count:-AS PER BELOW MENTION

This is to certify that following Sites along with Technical Parameter pertaining to ODESC for above mentioned Work Order and of M/s. Excel Electricals being invoiced as per details attached, has been completed the following works.

**A) SOLAR CIVIL WORK :- GBT**

| Site ID            | WBS ID             | Technical Parameter |          |              |                 |     |
|--------------------|--------------------|---------------------|----------|--------------|-----------------|-----|
|                    |                    | Tower Type          | KIT/NKIT | Tower Height | Building Height | SBC |
| I-GJ-VASO-ENB-9001 | I-GJ-VASO-ENB-9001 | GBT                 | NONKTD   | 40M          | NA              | 5   |

Certified By:-

Engineer In-Charge (EIC):-

Circle Project Head (CPH):-

For, EXCEL ELECTRICALS

AUTH. SIGN.

  
**ANIL SHAH**  
MPCM-VADODARA-2  
Mob. No. 9374710314



## Work Completion Certificate

|              |                                       |                                     |                                    |                                  |                                  |                                     |
|--------------|---------------------------------------|-------------------------------------|------------------------------------|----------------------------------|----------------------------------|-------------------------------------|
| State        | Gujarat                               |                                     |                                    | Maintenance Point                |                                  |                                     |
| Project Type | 93 K<br><input type="checkbox"/>      | Infill<br><input type="checkbox"/>  | Growth<br><input type="checkbox"/> | Other (Specify)                  |                                  |                                     |
| Site Type    | Own Built<br><input type="checkbox"/> | IP Colo<br><input type="checkbox"/> | RP1<br><input type="checkbox"/>    | BSNL<br><input type="checkbox"/> | MAG1<br><input type="checkbox"/> | NLD AG1<br><input type="checkbox"/> |
| Tower type   | GBT<br><input type="checkbox"/>       | RTT<br><input type="checkbox"/>     | RTP<br><input type="checkbox"/>    | GBM<br><input type="checkbox"/>  | NBT<br><input type="checkbox"/>  | Other (Specify)                     |

This is to certify that work has been completed as per specification given in workorder on the sites mentioned

The required ITP / Checklists are available and verified in system

Site I.D.

I-GJ-VASO-ENB-9001

SAP ID

I-GJ-VASO-ENB-9001

W.O.Number

P21/630180228

Vendor Name

M/S. EXCEL ELECTRICALS

No of Sites

1

Completion Date

25-Mar-22

### Vendor Representative

Name

Sign

Date

For, EXCEL ELECTRICALS

AUTH. SIGN.

### RJIL Representative

Name

Sign

Date

ANIL SHAH  
MPCM-VADODARA-2  
Mob: No. 9377710314

Remarks, if any:

Note :

In case of Multiple sites, please attach applicable site details with this certificate

# EXCEL ELECTRICALS

## SOLAR Civil Quantity Measurement Sheet

Reliance SAP I-GJ-VASO-ENB-9001

Vendor Name:-Excel Electricals

TOWER HEIGHT:- 40M GBT

Opco Name:- Reliance -4G

District:- Vadodara-2

Circle Name:- Vadodara-2- Gujarat


Wo No :- P21/630180228

| NO | Item Code | Item                                 | Description                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | Quantity | UOM | Quantity |
|----|-----------|--------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------|-----|----------|
| 10 | 3343857   | CHRG CVL SOLAR 2M 20-25DT 28 WT 5SBC | Charges for providing materials and services for execution of CIVIL works for solar work having 28 module at 2m height with 20-25 degree tilt and soil with water table and 5 SBC. The scope of work includes site preparation & restoration, excavation for footing, disposal of surplus earth, backfilling with selected earth, providing and fixing/ laying of steel reinforcement, shuttering, and concrete, transportation, fixing and alignment of stubs/ foundation bolts/ CIP, construction of support wall, grouting related work etc., and other site specific works as per requirement. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge. | 1.00     | EA  | 1.00     |


|                                   |                               |                                |
|-----------------------------------|-------------------------------|--------------------------------|
| Excel Engg                        | FE                            | AM/CDP                         |
| Name :-<br>For, EXCEL ELECTRICALS | Name :-<br>J. V. Patel        | Name :-<br>ANIL SHAH           |
| Signature :-<br>AUTH. SIGN.       | Signature :-<br>JEVIN PATEL   | Signature :-<br>MCM-VADODARA-2 |
| Date :-                           | Date :-<br>Mo. No. 9662609867 | Date :-<br>Mob. No. 9374710314 |




| Dimensions     |         |
|----------------|---------|
| L1             | 2.900 m |
| L2             | 1.950 m |
| B              | 1.050 m |
| B1             | 3.950 m |
| B2             | 3.000 m |
| S              | 0.300 m |
| G1             | 0.200 m |
| SOK            | 0.300 m |
| d1             | 1.250 m |
| d2             | 1.450 m |
| D              | 1.500 m |
| Embedded depth | 0.400 m |

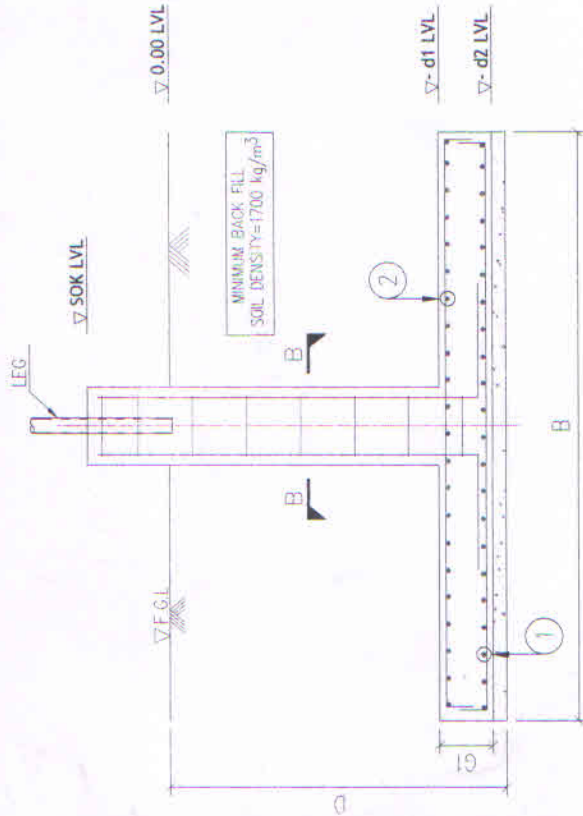


FOUNDATION DETAIL  
(SECTION "A-A")

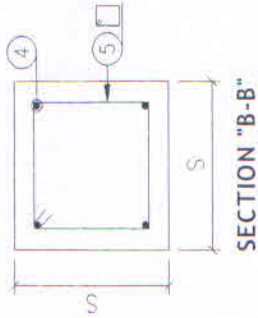

SECTION "B-B"

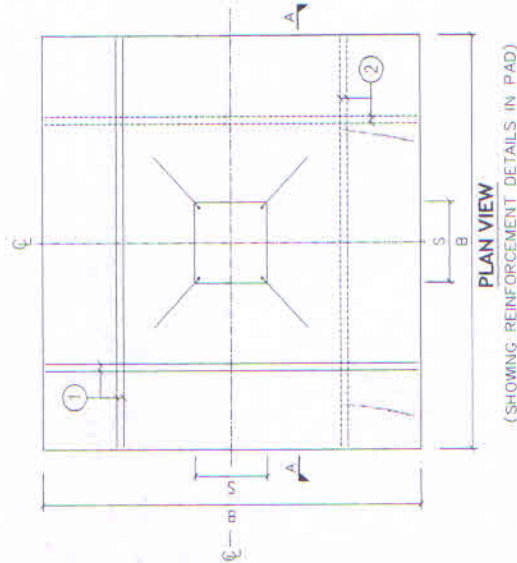

PLAN VIEW

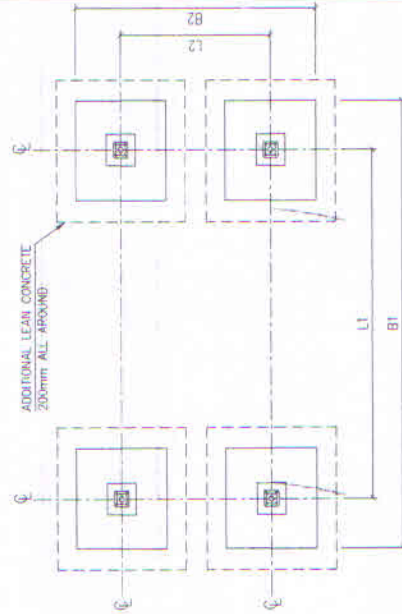

EXCAVATION PLAN

(SHOWING REINFORCEMENT DETAILS IN PAD)

For, EXCEL ELECTRICALS

AUTH. SIGN.

# General notes

1. This is a generic foundation drawing.
2. The following are the assumed parameters considered during foundation design

Net safe bearing capacity (NSBC) = 57/m<sup>2</sup>

Ground water table = At Ground level

Depth of foundation = 1.5 m

Dry density of soil = 1700 kg/m<sup>3</sup>

Angle of internal friction = 10 deg

3. Before commencement of construction work using these designs, the owner/client/civil contractor shall carry out detailed soil investigation of every site.

4. Further, the soil investigation report shall be reviewed by a consultant and certification shall be obtained to ensure conformity between assumed parameters and soil report values before start of construction.

5. The foundation design is applicable only when the considered NSBC is available at or within 1.5 m depth from FGL. In both cases the minimum foundation depth shall be 1.5 m from FGL.

In case the required nsbc is available beyond 1.5 m depth, this foundation design does not stand applicable.

6. This foundation design shall not be used in case of organic silt, organic clay, or peat layers are found at any depths during soil investigation.

7. This foundation design shall not be adopted at sites where to ground improvement/liquefaction and in this case special foundation shall be done.

8. Any discrepancy in the drawing & site conditions shall be brought to the notice of site engineer & consultant.

9. In case top of pedestal is found to be lower than the road level/high flood level, then base plate encasement shall be taken up in site with site engineer/incharge/consultant.

| Foundation Quantity |               |
|---------------------|---------------|
| Items               | Per structure |
| Concrete            | 1.44 cum      |
| PCC                 | 0.22 cum      |
| Steel               | 123.8 kg      |
| Shuttering          | 10.80 sq.m    |
| Excavation          | 12.70 cum     |

Refer DWG. SPS-65GT-C-01 for baseplate and anchor bolt details

| Rev | Date       | Prepared | Approved |
|-----|------------|----------|----------|
| 0   | 09-03-2020 | GVR      | SSR      |



Tilt angle: 25deg

Panel Area : 4 x 4 m

Ground clearance : 2m

Net SBC : 5 T/m<sup>2</sup>

Water Table : At Ground level



DWG No: 15RIT-70/FD/4x4/2GC/25deg-5PWT

Sheet 1 of 3

Released for Construction

Isolated Foundation Structural drawing

# BAR BENDING SCHEDULE

| # | Shape of Bar                                                                                     | Length of Bar (mm) | Dia. of Bar (mm) | Spacing (mm) | No. of Bars/ leg | No. of Bars/ structure | Unit Weight | Total Weight |
|---|--------------------------------------------------------------------------------------------------|--------------------|------------------|--------------|------------------|------------------------|-------------|--------------|
| 1 |                 | 1050               | 10               | 300          | 10               | 40                     | 0.62        | 26.0         |
| 2 |                 | 1050               | 10               | 300          | 10               | 40                     | 0.62        | 26.0         |
| 4 |                 | 2050               | 16               | -            | 4                | 16                     | 1.58        | 51.8         |
| 5 | <br>Hook - 50mm | 900                | 8                | 200          | 10               | 40                     | 0.39        | 14.0         |

\* Refer note 1.13

|                           |       |
|---------------------------|-------|
| Weight of steel (kg)      | 117.9 |
| Wastage and splices (kg)  | 5.9   |
| Total Steel Quantity (kg) | 123.8 |

For, EXCEL ELECTRICALS

AUTH. SIGN.

|     |            |          |          |
|-----|------------|----------|----------|
| Rev | Date       | Prepared | Approved |
| 0   | 09-03-2020 | GVR      | SSR      |

**RAMBOLL**

Tilt angle: 25deg

Panel Area : 4 x 4 m

Ground clearance : 2m

Net SBC : 5 T/m<sup>2</sup>

Water Table : At Ground level

DWG No: 15RIT-70/FD/4x4/2GC/25deg-5FWT

Sheet 2 of 3

Released for Construction

Isolated Foundation Structural drawing

## GENERAL NOTES

### 1. GENERAL & MATERIAL

- 1.1 ALL DIMENSIONS ARE IN "mm" U.O.S.
- 1.2 DO NOT SCALE DRAWING.
- 1.3 RCC & LEAN CONCRETE SHALL BE OF GRADE M20 & M10 RESPECTIVELY.
- 1.4 FOR AGGRESSIVE SOIL/EXPOSURE CONDITIONS, MINIMUM GRADE OF CONCRETE SHALL BE REFERRED AS PER IS456:2000, TABLE 3 AND 5.
- 1.5 LEAN CONCRETE SHALL BE OF GRADE M10 WITH MIX PROPORTION OF 1:3:6
- 1.6 STEEL GRADE IS Fe415 U.O.S. AS PER IS 1786 / IS 1159
- 1.7 IF ANY LEVEL DIFFERENCE IN EXISTING GROUND IS FOUND, THEN SOIL EXCAVATION FOR FOUNDATION SHALL BE STARTED WITH REFERENCE TO THE LOWER LEVEL AND THE SOIL SHALL BE BACK FILLED AND COMPACTED UP TO THE TOP MOST LEVEL OF NATURAL GROUND LEVEL TO AVOID SOIL EROSION.
- 1.8 VERIFY THE ADJACENT SITE FEATURES BEFORE EXCAVATION. PROPER CARE SHALL BE TAKEN TO AVOID DAMAGE TO ADJACENT STRUCTURE.
- 1.9 ANY DISCREPANCY IN THE DRAWING (VS) SITE CONDITIONS SHALL BE BROUGHT TO THE NOTICE OF SITE ENGINEER & CONSULTANT (Ramboll India Pvt. Ltd.)
- 1.10 NO FURTHER EXCAVATION/CONSTRUCTION IS ALLOWED WITHIN ZONE OF FOUNDATION AND IF ANY SHALL BE VALIDATED BY CONSULTANT.
- 1.11 REINFORCEMENT SHALL BE SUITABLY ADJUSTED AT SITE TO CLEAR POCKETS, BOLTS, OPENINGS, CUTOUT, ETC. AS APPROVED BY SITE ENGINEER UNLESS OTHERWISE SHOWN IN DRAWING.
- 1.12 THE CONTRACTOR/CLIENT SHALL VERIFY ALL QUANTITY, DIMENSION AND CONDITION WITH SITE AND NOTIFY THE ENGINEER/CONSULTANT, IF ANY DISCREPANCY IN DRAWING AND/OR SPECIFICATION BEFORE PROCEEDING THE WORK.
- 1.13 THE TOTAL LENGTH OF BARS (CUTTING LENGTH) SHALL BE CALCULATED ON THE BASIS OF THE APPROPRIATE BENDING DIMENSIONS WITH CORRECTIONS FOR BENDS AND ALLOWANCES FOR ANCHORAGES.

### 2. TECHNICAL SPECS

- 2.1 MINIMUM COVER TO THE MAIN REINFORCEMENT  
FOR COLUMN 50mm  
FOR PAD(DRAFT SLAB) 50mm  
FOR BEAM 50mm.
- 2.2 THE LAP LENGTH/DEVELOPMENT LENGTH OF BARS SHALL BE AS PER  
DOC. No.R4G-70-TWC-GEN-PR-049 OR RELEVANT IS CODE.
- 2.3 NO HONEYCOMB/CAP SHALL BE PERMITTED WHILE CONCRETING.
- 2.4 NO CONSTRUCTION JOINT SHALL BE ALLOWED OTHER THAN SPECIFIED.
- 2.5 CONSTRUCTION SHALL BE CARRIED OUT IN ACCORDANCE TO VARIOUS PROVISIONS LAID DOWN IN IS:456/IS:800 STANDARDS.
- 2.6 STRIPPING OF FORMWORK & CURING SHALL BE CARRIED OUT AS PER THE PROVISIONS OF IS:456.

### 3. EXCAVATION & BACKFILLING

- 3.1 THE SIDE SLOPES FOR EXCAVATION SHALL BE DIVIDED AS PER THE FOLLOWING GUIDELINES:
  - a) FOR SANDY SOILS, SLOPE 1V:2H
  - b) FOR CLAYEY SOILS, SLOPE 1V:1H
  - c) FOR HARD STRATA, VERTICAL CUTALTERNATIVELY, SUFFICIENT SHEET PILES/SHORING SHALL BE USED DURING EXCAVATION TO PREVENT SIDE COLLAPSE.
- 3.2 SAND BEDDING/STONE BEDDING SHALL BE PROVIDED IN FOUNDATIONS OF MARSHILY AND WET BLACK COTTON SOIL.

- 3.3 IN CASE OF NO GROUND WATER, ALL FOUNDATION PITS SHALL BE SOAKED WITH WATER FOR 24 HOURS AND COMPACTED WELL BEFORE PLACING LEAN CONCRETE.
- 3.4 LOOSE POCKETS OF SOIL, (IF ANY FOUND) IN FOUNDATION PITS SHALL BE COMPLETELY REMOVED FOR LOOSE MATERIAL AND FILLED WITH LEAN CONCRETE & COMPACTED WELL BEFORE FOUNDATIONS IS LAID.
- 3.5 FOUNDATION PIT SHALL BE KEPT DRY (FREE FROM WATER) DURING LAYING OF LEAN CONCRETE & RCC AND FURTHER TO A PERIOD OF 48 HOURS (MIN) FROM THE CONCRETE LAYING TIME.
- 3.6 ALL BACK FILLING OF FOUNDATION SHOULD BE DONE WITH WELL COMPACTED MURRUM SOIL.
- 3.7 THE BACK FILLING MATERIALS SHOULD BE CLEAN AND FREE FROM ORGANIC OR OTHER FOREIGN MATERIALS.
- 3.8 SOIL BACK FILL SHALL BE DONE IN LAYERS OF APPROX. 150-200mm, EACH LAYERS SHALL BE DENSELY COMPACTED BY SPRINKLING MINIMUM QUANTITY OF WATER AS NECESSARY FOR PROPER COMPACTION AND MINIMUM BACKFILL SOIL DENSITY SHALL BE 1700 kg/m<sup>3</sup>
- 3.9 CARE SHALL BE TAKEN THAT THE BACK FILLING IS STARTED FROM THE CENTRE TOWARDS THE OUTER ENDS
- 3.10 AFTER BACK FILLING 50mm HIGH EARTHEN EMBANKMENT(BUND) TO BE MADE ALONG THE SIDES OF EXCAVATED PITS AND SUFFICIENT WATER WILL BE POURED OVER THE BACK FILLED EARTH FOR ATLEAST 24HRS.
- 3.11 FINISHED GROUND LEVEL AT COLUMN/CHIMNEY SHOULD BE SLOPED AWAY, WITH SLOPE OF 1:3 TO PREVENT ACCUMULATION OR PONDING OF WATER.
- 3.12 SURFACE DRAINAGE OF THE PLOT SHOULD BE MADE SO AS TO AVOID WATER LOGGING IN THE PLOT, IN PARTICULAR AROUND THE FOUNDATION
- 3.13 IN CASE TOP OF PEDESTAL IS FOUND TO BE LOWER THAN THE ROAD LEVEL/HIGH FLOOD LEVEL, THEN BASE PLATE ENCASMENT SHALL BE TAKEN UP IN CONSULTATION WITH THE SITE ENGINEER/INCHARGE/CONSULTANT.
- 3.14 EXCAVATION PLAN & VOLUME SHOWN IN DRAWING IS INDICATIVE ONLY & THIS IS APPLICABLE FOR NORMAL SOIL CONDITIONS. IT MAY VARY, AS PER SITE CONDITION & STRATA ENCOUNTERED.

### 4. TEMPLATE ASSEMBLY/ GROUTING

- 4.1 VERIFY BOLT, NUT SIZE AND LENGTH AS PER TEMPLATE/BASE ASSEMBLY DRAWING.
- 4.2 CHECK THE INTEGRITY OF BOLT AND NUT BEFORE EXECUTION AT SITE. IF ANY PLAY FOUND, CONSULT SITE ENGINEER/CONSULTANT.
- 4.3 GROUTING UNDER BASE PLATE HAS TO BE DONE WITH FREE FLOW NON SHRINK GROUT HAVING MINIMUM STRENGTH AS THAT OF CONCRETE.

### LEGEND

U.O.S. - UNLESS OTHERWISE SPECIFIED.

→ - INDICATES CHAIR LOCATIONS

F.G.L + FINISHED GROUND LEVEL

E.G.L + EXISTING GROUND LEVEL

T & B' - TOP AND BOTTOM

TOS - TOP OF SLAB

BOS - BOTTOM OF SLAB

FOR, **EXCEL ELECTRICALS**

**AUTH. SIGN.**

**RAMBOLL**

| Rev | Date       | Prepared | Approved |
|-----|------------|----------|----------|
| 0   | 09-03-2020 | GVR      | SSR      |

Tilt angle: 25deg

Panel Area : 4 x 4 m

Ground clearance : 2m

Net SBC : 5 T/m<sup>2</sup>

Water Table : At Ground level

DWG No: 15RIT-70/FD/4x4/2G/25deg-5FWT

Sheet 3 of 3

Released for Construction

Isolated Foundation Structural drawing

### Vendor Document Review Sheet

|                     |                                                                                                                                        |
|---------------------|----------------------------------------------------------------------------------------------------------------------------------------|
| PROJECT TITLE:      | 4G Project                                                                                                                             |
| VENDOR NAME:        | Ramboll India Pvt Ltd                                                                                                                  |
| DOCUMENT TITLE:     | Foundation drawing for Solar supporting structure (Panel area: 4x10m) Tilt: 25 deg Ground clearance- 2m_SBC: 5T/m^2 (Full water Table) |
| VENDOR DOCUMENT NO. | 15RIT-70/FD/4x10/2GC/25deg-5FWT                                                                                                        |
| VENDOR REVISION NO: | 0                                                                                                                                      |

### VENDOR DOCUMENT REVIEW FEEDBACK

Permission to proceed does not constitute acceptance or approval of Design Detail, Calculations, Analysis, Test Methods or Materials developed OR selected by Vendor, and does NOT relieve Vendor from FULL compliance with Contractual Obligations


- |                                                                                                        |                                                                          |
|--------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------|
| <input type="checkbox"/> 1 Work may proceed.                                                           | <input type="checkbox"/> 5 Revise and Resubmit.<br>Work may not proceed. |
| <input checked="" type="checkbox"/> 2 Review not required, Work may proceed.                           | <input type="checkbox"/> 6 For Information Only                          |
| <input type="checkbox"/> 3 Revise & Resubmit at Final stage                                            | <input type="checkbox"/> SUP Superseded                                  |
| <input type="checkbox"/> 4 Revise & Resubmit. Work may proceed,<br>subject to incorporation of changes | <input type="checkbox"/> CAN Cancelled / Not required.                   |

By: Deepa Nair Date: 21.05.2020


|                                  |                                                                                                                                                                                                                             |           |          |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|----------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------|----------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
| Discipline:                      |                                                                                                                                                                                                                             |           |          |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Equipment No.<br>(if applicable) |                                                                                                                                                                                                                             |           |          |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| MR Number<br>(if applicable)     | <table border="1"> <tr> <td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td> </tr> </table> |           |          |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|                                  |                                                                                                                                                                                                                             |           |          |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Project No                       | PO No                                                                                                                                                                                                                       | Cat. Code | Seq. No. |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 10070                            | 1 1 8 - 6 3 5 1 0 6 5 9                                                                                                                                                                                                     | B 0 5     | 1 4 0    |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|                                  |                                                                                                                                                                                                                             |           | Rev No   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|                                  |                                                                                                                                                                                                                             |           | 0 0      |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |

For, EXCEL ELECTRICALS  
  
 AUTH. SIGN.


| Dimensions     |         |
|----------------|---------|
| L1             | 3.900 m |
| L2             | 1.950 m |
| B              | 1.500 m |
| B1             | 9.300 m |
| B2             | 3.450 m |
| S              | 0.300 m |
| G1             | 0.200 m |
| SOK            | 0.300 m |
| d1             | 1.250 m |
| d2             | 1.450 m |
| D              | 1.500 m |
| Embedded depth | 0.400 m |

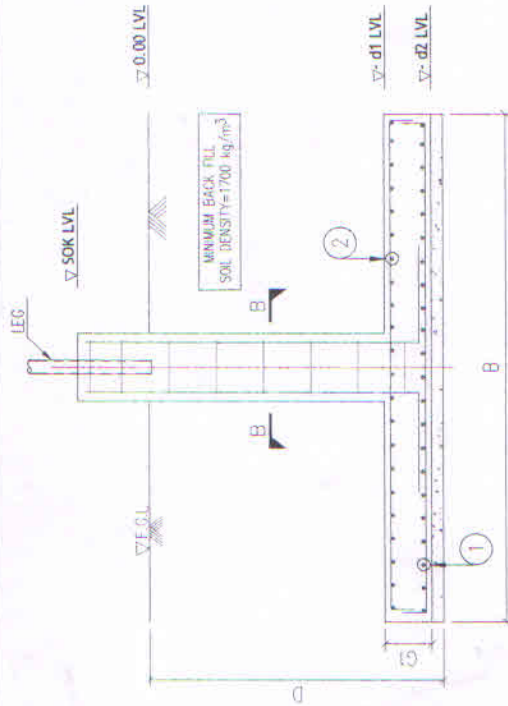

**FOUNDATION DETAIL**  
(SECTION "A-A")




**SECTION "B-B"**

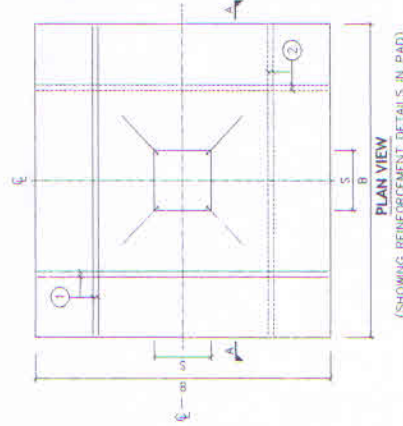

**PLAN VIEW**

(SHOWING REINFORCEMENT DETAILS IN PAD)

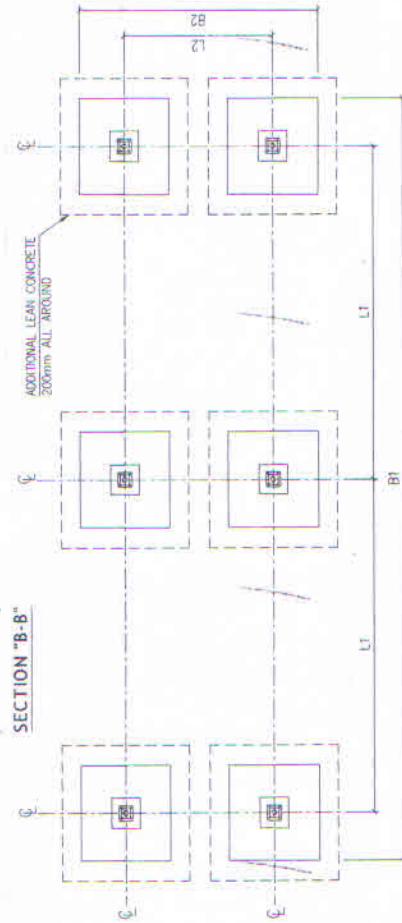

**EXCAVATION PLAN**

**For, EXCEL ELECTRICALS**

**AUTH. SIGN.**

**General notes**

1. This is a generic foundation drawing.
2. The following are the assumed parameters considered during foundation design

Net safe bearing capacity (NSBC) =  $57/\text{m}^2$

Ground water table = At Ground level

Depth of foundation = 1.5 m

Dry density of soil =  $1700 \text{ kg/m}^3$

Angle of internal friction = 10 deg

3. Before commencement of construction work using these designs, the owner/client/civil contractor shall carry out detailed soil investigation of every site.

4. Further, the soil investigation report shall be reviewed by a consultant and certification shall be obtained to ensure conformity between assumed parameters and soil report values before start of construction.

5. The foundation design is applicable only when the considered NSBC is available at or within 1.5 m depth from FGL. In both cases the minimum foundation depth shall be 1.5 m from FGL.

In case the required nsbc is available beyond 1.5 m depth, this foundation design does not stand applicable.

6. This foundation design shall not be used in case of organic silt, organic clay, or peat layers are found at any depths during soil investigation.

7. This foundation design shall not be adopted at sites where to ground improvement/liquefaction and in this case special foundation shall be done.

8. Any discrepancy in the drawing & site conditions shall be brought to the notice of site engineer & consultant.

9. In case top of pedestal is found to be lower than the road level/high flood level, then base plate encasement shall be taken up in site with the site engineer/incharge/consultant.

| Items      | Per structure |
|------------|---------------|
| Concrete   | 3.54 cum      |
| PCC        | 0.68 cum      |
| Steel      | 252.3 kg      |
| Shuttering | 18.36 sq.m    |
| Excavation | 32.50 cum     |

Note: For excavation, 200mm extra considered over pad size

Refer DWG. SPS-65GT-C-01 for baseplate and anchor bolt details

| Rev | Date       | Prepared | Approved |
|-----|------------|----------|----------|
| 0   | 09-03-2020 | GVR      | SSR      |



Tilt angle : 25deg

Panel Area : 4 x 10 m

Ground clearance : 2 m

Net SBC :  $57/\text{m}^2$

Water Table : At Ground level



DWG No: 15RIT-70/FD/4x10/25deg/2GC-5PWT

Sheet 1 of 3

Released for Construction

Isolated Foundation Structural drawing

### BAR BENDING SCHEDULE

| # | Shape of Bar                                                                                     | Length of Bar (mm) | Dia. of Bar (mm) | Spacing (mm) | No. of Bars/ leg | No. of Bars/ structure | Unit Weight | Total Weight |
|---|--------------------------------------------------------------------------------------------------|--------------------|------------------|--------------|------------------|------------------------|-------------|--------------|
| 1 |                 | 1500               | 10               | 300          | 12               | 72                     | 0.62        | 67.0         |
| 2 |                 | 1500               | 10               | 300          | 12               | 72                     | 0.62        | 67.0         |
| 4 |                 | 2250               | 16               | -            | 4                | 24                     | 1.58        | 85.3         |
| 5 | <br>Hook - 50mm | 900                | 8                | 200          | 10               | 60                     | 0.39        | 21.1         |

\* Refer note 1.13

|                           |       |
|---------------------------|-------|
| Weight of steel (kg)      | 240.3 |
| Wastage and splices (kg)  | 12.0  |
| Total Steel Quantity (kg) | 252.3 |

For, EXCEL ELECTRICALS

  
AUTH. SIGN.

|     |            |          |          |
|-----|------------|----------|----------|
| Rev | Date       | Prepared | Approved |
| 0   | 09-03-2020 | GVR      | SSR      |

**RAMBOLL**

Tilt angle : 25deg

Panel Area : 4 x 10 m

Ground clearance : 2 m

Net SBC : 5 T/m<sup>2</sup>

Water Table : At Ground level

DWG No: 15RIT-70/FD/4x10/25deg/2GC-5FWT

Sheet 2 of 3

Released for Construction

Isolated Foundation Structural drawing

## GENERAL NOTES

### 1. GENERAL & MATERIAL

- 1.1 ALL DIMENSIONS ARE IN "mm" U.O.S.
- 1.2 DO NOT SCALE DRAWING.
- 1.3 RCC & LEAN CONCRETE SHALL BE OF GRADE M20 & M10 RESPECTIVELY
- 1.4 FOR AGGRESSIVE SOIL/EXPOSURE CONDITIONS, MINIMUM GRADE OF CONCRETE SHALL BE REFERRED AS PER IS:456 2000, TABLE 3 AND 5
- 1.5 LEAN CONCRETE SHALL BE OF GRADE M10 WITH MIX PROPORTION OF 1:3:6
- 1.6 STEEL GRADE IS Fe415 U.O.S. AS PER IS 1786 / IS 1159
- 1.7 IF ANY LEVEL DIFFERENCE IN EXISTING GROUND IS FOUND, THEN SOIL EXCAVATION FOR FOUNDATION SHALL BE STARTED WITH REFERENCE TO THE LOWER LEVEL AND THE SOIL SHALL BE BACK FILLED AND COMPACTED UP TO THE TOP MOST LEVEL OF NATURAL GROUND LEVEL TO AVOID SOIL EROSION.
- 1.8 VERIFY THE ADJACENT SITE FEATURES BEFORE EXCAVATION, PROPER CARE SHALL BE TAKEN TO AVOID DAMAGE TO ADJACENT STRUCTURE.
- 1.9 ANY DISCREPANCY IN THE DRAWING (VS) SITE CONDITIONS SHALL BE BROUGHT TO THE NOTICE OF SITE ENGINEER & CONSULTANT (Ramboll India Pvt. Ltd.)
- 1.10 NO FURTHER EXCAVATION/CONSTRUCTION IS ALLOWED WITHIN ZONE OF FOUNDATION AND IF ANY SHALL BE VALIDATED BY CONSULTANT.
- 1.11 REINFORCEMENT SHALL BE SUITABLY ADJUSTED AT SITE TO CLEAR POCKETS, BOLTS, OPENINGS, CUTOUT, ETC. AS APPROVED BY SITE ENGINEER UNLESS OTHERWISE SHOWN IN DRAWING.
- 1.12 THE CONTRACTOR/CLIENT SHALL VERIFY ALL QUANTITY, DIMENSION AND CONDITION WITH SITE AND NOTIFY THE ENGINEER/CONSULTANT IF ANY DISCREPANCY IN DRAWING AND/OR SPECIFICATION BEFORE PROCEEDING THE WORK.
- 1.13 THE TOTAL LENGTH OF BARS (CUTTING LENGTH) SHALL BE CALCULATED ON THE BASIS OF THE APPROPRIATE BENDING DIMENSIONS WITH CORRECTIONS FOR BENDS AND ALLOWANCES FOR ANCHORAGES.

### 2. TECHNICAL SPECS

- 2.1 MINIMUM COVER TO THE MAIN REINFORCEMENT  
FOR COLUMN 50mm  
FOR PAD/RAFT SLAB) 50mm  
FOR BEAM 50mm.
- 2.2 THE LAP LENGTH/DEVELOPMENT LENGTH OF BARS SHALL BE AS PER  
DOC. No.R46-70-TWC-GEN-PR-049 OR RELEVANT IS CODE.
- 2.3 NO HONEYCOMB/GAP SHALL BE PERMITTED WHILE CONCRETING.
- 2.4 NO CONSTRUCTION JOINT SHALL BE ALLOWED OTHER THAN SPECIFIED
- 2.5 CONSTRUCTION SHALL BE CARRIED OUT IN ACCORDANCE TO VARIOUS PROVISIONS LAID DOWN IN IS:456/IS:800 STANDARDS.
- 2.6 STRIPPING OF FORMWORK & CURING SHALL BE CARRIED OUT AS PER THE PROVISIONS OF IS:456.

### 3. EXCAVATION & BACKFILLING

- 3.1 THE SIDE SLOPES FOR EXCAVATION SHALL BE DIVIDED AS PER THE FOLLOWING GUIDELINES:
  - a) FOR SANDY SOILS, SLOPE 1V:2H
  - b) FOR CLAYEY SOILS, SLOPE 1V:1H
  - c) FOR HARD STRATA, VERTICAL CUTALTERNATIVELY, SUFFICIENT SHEET PILES/SHORING SHALL BE USED DURING EXCAVATION TO PREVENT SIDE COLLAPSE.
- 3.2 SAND BEDDING/STONE BEDDING SHALL BE PROVIDED IN FOUNDATIONS OF MARSHLY AND WET BLACK COTTON SOIL

- 3.3 IN CASE OF NO GROUND WATER, ALL FOUNDATION PITS SHALL BE SOAKED WITH WATER FOR 24 HOURS AND COMPACTED WELL BEFORE PLACING LEAN CONCRETE.
- 3.4 LOOSE POCKETS OF SOIL, IF ANY FOUND IN FOUNDATION PITS SHALL BE COMPLETELY REMOVED FOR LOOSE MATERIAL AND FILLED WITH LEAN CONCRETE & COMPACTED WELL BEFORE FOUNDATION IS LAID.
- 3.5 FOUNDATION PIT SHALL BE KEPT DRY (FREE FROM WATER) DURING LAYING OF LEAN CONCRETE & RCC AND FURTHER TO A PERIOD OF 48 HOURS (MIN.) FROM THE CONCRETE LAYING TIME.
- 3.6 ALL BACK FILLING OF FOUNDATION SHOULD BE DONE WITH WELL COMPACTED MURRUM SOIL.
- 3.7 THE BACK FILLING MATERIALS SHOULD BE CLEAN AND FREE FROM ORGANIC OR OTHER FOREIGN MATERIALS.
- 3.8 SOIL BACK FILL SHALL BE DONE IN LAYERS OF APPROX. 150-200mm, EACH LAYERS SHALL BE DENSELY COMPACTED BY SPRINKLING MINIMUM QUANTITY OF WATER AS NECESSARY FOR PROPER COMPACTION AND MINIMUM BACKFILL SOIL DENSITY SHALL BE 1700 kg/m<sup>3</sup>
- 3.9 CARE SHALL BE TAKEN THAT THE BACK FILLING IS STARTED FROM THE CENTRE TOWARDS THE OUTER ENDS
- 3.10 AFTER BACK FILLING 50mm HIGH EARTHEN EMBANKMENT(BUND) TO BE MADE ALONG THE SIDES OF EXCAVATED PITS AND SUFFICIENT WATER WILL BE POURED OVER THE BACK FILLED EARTH FOR ATLEAST 24HRS.
- 3.11 FINISHED GROUND LEVEL AT COLUMN/CHIMNEY SHOULD BE SLOPED AWAY WITH SLOPE OF 1:3 TO PREVENT ACCUMULATION OR PONDING OF WATER
- 3.12 SURFACE DRAINAGE OF THE PLOT SHOULD BE MADE SO AS TO AVOID WATER LOGGING IN THE PLOT, IN PARTICULAR AROUND THE FOUNDATION
- 3.13 IN CASE TOP OF PILE/STAIL IS FOUND TO BE LOWER THAN THE ROAD LEVEL/HIGH FLOOD LEVEL, THEN BASE PLATE ENCASMENT SHALL BE TAKEN UP IN CONSULTATION WITH THE SITE ENGINEER/INCHARGE/CONSULTANT
- 3.14 EXCAVATION PLAN & VOLUME SHOWN IN DRAWING IS INDICATIVE ONLY & THIS IS APPLICABLE FOR NORMAL SOIL CONDITIONS. IT MAY VARY, AS PER SITE CONDITION & STRATA ENCOUNTERED.

### 4. TEMPLATE ASSEMBLY/ GROUTING

- 4.1 VERIFY BOLT, NUT SIZE AND LENGTH AS PER TEMPLATE/BASE ASSEMBLY DRAWING.
- 4.2 CHECK THE INTEGRITY OF BOLT AND NUT BEFORE EXECUTION AT SITE. IF ANY PLAY FOUND, CONSULT SITE ENGINEER/CONSULTANT.
- 4.3 GROUTING UNDER BASE PLATE HAS TO BE DONE WITH FREE FLOW NON SHRINK GROUT HAVING MINIMUM STRENGTH AS THAT OF CONCRETE.

### LEGEND

U.O.S. - UNLESS OTHERWISE SPECIFIED.

↖ - INDICATES CHAIR LOCATIONS

F.G.L - FINISHED GROUND LEVEL

E.G.L - EXISTING GROUND LEVEL

T & B - TOP AND BOTTOM

TOS - TOP OF SLAB

BOS - BOTTOM OF SLAB

For, **EXCEL ELECTRICALS**

**AUTH. SIGN.**

**RAMBOLL**

| Rev | Date       | Prepared | Approved |
|-----|------------|----------|----------|
| 0   | 09-03-2020 | GVR      | SSR      |

Tilt angle : 25deg

Panel Area : 4 x 10 m

Ground clearance : 2 m

Net SBC : 5 T/m<sup>2</sup>

Water Table : At Ground level

DWG No: 15RIT-70/FD/4x10/25deg/2GC-5FWT

Sheet 3 of 3

Released for Construction

Isolated Foundation Structural drawing



Geo Technical Solutions

# Om Geo Tech Services

(ISO 9001 CERTIFIED LAB)

NADIAD

CIVIL ENGINEERING CONSULTANCY & TESTING LAB

■ Civil Engineering Material Testing ■ Destructive & Non Destructive Testing ■ Pile & Load Test  
■ BI & BBD in Highway Testing ■ Physical & Resistivity Survey

## Test Report on Compressive Strength of Concrete Cubes

E:\OM GEO TECH\20\TRF 0978-Excel\data\CC Cube

Discipline/Group » Mechanical-Buildings Material  
Sample ID No. » 01/20220418/CC Cube  
Report Ref No » OGTS-2022-23/01/20220418/CC Cube

ULR-TC872622000001740F

Date of Report » 07-May-22

Customer » Reliance Jio  
Name of Work » Site ID:- I-GJ-VASO-ENB-9001  
Agency » Excel Electricals, Jamnagar

Witness Person » Mr. Jayeshbhai Panchal  
Date of Sample Received » 19-Apr-22  
Material Received » Concrete Cubes  
Method of Test » IS 516-1959 RA - 2018 Clause 5.0

Element » Raft

| Sr. No. | Sample ID | Date of Casting ** | Date of Testing | Required Age of Test (days) | Grade of Concrete ** | Length (mm) | Width (mm) | Height (mm) | Max.Load at Failure, (KN) | Weight of Spec. (Kg) | Comp. Strength, (N/mm <sup>2</sup> ) | Sample Density (Kg/m <sup>3</sup> ) |
|---------|-----------|--------------------|-----------------|-----------------------------|----------------------|-------------|------------|-------------|---------------------------|----------------------|--------------------------------------|-------------------------------------|
| 1       | Cube 1    | 18-Apr-22          | 07-May-22       | 19                          | M 20                 | 150.00      | 150.00     | 150.00      | 611.4                     | 8.98                 | 27.17                                | 2661.6                              |
| 2       | Cube 2    |                    |                 |                             |                      | 150.00      | 150.00     | 150.00      | 661.1                     | 9.05                 | 29.38                                | 2682.4                              |
| 3       | Cube 3    |                    |                 |                             |                      | 150.00      | 150.00     | 150.00      | 726.9                     | 9.01                 | 32.31                                | 2668.1                              |
| Average |           |                    |                 |                             |                      |             |            |             |                           |                      | 29.62                                | 2670.7                              |

» **Remark :-** The Average of Three Samples Values shall be taken as the Representative of the Batch provided the individual variation is not more than  $\pm 15\%$  of the Average. Otherwise repeat tests shall be made as per IS 516-Clause-5.6

Requirements as per IS 456:2000-(Reaffirmed-2016)Table No.2 (Clause 6.1, 9.2.2, 15.1.1, and 36.1)

| Grade of Concrete                                                         | M10 | M15 | M20 | M25 | M30 | M35 | M40 | M45 |
|---------------------------------------------------------------------------|-----|-----|-----|-----|-----|-----|-----|-----|
| Accepted Strength on 28 days of curing for Nominal Mix, N/mm <sup>2</sup> | 10  | 15  | 20  | 25  | 30  | 35  | 40  | 45  |

\*\* M-10 is a Nominal Mix Concrete

•• End of Report ••

### Note :-

- The results are given only for the sample submitted by the Customer.
- The test report shall not be reproduced except in full, without written approval of the laboratory.
- Om Geo Tech Services is not responsible for any kind of interpretation of test results
- The results/report is not used for publicity.
- \*\* As informed by client



Doc ID: FMT-TST-01 / Page 1/1



Nadiad - Dabhan Road,  
Nr. Bhutia Bunglow, Nr. MGVL Office,  
NADIAD - 387 320



omgeotech18@gmail.com



94273 16024 , 99987 89919



Geo Technical Solutions

# Om Geo Tech Services

(ISO 9001 CERTIFIED LAB)

NADIAD

CIVIL ENGINEERING CONSULTANCY & TESTING LAB

■ Civil Engineering Material Testing ■ Destructive & Non Destructive Testing ■ Pile & Load Test  
■ BI & BBD in Highway Testing ■ Physical & Resistivity Survey

## Test Report on Compressive Strength of Concrete Cubes

E:\OM GEO TECH\JO\TRF 0978-Excel sheet\CC Cube

Discipline/Group » Mechanical-Buildings Material  
Sample ID No. » 01/20220427/CC Cube  
Report Ref No » OGTS-2022-23/01/20220427/CC Cube

ULR-TC872622000001743F

Date of Report » 07-May-22

Customer » Reliance Jio  
Name of Work » Site ID:- I-GJ-VASO-ENB-9001  
Agency » Excel Electricals, Jamnagar

Witness Person » Mr. Jayeshbhai Panchal  
Date of Sample Received » 28-Apr-22  
Material Received » Concrete Cubes  
Method of Test » IS 516-1959 RA - 2018 Clause 5.0

Element » Column

| Sr. No. | Sample ID | Date of Casting ** | Date of Testing | Required Age of Test (days) | Grade of Concrete ** | Length (mm) | Width (mm) | Height (mm) | Max.Load at Failure, (KN) | Weight of Spec. (Kg) | Comp. Strength, (N/mm <sup>2</sup> ) | Sample Density (Kg/m <sup>3</sup> ) |
|---------|-----------|--------------------|-----------------|-----------------------------|----------------------|-------------|------------|-------------|---------------------------|----------------------|--------------------------------------|-------------------------------------|
| 1       | Cube 1    | 27-Apr-22          | 07-May-22       | 10                          | M 20                 | 150.00      | 150.00     | 150.00      | 321.9                     | 8.50                 | 14.31                                | 2518.8                              |
| 2       | Cube 2    |                    |                 |                             |                      | 150.00      | 150.00     | 150.00      | 498.0                     | 8.45                 | 22.13                                | 2504.0                              |
| 3       | Cube 3    |                    |                 |                             |                      | 150.00      | 150.00     | 150.00      | 347.5                     | 8.71                 | 15.44                                | 2579.3                              |
| Average |           |                    |                 |                             |                      |             |            |             |                           |                      | 17.29                                | 2534.0                              |

» **Remark :-** The Average of Three Samples Values shall be taken as the Representative of the Batch provided the individual variation is not more than  $\pm 15\%$  of the Average. Otherwise repeat tests shall be made as per IS 516-Clause-5.6

Requirements as per IS 456:2000-(Reaffirmed-2016)Table No.2 (Clause 6.1, 9.2.2, 15.1.1, and 36.1)

| Grade of Concrete                                                         | M10 | M15 | M20 | M25 | M30 | M35 | M40 | M45 |
|---------------------------------------------------------------------------|-----|-----|-----|-----|-----|-----|-----|-----|
| Accepted Strength on 28 days of curing for Nominal Mix, N/mm <sup>2</sup> | 10  | 15  | 20  | 25  | 30  | 35  | 40  | 45  |

\*\* M-10 is a Nominal Mix Concrete

•• End of Report ••

### Note :-

- The results are given only for the sample submitted by the Customer.
- The test report shall not be reproduced except in full, without written approval of the laboratory.
- Om Geo Tech Services is not responsible for any kind of interpretation of test results
- The results/report is not used for publicity.
- \*\* As informed by client



Authorized Signatory

Doc ID : FMT-TST-01 / Page 1/1



Nadiad - Dabhan Road,  
Nr. Bhutia Bunglow, Nr. MGVCL Office,  
NADIAD - 387 320



omgeotech18@gmail.com



94273 16024 , 99987 89919



Geo Technical Solutions

# Om Geo Tech Services

(ISO 9001 CERTIFIED LAB)

NADIAD

CIVIL ENGINEERING CONSULTANCY & TESTING LAB

■ Civil Engineering Material Testing ■ Destructive & Non Destructive Testing ■ Pile & Load Test  
■ BI & BBD in Highway Testing ■ Physical & Resistivity Survey

## Test Report on Compressive Strength of Concrete Cubes

E:\OM GEO TECH\JIO\TRF 0978-Excel.xlsx\CC Cube

Discipline/Group » Mechanical-Buildings Material  
Sample ID No. » 01/20220427/CC Cube  
Report Ref No » OGTS-2022-23/01/20220427/CC Cube

ULR-TC872622000002161F

Date of Report » 04-Jun-22

Customer » Reliance Jio  
Name of Work » Site ID:- I-GJ-VASO-ENB-9001  
Agency » Excel Electricals, Jamnagar

Witness Person » Mr. Jayeshbhai Panchal  
Date of Sample Received » 28-Apr-22  
Material Received » Concrete Cubes  
Method of Test » IS 516-1959 RA - 2018 Clause 5.0

Element » Column

| Sr. No. | Sample ID | Date of Casting | Date of Testing | Required Age of Test (days) | Grade of Concrete ** | Length (mm) | Width (mm) | Height (mm) | Max.Load at Failure, (KN) | Weight of Spec. (Kg) | Comp. Strength, (N/mm <sup>2</sup> ) | Sample Density (Kg/m <sup>3</sup> ) |
|---------|-----------|-----------------|-----------------|-----------------------------|----------------------|-------------|------------|-------------|---------------------------|----------------------|--------------------------------------|-------------------------------------|
| 1       | Cube 1    | 27-Apr-22       | 04-Jun-22       | 38                          | M 20                 | 150.00      | 150.00     | 150.00      | 716.2                     | 8.68                 | 31.83                                | 2573.0                              |
| 2       | Cube 2    |                 |                 |                             |                      | 150.00      | 150.00     | 150.00      | 663.2                     | 8.32                 | 29.48                                | 2466.1                              |
| 3       | Cube 3    |                 |                 |                             |                      | 150.00      | 150.00     | 150.00      | 562.3                     | 8.52                 | 24.99                                | 2525.0                              |
| Average |           |                 |                 |                             |                      |             |            |             |                           |                      | 28.77                                | 2521.4                              |

» Remark :- The Average of Three Samples Values shall be taken as the Representative of the Batch provided the individual variation is not more than  $\pm 15\%$  of the Average. Otherwise repeat tests shall be made as per IS 516-Clause-5.6

Requirements as per IS 456:2000-(Reaffirmed-2016)Table No.2 (Clause 6.1, 9.2.2, 15.1.1, and 36.1)

| Grade of Concrete                                                         | M10 | M15 | M20 | M25 | M30 | M35 | M40 | M45 |
|---------------------------------------------------------------------------|-----|-----|-----|-----|-----|-----|-----|-----|
| Accepted Strength on 28 days of curing for Nominal Mix, N/mm <sup>2</sup> | 10  | 15  | 20  | 25  | 30  | 35  | 40  | 45  |

\*\* M-10 is a Nominal Mix Concrete

•• End of Report ••

Note :-

- The results are given only for the sample submitted by the Customer.
- The test report shall not be reproduced except in full, without written approval of the laboratory.
- Om Geo Tech Services is not responsible for any kind of interpretation of test results
- The results/report is not used for publicity.
- \*\* As informed by client



Doc ID :- FMT-TST-01 / Page 1/1



Nadiad - Dabhan Road,  
Nr. Bhutia Bunglow, Nr. MGVC Office,  
NADIAD - 387 320



omgeotech18@gmail.com



94273 16024 , 99987 89919



Geo Technical Solutions

# Om Geo Tech Services

(ISO 9001 CERTIFIED LAB)

NADIAD

CIVIL ENGINEERING CONSULTANCY & TESTING LAB

■ Civil Engineering Material Testing ■ Destructive & Non Destructive Testing ■ Pile & Load Test  
■ BI & BBD in Highway Testing ■ Physical & Resistivity Survey

## Test Report on Compressive Strength of Concrete Cubes

E:\OM GEO TECH\JIO\TRF 0979-Excel.xlsx\CC Cube

Discipline/Group » Mechanical-Buildings Material  
Sample ID No. » 01/20220418/CC Cube  
Report Ref No » OGTS-2022-23/01/20220418/CC Cube

ULR-TC872622000001939F

Date of Report » 20-May-22

Customer » Reliance Jio  
Name of Work » Site ID:- I-GJ-VASO-ENB-9001  
Agency » Excel Electricals, Jamnagar

Witness Person » Mr. Abhijibhai  
Date of Sample Received » 19-Apr-22  
Material Received » Concrete Cubes  
Method of Test » IS 516-1959 RA - 2018 Clause 5.0

Element » Raft

| Sr. No. | Sample ID | Date of Casting | Date of Testing | Required Age of Test (days) | Grade of Concrete ** | Length (mm) | Width (mm) | Height (mm) | Max.Load at Failure, (KN) | Weight of Spec. (Kg) | Comp. Strength, (N/mm <sup>2</sup> ) | Sample Density (Kg/m <sup>3</sup> ) |
|---------|-----------|-----------------|-----------------|-----------------------------|----------------------|-------------|------------|-------------|---------------------------|----------------------|--------------------------------------|-------------------------------------|
| 1       | Cube 1    | 18-Apr-22       | 20-May-22       | 32                          | M 20                 | 150.00      | 150.00     | 150.00      | 686.5                     | 9.25                 | 30.51                                | 2740.7                              |
| 2       | Cube 2    |                 |                 |                             |                      | 150.00      | 150.00     | 150.00      | 681.1                     | 9.08                 | 30.27                                | 2689.5                              |
| 3       | Cube 3    |                 |                 |                             |                      | 150.00      | 150.00     | 150.00      | 726.9                     | 8.92                 | 32.31                                | 2642.1                              |
| Average |           |                 |                 |                             |                      |             |            |             |                           |                      | 31.03                                | 2690.8                              |

» **Remark :-** The Average of Three Samples Values shall be taken as the Representative of the Batch provided the individual variation is not more than  $\pm 15\%$  of the Average. Otherwise repeat tests shall be made as per IS 516-Clause-5.6

Requirements as per IS 456:2000-(Reaffirmed-2016) Table No.2 (Clause 6.1, 9.2.2, 15.1.1, and 36.1)

| Grade of Concrete                                                         | M10 | M15 | M20 | M25 | M30 | M35 | M40 | M45 |
|---------------------------------------------------------------------------|-----|-----|-----|-----|-----|-----|-----|-----|
| Accepted Strength on 28 days of curing for Nominal Mix, N/mm <sup>2</sup> | 10  | 15  | 20  | 25  | 30  | 35  | 40  | 45  |

\*\* M-10 is a Nominal Mix Concrete

.. End of Report ..

**Note :-**

- The results are given only for the sample submitted by the Customer.
- The test report shall not be reproduced except in full, without written approval of the laboratory.
- Om Geo Tech Services is not responsible for any kind of interpretation of test results
- The results/report is not used for publicity.
- \*\* As informed by client



Doc ID: EMT-TST-01 / Page 1/1



Nadiad - Dabhan Road,  
Nr. Bhutia Bunglow, Nr. MGVL Office,  
NADIAD - 387 320



omgeotech18@gmail.com



94273 16024 , 99987 89919

## Solar Foundation

| Site Information |                                                                                                                 |
|------------------|-----------------------------------------------------------------------------------------------------------------|
| Sap Id           | I-GJ-VASO-ENB-9001                                                                                              |
| Candidate Id     | C1                                                                                                              |
| Form No          | R4G-70-CQM-FMT-PR-041                                                                                           |
| Site Name        | Thaledi                                                                                                         |
| Site Location    | Open Plot of Garm Panchayat, Nr. Samsan Gruh, Village : Thaledi, Taluka : Vaso, District : Kheda, VASO, Gujarat |
| City             | VASO                                                                                                            |
| Latitude         | 22.618501                                                                                                       |
| Longitude        | 72.802887                                                                                                       |
| R4G State        | Gujarat                                                                                                         |
| Contractor       | excel                                                                                                           |
| Date             | 01 June 2022                                                                                                    |
|                  |                                                                                                                 |
|                  |                                                                                                                 |

For, EXCEL ELECTRICALS  
  
 AUTH. SIGN.

### Inspection Report- Solar Foundation

| Sr.No.             | Description                                                              | Specifications                          | Observations     | Remarks |
|--------------------|--------------------------------------------------------------------------|-----------------------------------------|------------------|---------|
| Preliminary Checks |                                                                          |                                         |                  |         |
| 1.1                | Layout                                                                   | As per Drawing                          | Ok               |         |
| 1.2                | Latest IFC                                                               | Availability                            | Yes              |         |
| Materials          |                                                                          |                                         |                  |         |
| 2.1                | Steel Re-bar                                                             | Test Certificate/no rust/no cracks/Mark | no rust,no crack |         |
| 2.2                | Grade of concrete                                                        | As per Drawing                          | M20              |         |
| 2.3                | Cover blocks                                                             | As per Drawing                          | 50mm             |         |
| Raft Foundation    |                                                                          |                                         |                  |         |
| 3.1                | Check the size of excavated pit as per drawing with limits of excavation | L * B * D                               | 8.5*5*1.5        |         |
| 3.2                | Concrete- RMC/Machine Mix                                                | RMC/Manual                              | machine mix      |         |
| 3.3                | Reinforcement laying as per drawing                                      | As per BBS mentioned in drawing         | as per BBS       |         |
| 3.4.1              | Check spacing of rebars                                                  | As per Drawing                          | As per drawing   |         |
| 3.4.2              | Diameter of re-bars                                                      | As per Drawing                          | 10mm             |         |

For, EXCEL ELECTRICALS  
  
 AUTH. SIGN.

|       |                                                           |                                         |             |  |
|-------|-----------------------------------------------------------|-----------------------------------------|-------------|--|
| 3.5   | Check for Cover                                           | As per Drawing                          | 50mm        |  |
| 3.6   | Application of shuttering oil                             | Visual                                  | Ok          |  |
| 3.7   | Check raft dimension and its shuttering/supporting system | As per Drawing(L*B*D)                   | 1.5*1.5*0.2 |  |
| 3.8   | Check Column dimension and its supporting system          | As per Drawing(L*B*D)                   | 0.3*0.3*1.6 |  |
| 3.9   | Concrete Activity                                         | As per Drawing & Specifications         | Manual      |  |
| 3.9.1 | Grade of concrete                                         | M20/M25/M30                             | M20         |  |
| 3.10  | Use of chute if applicable and height limit 1.7 mtr       | Ht- Max.1.7 mtr                         | 1 mtr       |  |
| 3.11  | Use of vibrator                                           | Needle size                             | 60mm        |  |
| 3.12  | Cubes taken for test                                      | 06 Number of Cubes with Site ID on Cube | 06          |  |
| 3.13  | Ensure Curing                                             | 7 Days by water/Curing Compound         | water       |  |

Pedestal/Column

|       |                                             |                                 |            |  |
|-------|---------------------------------------------|---------------------------------|------------|--|
| 4.1.1 | Reinforcement binding as per drawing        | As per BBS mentioned in drawing | as per BBS |  |
| 4.1.2 | Main Bar, Spacing of rings, stirrups, hooks | As per Drawing                  | 200mm      |  |
| 4.1.3 | Cover                                       | 50mm                            | 50mm       |  |
| 4.1.4 | Application of shuttering oil               | Visual                          | Ok         |  |

For, EXCEL ELECTRICALS

AUTH. SIGN.

|              |                                                                                                             |                                      |                 |  |
|--------------|-------------------------------------------------------------------------------------------------------------|--------------------------------------|-----------------|--|
| 4.1.5        | Column dimension (L*B*D) and its supporting system                                                          | As per Drawing                       | 0.3*0.3         |  |
| 4.1.6.1      | Concreting- Grade-M20/M25/M30                                                                               | As per Drawing & Specification       | M20             |  |
| 4.1.6.2      | Concrete with-RMC/Machine Mix                                                                               | As per Drawing & Specification       | Machine Mix     |  |
| 4.1.7        | Cubes taken for test                                                                                        | 6 Nos. Of Cubes with Site ID on cube | 06              |  |
| 4.1.8        | Ensure Curing                                                                                               | 7 Days by water/Curing Compound      | 7 days by water |  |
| 4.1.9        | Ensure Proper Backfilling with compaction after ensuring 3 days of Curing or application of Curing Compound | As per Guideline                     | ok              |  |
| 4.2.1        | Stub projection from top of concrete & its alignment                                                        | As per Drawing                       | 200mm           |  |
| 4.2.2.1      | Top level of Foundation Stub of all pedestals                                                               | Check with water level Lvl-P1        | 1mm             |  |
| 4.2.2.2      | Top level of Foundation Stub of all pedestals                                                               | Check with water level Lvl-P2        | 00              |  |
| 4.2.2.3      | Top level of Foundation Stub of all pedestals                                                               | Check with water level Lvl-P3        | 2mm             |  |
| Post Casting |                                                                                                             |                                      |                 |  |
| 5.1          | Visual check for cracks,bulging,honeycombing & exposed steel etc. in foundation                             | No Damages                           | no damages      |  |
| 5.2          | Check the c/c distance between foundation bolts                                                             | As per Drawing                       | na              |  |
| 5.3          | Ensure proper backfilling has been done with compaction                                                     | As per Specification                 | ok              |  |

|       |                                                         |                                        |                       |  |
|-------|---------------------------------------------------------|----------------------------------------|-----------------------|--|
| 5.4.1 | 7 days Cube Strength(Raft)                              | 67% & Above                            | to be done            |  |
| 5.4.2 | 7 days Cube Strength(Pedestal)                          | 67% & Above                            | to be done            |  |
| 5.5.1 | 28 Days Cube Strength(Raft)                             | 100% & Above                           | to be done            |  |
| 5.5.2 | 28 Days Cube Strength(Pedestal)                         | 100% & Above                           | to be done            |  |
| 5.6   | Curing of Foundation and Pedestal/Apply curing compound | 7 days curing by water/Curing Compound | 7 day by curing water |  |

Observations and Comments:

ok

For, EXCEL ELECTRICALS

  
AUTH. SIGN.

| CFQ details |                                                                                   |                                                                                    |                                                                                     |
|-------------|-----------------------------------------------------------------------------------|------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|
|             | Contractor's representative                                                       | Field Engineer                                                                     | QC Engineer                                                                         |
| Signature   |  |  |  |
| Name        | bhaveshbhai                                                                       | dilrajbhai                                                                         |                                                                                     |
| Date        | 01 June 2022                                                                      | 01 June 2022                                                                       | --                                                                                  |

  
**ANIL SHAH**  
 MPCM-VADODARA-2  
 Mob. No. 9374710314

For, EXCEL ELECTRICALS

  
 AUTH. SIGN.



|                       | Decimal   | DMS         |
|-----------------------|-----------|-------------|
| Latitude              | 22.702812 | 22°42'10" N |
| Longitude             | 72.84126  | 72°50'28" E |
| 2022-04-28(Thu) 14:26 |           |             |

**ANIL SHAH**  
MPCM-VADODARA-2  
Mob. No. 9374710314

For, EXCEL ELECTRICALS

AUTH. SIGN.

From: [Hardik1.Suthar@ril.com](mailto:Hardik1.Suthar@ril.com)

To: [project.gujarat@excelelectricals.com](mailto:project.gujarat@excelelectricals.com)

Date: 5/9/2022 11:05:16 PM

Subject: RE: [External]RE: Material Reconciliation \_ Excel Electricals

Attachments: RICCO-630186908\_MAY-14 Electrical.pdf  
RICCO-630150746\_MAY-08 Electrical.pdf  
RICCO-630150746\_MAY-09 Electrical.pdf  
RICCO-630163294\_MAY-15 Electrical.pdf  
RICCO-630164230\_MAY-13 Electrical.pdf  
RICCO-630170811\_MAY-01 Electrical.pdf  
RICCO-630170811\_MAY-06 Electrical.pdf  
RICCO-630170811\_MAY-07 Electrical.pdf  
RICCO-630180228\_MAY-04 Civil.pdf  
RICCO-630180228\_MAY-05 Civil.pdf  
RICCO-630186905\_MAY-12 Civil.pdf

QTY in your Ricco found ok As per issued qty.

Pls validate Ricco Site material consumption qty through MPCM/PMO/SITE engineer for billing.

Thanks & Regards  
Hardik Suthar  
7043055098

From: Bhavesh Sadhu <[project.gujarat@excelelectricals.com](mailto:project.gujarat@excelelectricals.com)>

Sent: 05 May 2022 12:11

To: Akash Gandhi <[Akash.Gandhi@ril.com](mailto:Akash.Gandhi@ril.com)>; Subhash1 Khimaniya <[Subhash1.Khimaniya@ril.com](mailto:Subhash1.Khimaniya@ril.com)>

Cc: ilesh.soni@excelelectricals.com; Hardik1 Suthar <[Hardik1.Suthar@ril.com](mailto:Hardik1.Suthar@ril.com)>; Chirag M Shah <[Chirag.M.Shah@ril.com](mailto:Chirag.M.Shah@ril.com)>

Subject: [External]RE: Material Reconciliation \_ Excel Electricals

**Caution:** The e-mail below is from an external source. Please do not open attachments or click links unless this email comes from a known sender and you know the content is safe.

Dear Sir,

Please find attached Reco. for below sites for validation.

Kindly check & validate for further approval.

| SR NO | MP | SAP ID | PROJECT | Material Reconciliation |          |            | SITE RFE1 DATE |
|-------|----|--------|---------|-------------------------|----------|------------|----------------|
|       |    |        |         | Civil                   | Erection | Electrical |                |

For, EXCEL ELECTRICALS

AUTH. SIGN.

|    |             |                    |       |     |     |     |           |
|----|-------------|--------------------|-------|-----|-----|-----|-----------|
| 1  | Ahmedabad-1 | I-GJ-AMBD-ENB-0498 | 5G    | No  | No  | Yes | 30-Apr-22 |
| 2  | Ahmedabad-1 | I-GJ-AMBD-ENB-0041 | 5G    | No  | No  | Yes | 21-Apr-22 |
| 3  | Ahmedabad-2 | I-GJ-BVLA-ESC-0024 | ESC   | No  | Yes | Yes | 28-Feb-22 |
| 4  | Vadodara-2  | I-GJ-KLAL-ESC-0025 | ESC   | No  | Yes | Yes | 8-Apr-22  |
| 5  | Ahmedabad-1 | I-GJ-AMBD-ENB-0871 | 5G    | No  | No  | Yes | 30-Apr-22 |
| 6  | Ahmedabad-1 | I-GJ-AMBD-ENB-0725 | 5G    | No  | No  | Yes | 30-Apr-22 |
| 7  | Ahmedabad-1 | I-GJ-AMBD-ENB-1109 | 5G    | No  | No  | Yes | 29-Mar-22 |
| 8  | Vadodara-2  | I-GJ-MTAR-ENB-9023 | SOLAR | Yes | No  | No  |           |
| 9  | Vadodara-2  | I-GJ-VASO-ENB-9001 | SOLAR | Yes | No  | No  |           |
| 10 | Vadodara-2  | I-GJ-SAQE-ESC-0002 | ESC   | Yes | No  | No  | 28-Apr-22 |

Regards,

**Bhavesh Sadhu**

**Excel Electricals**

**9979130791**

**From:** Bhavesh Sadhu <project.gujarat@excelelectricals.com>

**Sent:** Monday, May 02, 2022 9:07 PM

**To:** 'Akash.Gandhi@ril.com' <Akash.Gandhi@ril.com>; 'Subhash1.Khimaniya@ril.com' <Subhash1.Khimaniya@ril.com>

**Cc:** 'ilesh.soni@excelelectricals.com' <ilesh.soni@excelelectricals.com>; 'Hardik1.Suthar@ril.com'

<Hardik1.Suthar@ril.com>; 'Chirag.M.Shah@ril.com' <Chirag.M.Shah@ril.com>

**Subject:** Material Reconciliation \_ Excel Electricals

Dear Sir,

Please find attached Reco. for below sites for validation.

Kindly check & validate for further approval.

| SR NO | MP          | SAP ID             | PROJECT | Material Reconciliation |          |            | SITE RFE1 DATE |
|-------|-------------|--------------------|---------|-------------------------|----------|------------|----------------|
|       |             |                    |         | Civil                   | Erection | Electrical |                |
| 1     | Ahmedabad-1 | I-GJ-AMBD-ENB-0498 | 5G      | No                      | No       | Yes        | 30-Apr-22      |
| 2     | Ahmedabad-1 | I-GJ-AMBD-ENB-0041 | 5G      | No                      | No       | Yes        | 21-Apr-22      |
| 3     | Ahmedabad-2 | I-GJ-BVLA-ESC-0024 | ESC     | No                      | Yes      | Yes        | 28-Feb-22      |
| 4     | Vadodara-2  | I-GJ-KLAL-ESC-0025 | ESC     | No                      | Yes      | Yes        | 8-Apr-22       |
| 5     | Ahmedabad-1 | I-GJ-AMBD-ENB-0871 | 5G      | No                      | No       | Yes        | 30-Apr-22      |
| 6     | Ahmedabad-1 | I-GJ-AMBD-ENB-0725 | 5G      | No                      | No       | Yes        | 30-Apr-22      |
| 7     | Ahmedabad-1 | I-GJ-AMBD-ENB-1109 | 5G      | No                      | No       | Yes        | 29-Mar-22      |
| 8     | Vadodara-2  | I-GJ-MTAR-ENB-9023 | SOLAR   | Yes                     | No       | No         |                |
| 9     | Vadodara-2  | I-GJ-VASO-ENB-9001 | SOLAR   | Yes                     | No       | No         |                |
| 10    | Vadodara-2  | I-GJ-SAQE-ESC-0002 | ESC     | Yes                     | No       | No         | 28-Apr-22      |

Regards,

**Bhavesh Sadhu**

For, EXCEL ELECTRICALS

  
AUTH. SIGN.

**Excel Electricals**

**9979130791**

**"Confidentiality Warning :** This message and any attachments are intended only for the use of the intended recipient(s), are confidential and may be privileged. If you are not the intended recipient, you are hereby notified that any review, re-transmission, conversion to hard copy, copying, circulation or other use of this message and any attachments is strictly prohibited. If you are not the intended recipient, please notify the sender immediately by return email and delete this message and any attachments from your system.

**Virus Warning:** Although the company has taken reasonable precautions to ensure no viruses are present in this email. The company cannot accept responsibility for any loss or damage arising from the use of this email or attachment."

For, EXCEL ELECTRICALS  
  
AUTH. SIGN.

| Material Reconciliation Statement                                                                                                                                                                                                                                                                                                                                                                                                                                                                               |                                                                  |                                                                                                                                                        |                           |                   |                    |                             |                             |                               |                             |                               |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------|-------------------|--------------------|-----------------------------|-----------------------------|-------------------------------|-----------------------------|-------------------------------|--|---------------------------------------------------------------------------------------|------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------|--------------|---------------|-----------|
| Contractor Name : M/s. Excel Electricals<br>Circle Name : Gujarat North<br>Site ID & Name :<br>Site Count Billed : 01                                                                                                                                                                                                                                                                                                                                                                                           |                                                                  |                                                                                                                                                        |                           |                   |                    |                             |                             |                               |                             |                               |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |
| <table border="1"> <tr> <td>WO No. :</td> <td>630180228</td> </tr> <tr> <td>Invoice No. :</td> <td>MAY/22-23/05</td> </tr> <tr> <td>Invoice Date:</td> <td>01-May-22</td> </tr> </table>                                                                                                                                                                                                                                                                                                                        |                                                                  |                                                                                                                                                        |                           |                   |                    |                             |                             |                               |                             |                               |  | WO No. :                                                                              | 630180228                                                        | Invoice No. :                                                                                                                                          | MAY/22-23/05 | Invoice Date: | 01-May-22 |
| WO No. :                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        | 630180228                                                        |                                                                                                                                                        |                           |                   |                    |                             |                             |                               |                             |                               |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |
| Invoice No. :                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   | MAY/22-23/05                                                     |                                                                                                                                                        |                           |                   |                    |                             |                             |                               |                             |                               |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |
| Invoice Date:                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   | 01-May-22                                                        |                                                                                                                                                        |                           |                   |                    |                             |                             |                               |                             |                               |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |
| A                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | B                                                                | C                                                                                                                                                      | D                         | E                 | F                  | G                           | H                           | I                             | J                           | K                             |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |
| Material No                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     | Material Description                                             | UOM                                                                                                                                                    | Material Received from WH | Received BTN (IN) | Transfer BTN (OUT) | Material Return To WH (MRN) | Consumed & Invoiced Earlier | Consumed & Invoiced Currently | Total Consumption Till Date | Balance with Contractor / WIP |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |
| 2002159304                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      | CIP F 20 PANEL, 4X10 SOLAR PANEL STRUCTR                         | EA                                                                                                                                                     | 4                         | 0                 | 0                  | 0                           | 3                           | 1                             | 4                           | 0                             |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |
| Remarks If Any:-                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                                                                  |                                                                                                                                                        |                           |                   |                    |                             |                             |                               |                             |                               |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |
| >Material Net issuance verified by Material Coordinator(Column NO- "D" TO "G".)<br>>Site ID, Inv No + Previous and current bill quantities booking verify by MPCM/PMO                                                                                                                                                                                                                                                                                                                                           |                                                                  |                                                                                                                                                        |                           |                   |                    |                             |                             |                               |                             |                               |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |
| Verified & Signed By:-                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |                                                                  |                                                                                                                                                        |                           |                   |                    |                             |                             |                               |                             |                               |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |
| <table border="1"> <tr> <td>           MPCM :- <i>Anil</i> SIX<br/> <b>ANIL SHAH</b><br/>           MPCM-VADODARA-2<br/>           Mob. No. 9374710314         </td> <td>           Material Coordinator:-<br/><br/>           Hardik suthar<br/>           Date : 10-05-2022         </td> <td>           Contractor :-<br/><br/> <b>For, EXCEL ELECTRICALS</b><br/> <br/>           AUTH. SIGN.         </td> </tr> </table> |                                                                  |                                                                                                                                                        |                           |                   |                    |                             |                             |                               |                             |                               |  | MPCM :- <i>Anil</i> SIX<br><b>ANIL SHAH</b><br>MPCM-VADODARA-2<br>Mob. No. 9374710314 | Material Coordinator:-<br><br>Hardik suthar<br>Date : 10-05-2022 | Contractor :-<br><br><b>For, EXCEL ELECTRICALS</b><br><br>AUTH. SIGN. |              |               |           |
| MPCM :- <i>Anil</i> SIX<br><b>ANIL SHAH</b><br>MPCM-VADODARA-2<br>Mob. No. 9374710314                                                                                                                                                                                                                                                                                                                                                                                                                           | Material Coordinator:-<br><br>Hardik suthar<br>Date : 10-05-2022 | Contractor :-<br><br><b>For, EXCEL ELECTRICALS</b><br><br>AUTH. SIGN. |                           |                   |                    |                             |                             |                               |                             |                               |  |                                                                                       |                                                                  |                                                                                                                                                        |              |               |           |

For, EXCEL ELECTRICALS

 AUTH. SIGN.

| Site Wise Consumption                                                                                                                             |                                          |                                                                                                                            |                    |       |
|---------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------|----------------------------------------------------------------------------------------------------------------------------|--------------------|-------|
| Contractor Name : M/s. Excel Electricals<br>Circle Name : Gujarat North<br>Site Count in Contract :<br>Site Count Billed : 01                     |                                          |                                                                                                                            |                    |       |
| WO No. : 630180228<br>Invoice No. : MAY/22-23/04<br>Invoice Date: 01-May-2022                                                                     |                                          |                                                                                                                            |                    |       |
| Material No                                                                                                                                       | Material Description                     | UOM                                                                                                                        | I-GJ-VASO-ENB-9001 | Total |
| 2002159304                                                                                                                                        | CIP F 20 PANEL, 4X10 SOLAR PANEL STRUCTR | EA                                                                                                                         | 1                  | 1     |
| Remarks If Any :-                                                                                                                                 |                                          |                                                                                                                            |                    |       |
| >Material Net issuance verified by Material Coordinator<br>>Site wise consumption QTY verify by MPCM/PMO.                                         |                                          |                                                                                                                            |                    |       |
| Verified & Signed By :-                                                                                                                           |                                          |                                                                                                                            |                    |       |
| MPCM:-                                                                                                                                            |                                          | Contractor :-                                                                                                              |                    |       |
| <br><b>ANIL SHAH</b><br>MPCM-VADODARA-2<br>Mob. No. 9374710314 |                                          | Hardik suthar<br>Date : 10-05-2022                                                                                         |                    |       |
|                                                                                                                                                   |                                          | For, EXCEL ELECTRICALS<br><br>AUTH. SIGN. |                    |       |

For, EXCEL ELECTRICALS  
  
 AUTH. SIGN.



Tel. : (0288) 2555750  
M. : 97129 09040, 93774 58805  
E-mail: excel19680@rediffmail.com  
excel19680@gmail.com

116, Siddhnath Complex,  
1st Floor, Near Indian Bank,  
K. V. Road, Jamnagar - 361 001

**GOVT. APPROVED CIVIL, EHV - HT - LT ELECTRICALS,  
TELECOM WORKS & LABOUR CONTRACTORS**

**To,**

**Reliance Projects and Property Management Services Limited  
5, TTS Industrial Area, Thane Belapur Road,  
Ghansoli, Navi Mumbai - 400701**


I/We/M/s. **EXCEL ELECTRICALS**. Hereby declare that we will not engage any child labour or Inter State Migrant Workmen on any day during the period of contract in the establishment of **M/s Reliance Digital Platform & Project Services Limited** for execution of the work awarded to us vide WO No. **P21/630180228**

We hereby indemnify M/s Reliance Corporate IT Park Limited against any legal hassles arising due to lapses on our part under **The Child Labour (Prohibition & Regulation) Act 1986 and Inter State Migrant Workmen (Regulation of Employment and Conditions of Services) Act, 1979.**

Thanking You,

**(Authorized Signatory)**

For, EXCEL ELECTRICALS

  
AUTH. SIGN.



GOVT. APPROVED CIVIL, EHV - HT - LT ELECTRICALS,  
TELECOM WORKS & LABOUR CONTRACTORS

TeL. : (0288) 2555750  
M. : 97129 09040, 93774 58805  
E-mail: excel19680@rediffmail.com  
excel19680@gmail.com

116, Siddhnath Complex,  
1st Floor, Near Indian Bank,  
K. V. Road, Jamnagar - 361 001

This is to inform and certify that **M/S. Excel Electricals** will not be deploying 20 or more contract workmen/labour on any day during the execution of the contract work in the allotted vide Work Order No. P21/630180228

However, in future, if ever the number of contract workmen to be deployed exceeds the stipulated statutory number of 20 or more workmen, the contractor will immediately apply and obtain labour license for the required capacity from the concerned Licensing Authority under CL(R&A) Act, 1970/Central Rules, 1971.

Thanking You,

For, EXCEL ELECTRICALS

  
AUTH. SIGN.

Serial No. 454/202

23-9-21



सत्यमेव जयते

INDIA NON JUDICIAL NOTARY

## Government of Gujarat

### Certificate of Stamp Duty

Certificate No. : IN-GJ26100522199170T  
Certificate Issued Date : 23-Sep-2021 05:36 PM  
Account Reference : IMPACC (AC)/ gj13336711/ GULBAI TEKRA/ GJ-AH  
Unique Doc. Reference : SUBIN-GJGJ1333671186961021756150T  
Purchased by : EXCEL ELECTRICAL  
Description of Document : Article 14 Bond  
Description : Not Applicable  
Consideration Price (Rs.) : 0  
(Zero)  
First Party : EXCEL ELECTRICAL  
Second Party : Not Applicable  
Stamp Duty Paid By : EXCEL ELECTRICAL  
Stamp Duty Amount(Rs.) : 500  
(Five Hundred only)



Abuzar

KC 0015322762

For, EXCEL ELECTRICALS

AUTH. SIGN.

P131

Last Updationon :25.11.16

### DECLARATION CUM INDEMNITY BOND


THIS DECLARATION CUM INDEMNITY BOND made at by M/s Excel Electrical their registered Office at **116, Siddhnath Complex, K.V. Road, Near Indian Bank, Jamnagar-361001** (hereinafter referred to as “**Contractor**” which expression shall unless it be repugnant to the context or meaning thereof, be deemed to mean and include their respective assigns, successors, executors and/or administrators) of the ONE PART in favor of the Company M/s. **Reliance Projects And Property Management Service Limited**

Registered under the Companies Act, 1956, and having its registered office at **Auda TP Scheme, Bodakdev No 1/A F P No.5 2<sup>nd</sup> Floor, Opp. Drive-in Cinema, Drive-in Road Ahemdabad-380054** (hereinafter referred to as the “**Company**”, which expression shall unless it be repugnant to the context or meaning thereof be deemed to mean and include its assigns, successors,) of the OTHER PART.

WHEREAS the Company has entered into a contract by issuing Work Order(s) to the Contractor for the

|               |               |               |               |
|---------------|---------------|---------------|---------------|
| P21/54023589  | P21/630132499 | P21/630144520 | P21/630144516 |
| P21/630150017 | P21/630150100 | P21/630149196 | P21/630149213 |
| P21/630147145 | P21/630143718 | P21/630143719 | P21/630152402 |
| P21/630152403 | P21/630150746 | P21/630155636 | P21/630155637 |
| P21/630155650 | P21/630155651 | P21/630157110 | P21/630157111 |
| P21/630159071 | P21/630159081 | P21/630160651 | P21/630160652 |
| P21/630161205 | P21/630162363 | P21/630163207 | P21/630163602 |
| P21/630163292 | P21/630163294 | P21/630163603 | P21/630163680 |
| P21/630163207 | P21/630162369 | P21/630164228 | P21/630164230 |
| P21/630164338 | P21/630164360 | P21/630165881 | P21/630165883 |
| P21/630166047 | P21/630166913 | P21/630168426 | P21/630168427 |
| P21/630170776 | P21/630169751 | P21/630169585 | P21/630169584 |
| P21/630170205 | P21/630170206 | P21/630170809 | P21/630170811 |
| P21/630171733 | P21/630173004 | P21/630173001 | P21/630172817 |
| P21/630174759 | P21/630174215 | P21/630174208 | P21/630173920 |
| P21/630177304 | P21/630177299 | P21/630177208 | P21/630177206 |
| P21/630176190 | P21/630174761 | P21/630174759 | P21/630177302 |
| P21/630177300 | P21/630179113 | P21/630179110 | P21/630178361 |
| P21/630186317 | P21/630186315 | P21/630184297 | P21/630180929 |
| P21/630180926 | P21/630180228 | P21/630195709 | P21/630195708 |
| P21/630195706 | P21/630195705 | P21/630195703 | P21/630194522 |
| P21/630191437 | P21/630191436 | P21/630188716 | P21/630188720 |
| P21/630187840 | P21/630186905 | P21/630186908 |               |
|               |               |               |               |

For, EXCEL ELECTRICALS

  
AUTH. SIGN.

(Hereinafter called the “**Contract**”)

P131

Last Updationon :25.11.16

(Hereinafter called the "**Contract**")

AND WHEREAS it is one of these essential conditions of the Contract that the Contractor shall comply with all the provisions of the Labor & Industrial Laws, as may be applicable from time to time for the discharge and completion of the Works and/or Services covered under said Contract by the Contractor including but not limited to the observance and compliance of The Contract Labor (R & A) Act 1970, Child Labor (Prohibition and Regulation) Act 1986, The Employees Provident Funds & Miscellaneous Provisions Act, 1952, Employees State Insurance Act 1948, Minimum Wages Act, 1948, Payment of Bonus Act, 1965, Payment of Wages Act, 1936, Employees Compensation Act.1923, and other Labor Laws applicable to the contractor (hereinafter referred as the '**Laws**').

AND WHEREAS the Contractor has agreed to execute this Declaration cum Indemnity Bond to this effect and has agreed to indemnify and keep the Company, its directors and employees and representatives indemnified and hold harmless against all third party claims, charges, penalties, fines, expenses, losses, damages, costs, suits or any other levy against the Company and/or the management due to the failure of the Contractor to observe or follow any Laws.

**NOW THIS DEED WITNESSETH AS UNDER:**

1. In consideration of the Company awarding the Contract/ Work Order to the Contractor subject to the condition of execution of this Declaration cum Indemnity bond, the Contractor declares and represents to the Company that the Contractor has obtained all statutory registrations, certificates, licenses and approvals required under the Laws enabling the Contractor to execute the Contract in a legal and lawful manner.
2. That in the event of any liability arising out of non-compliance of any such 'Laws' by the Contractor in connection with the execution of the Contract, the Contractor shall bear all the resultant whatsoever liability(IES), if any arising out thereof and that the Company, its directors, employees, representatives, shall not be liable for any such liability(IES). The Contractor agrees to indemnify and keep the Company and its directors, employees, representatives indemnified, defend and hold harmless, against all losses, costs, damages, claims, penalties, interest, expenses, demands, fines, legal liability, causes of action, injury to persons suites which may be suffered, incurred, undergone and / or sustained by the Company including the costs and expenses that may be incurred in defending any such liability(ies) claim(s), proceeding(s) etc. that may be made or taken or arise on the same by any person, body, authority, government, judicial / quasi-judicial authority due to the failure or noncompliance of any such laws and rules there under (including any amendments in acts, laws, statutes & rules there under) of whatsoever kind and nature arising out of or in any way connected with, whether or not such acts or omissions are actual or alleged, active or passive with regard to the discharge of the said Contract.
3. The Contractor hereby agrees and undertakes to make good any loss, damage, penalties, interests, claims, suits, demands, decrees, expenses that the Company may suffer to the fullest satisfaction of the Company and if the Contractor fails to make good the same then the Company shall have the right to recover the same and or any other loss sustained, without any restriction or limitation, together with any other incidental expenses, costs, and all incidental logistic expenses etc that may be suffered by the Company, from the Contractor.

For, EXCEL ELECTRICALS

AUTH. SIGN.

P131

Last Updationon :25.11.16

4. The Contractor hereby further confirms and declares that this Declaration cum Indemnity Bond is irrevocable and shall be final and binding on it / him heirs, executors, administrators, legal representatives, successors and assigns, wherever the context applies. Any claims, demands, shall be adjusted against any amount due and payable to the Contractor and the Company shall have the right to withhold any amounts due and payable to the Contractor, till the settlement of such claims, disputes to the satisfaction of the Company or alternatively make demand sufficient security from the Contractor towards discharge of such claims, obligations etc.
5. The Declaration cum Indemnity Bond shall be applicable for any and all Work Orders issued to the Contractor in this regard.
6. This Declaration cum indemnity bond shall be in accordance with the laws of India and any dispute between the parties with regard to this Declaration cum Indemnity Bond shall be resolved through the dispute resolution process mentioned in the General Conditions of the Contract (GCC).
7. Any terms used in this indemnity bond, but not expressly defined herein shall have the meaning assigned to it in the General terms and Conditions (GTC) forming part of the Work Orders issued.

IN WITNESS WHEREOF, the said Contractor has hereunto set their hand the day and year first hereinabove written.

**SIGNED SEALED AND DELIVERED**  
**By the within named "CONTRACTOR")**

**For, EXCEL ELECTRICALS**

*Chitwan*

**AUTH. SIGN.**

(Authorized Signatory)  
Rubber Stamp of Firm/Company  
Name:  
Designation:  
Date:

*Contractor*

**BEFORE ME**

*Signature*

**A. M. UJJAINI**  
NOTARY  
GOVT. OF INDIA

*23/9/21*

For, EXCEL ELECTRICALS

*Signature*  
AUTH. SIGN.



**RELIANCE PROJECTS & PROPERTY MANAGEMENT SERVICES LIMITED**

(FORMERLY RELIANCE DIGITAL PLATFORM &amp; PROJECT SERVICES LTD)

AUDA TP SCHEME, BODAKDEV NO: 1/A,, F P NO.: 5, 2ND FLOOR,

OPP. DRIVE IN CINEMA, DRIVE IN ROAD, AHMEDABAD-380054, GUJARAT, INDIA

Telephone : +91 79 -8879387831/40014190

Email: SUNILKUMAR.LIMBACHIA@RIL.COM

**WORK ORDER**

|                                                                                                                                                                                                                                                                                                                                       |                                                                                                                                                                                                                                                                                  |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>To</b><br><b>399452</b><br><b>EXCEL ELECTRICALS</b><br><b>116, SIDDHNATH COMPLEX,</b><br><b>K. V. ROAD, NR. INDIAN BANK</b><br><br><b>JAMNAGAR GUJARAT</b><br><b>Pin Code : 361001 INDIA</b><br><br><b>Phone : +91-288-2555750</b><br><b>Fax :</b><br><b>E-Mail : EXCEL19680@GMAIL.COM</b><br><b>Attention : PARESH LUNAGARIYA</b> | <b>Work Order No. : P21/630180228</b><br><br><b>Date : 12.02.2022</b><br><br><b>Contractor's</b><br><b>Quot. Ref :</b><br><b>Date :</b><br><b>Our Ref : 6011</b><br><br><b>GSTN Of Biller : 24AADFE1348L1ZJ</b><br><b>Bill From State : Gujarat</b><br><b>Bill From : 399452</b> |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|

This WORK ORDER, the SPECIAL CONDITIONS OF CONTRACT, the GENERAL CONDITIONS OF CONTRACT, the annexures enclosed to each of the foregoing, including any other document forming part of CONTRACT DOCUMENTS contain all the express terms and conditions of contract of supply of SERVICES ordered pursuant to this WORK ORDER and confirms and supersedes the LETTER OF COMMITMENT (if any) issued by COMPANY. CONTRACTOR agrees to supply the SERVICES, including all DELIVERABLES in full accordance with the foregoing terms and conditions. Capitalized terms used in this WORK ORDER but not defined in the WORK ORDER shall have the meaning ascribed to such terms in the foregoing SPECIAL CONDITIONS OF CONTRACT and GENERAL CONDITIONS OF CONTRACT. CONTRACTOR shall sign and return this WORK ORDER acknowledging the acceptance of this WORK ORDER within three (3) days of receipt at the communication address mentioned in this WORK ORDER. If acknowledgement is not received within three (3) days, this WORK ORDER will be deemed accepted by the CONTRACTOR. No other form of acceptance shall be binding on the PARTIES. For all future correspondence please quote this WORK ORDER NUMBER.

|                                                      |               |     |            |
|------------------------------------------------------|---------------|-----|------------|
| WO Period From DT : 12.02.2022<br>To DT : 30.04.2022 | Value of Work | INR | 315,590.00 |
|                                                      | CGST          | INR | 28,403.10  |
|                                                      | SGST          | INR | 28,403.10  |
|                                                      |               |     |            |

**TOTAL ORDER VALUE INR 372,396.20**

Value in Words : ( Rs. Three Lakh Seventy Two Thousand Three Hundred Ninety Six and Paise Twenty only )

For other details, please refer line items.

**Delivery Terms : N/A**  
**Engineer in Charge : Anil Shah**
**Payment Terms : See Page Inside**

|                       |                                                                                                                                                                                                                                                       |                                                                   |
|-----------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------|
| <b>BUYER : Pandey</b> | <b>for RELIANCE PROJECTS &amp; PROPERTY MANAGEMENT</b><br><b>SERVICES LIMITED</b><br><b>(FORMERLY RELIANCE DIGITAL PLATFORM &amp; PROJECT SERVICES LTD)</b><br><br><b>This is a computer generated document</b><br><b>not requiring any signature</b> | <b>CONTRACTOR'S Acceptance</b><br><br><b>Signature Title Date</b> |
|-----------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------|

REGISTERED OFFICE : Office-101, Saffron, Nr. Centre Point Panchwati 5 Rasta, Ambawadi Ahmedabad -380006

*Anil Shah*  
**ANIL SHAH**  
**MPCM-VADODARA-2**  
**Mob. No. 9374710314**

For, EXCEL ELECTRICALS  
*[Signature]*  
**AUTH. SIGN.**



## WORK ORDER

W.O Number P21 / 630180228 Dt.12.02.2022  
Page No: 1

WORK ORDER ISSUED FOR SOLAR PANEL INSTALLATION WORK\_ 3 SITES AT NORTH GUJARAT  
(Including Digital Conditions)

1. FIM - Applicable - Applicable
2. Indemnity Clause - Applicable
3. Performance Bank Guarantee (BG) - Applicable
4. Retention Clause - Applicable
5. DLP - 12 Months

| No | Item Code            | Material/Work Description         | Quantity | UOM | Price Details                 | Unit Rate        | Amount (INR)                      |
|----|----------------------|-----------------------------------|----------|-----|-------------------------------|------------------|-----------------------------------|
| 1  | I-GJ-VASO-ENB-9001_C | I-GJ-VASO-ENB-9001                | 1        | AU  |                               |                  |                                   |
|    |                      | Service Accounting Number: 995428 |          |     | Value of Work<br>CGST<br>SGST | INR/AU<br>%<br>% | 91,901.00<br>8,271.09<br>8,271.09 |

### The item covers the following Work :

10 3343857 CHRG CVL SOLAR 2M 20-25DT 28 WT 5SBC

1 EA - each

Net value of item 91,901.00

Charges for providing materials and services for execution of CIVIL works for solar work having 28 module at 2m height with 20-25 degree tilt and soil with water table and 5 SBC. The scope of work includes site preparation & restoration, excavation for footing, disposal of surplus earth, backfilling with selected earth, providing and fixing/ laying of steel reinforcement, shuttering, and concrete, transportation, fixing and alignment of stubs/ foundation bolts/ CIP, construction of support wall, grouting related work etc., and other site specific works as per requirement. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge #

|   |                      |                                   |   |    |                               |                  |                                   |
|---|----------------------|-----------------------------------|---|----|-------------------------------|------------------|-----------------------------------|
| 2 | I-GJ-MTAR-ENB-9023_C | I-GJ-MTAR-ENB-9023                | 1 | AU |                               |                  |                                   |
|   |                      | Service Accounting Number: 995428 |   |    | Value of Work<br>CGST<br>SGST | INR/AU<br>%<br>% | 91,901.00<br>8,271.09<br>8,271.09 |

### The item covers the following Work :

10 3343857 CHRG CVL SOLAR 2M 20-25DT 28 WT 5SBC

1 EA - each

Net value of item 91,901.00

Charges for providing materials and services for execution of CIVIL works for solar work having 28 module at 2m height with 20-25 degree tilt and soil with water table and 5 SBC. The scope of work includes site preparation & restoration, excavation for footing, disposal of surplus earth, backfilling with selected earth, providing and fixing/ laying of steel reinforcement, shuttering, and concrete, transportation, fixing and alignment of stubs/ foundation bolts/ CIP, construction of support wall, grouting related work etc., and other site specific works as per requirement. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge #

For, EXCEL ELECTRICALS

AUTH. SIGN.



## WORK ORDER

W.O Number P21 / 630180228 Dt.12.02.2022  
Page No: 4

|                     |     |            |
|---------------------|-----|------------|
| Total Value of Work | INR | 315,590.00 |
| Total CGST          | INR | 28,403.10  |
| Total SGST          | INR | 28,403.10  |

|                    |     |            |
|--------------------|-----|------------|
| Total Order Value: | INR | 372,396.20 |
|--------------------|-----|------------|

### Terms of payment :

Payment shall be made as per Detailed Payment Terms specified in the purchasing document.

### Vendor Bank Details:

Bank Account No. : 917030011070652  
Bank Name : AXIS BANK LTD  
City : JAMNAGAR

### Liquidated Damages :

0.5 % PER WEEK TO MAX OF 5%

### Engineer-In-charge :

Anil Shah  
Ankur Shah  
Arvind Pipaliya  
Chandrajeet Yadav  
Girish Modi  
Pavan Pandey  
Nayan Patel  
Saurabh Desai  
Rakesh Shah  
Kamal Patel  
Pitar Simon  
Ravi k verma  
Satish Padhiyar  
Kapil Gurubaxani  
Alex Rao  
Chirag Shah

### Document Submission Bank:

**Note(S): 1.** It is essential that the Contractor shall mention Item No. & Item code along with corresponding Material/Work Description and W.O.No. as mentioned above, in the Delivery challan (On-Shore Order), Measurement sheet and invoice for ease of material Inwarding, Certification of work and Bill Processing. Failure to do so may be the grounds for the rejections(s) or delay in release of payment(s).

PLANT REGISTRATION NO. : 24AAJCR6636BIZI

For, EXCEL ELECTRICALS

AUTH. SIGN.
