

**ELECTRICALS**GOVT. APPROVED CIVIL, EHV, HT, LT ELECTRICALS,
TELECOM WORKS & LABOUR CONTRACTORSTel : (0288) 2555750
M. : 97129 09010, 93774 58805
E mail : excel19680@gmail.com
excel19680@rediffmail.com116, Siddhnath Complex,
1st Floor, Near Indian Bank,
K. V. Road, Jamnagar - 361 001

Ref. No.

Date :

TAX INVOICE						
ORIGINAL FOR RECIPIENT						
Excel Electrical 116, Siddhnath Complex, 1st Floor, Near Indian Bank, K.V. Road, Jamnagar-361001				NA		
TO,				Invoice No	MAY/22-23/12	
Reliance Projects And Property Management Services Limited				Invoice Date	01-05-22	
First Floor 101, Saffron, Panchwati 5 Rasta, Nr Bank of Baroda, Ambawadi, Ahmedabad- Gujarat- 380006				Contract- WO No.	P21/630186905	
				Route Name	NA	
				Site ID	As Par Abstract	
				Site Name	As Par Abstract	
				Vendor Code	399452	
				Supplier's PAN No.	AADFE1348L	
				Supplier's GSTIN	24AADFE1348L1ZJ	
State - State Code as per GST : GUJARAT - 24				Period of Supply	01/04/2022 to 03/04/2022	
GSTIN / Unique ID : 24AAJCR6636B1ZJ				Nature of Supply	Civil Work	
PAN No. : AAJCR6636B				Place of supply of	GUJARAT	
Sr.	SAC : Code	Service Description	Qty (A)	UOM	Rate (Rs. / UoM) (B)	Amount (Rs.) (A*B*C)
1	995428	[3338609] CHRG CVL ODSC 20M LT SD NWT SSBC	1.00	EA	65,959.00	65,959.00
2	995428	[3342847] CHRG DIF RATE P/RCC ESC LATTICE TOWER	3.897	CUM	1,590.00	6,196.23
3	995428	[3342845] CHRG DIFF BOULDER SOLING ESC WORKS	0.67	CUM	920.00	616.40
4	995428	[3243408] DIFFERENTIAL PAYMENT FOR RATE INCREASE	353.21	EA	17.00	6,004.57
Total Supply Value of Milestone (Basic Value)						78,776.20
Less : Basic value of Advance Paid with Service Tax						
Balance Invoice Value (Net off Advance paid with Tax)						78,776.20
Central GST @ 9%						7,089.86
State GST @ 9%						7,089.86
Total GST Payable on Balance Invoice Value (Net off Advance paid with Service Tax)						14,179.72
Total Invoice Value with GST						92,955.92
Less - Advance paid without Service Tax						
Net Payable Amount						92,955.92
Round Off Net amount						92,956.00
Amount in Words :- Ninety Two Thousand Nine Hundred Fifty Six Rupees Only						
GST Amount in Words :- Fourteen Thousand One Hundred Seventy Nine Rupees Seventy Two Paise						
For:- Excel Electricals						
Authorised Signatory						
Declaration:						
a) Certified that all the particulars given above are true and correct.						



GOVT. APPROVED CIVIL, EHV - HT - LT ELECTRICALS,
TELECOM WORKS & LABOUR CONTRACTORS

Tel. : (0288) 2555750
M. : 97129 09040, 93774 58805
E-mail: excel19680@rediffmail.com
excel19680@gmail.com

116, Siddhnath Complex,
1st Floor, Near Indian Bank,
K. V. Road, Jamnagar - 361 001

NO CLAIM CERTIFICATE

WO/Contract Order and Frame Order no : P21/630186905

WO/Contract Order and Frame Order Date: 27/04/2022

Circle/State : North Gujarat

Site Name :-As Per Attached BOQ

Scope of Work :- LATTICE 20M CIVIL WORK

Invoice no :- MAY/22-23/12

Invoice Date :- 01-05-2022

We hereby confirm that we have carried out above scope of work in accordance with the, w.o/Contract order and Frame Order scope, terms and instruction of EIC and RS/- (92,956=00) (Ninety Two Thousand Nine Hundred Fifty Six Rupees Only) as our final claim. We confirm that there is no further claim by us in respect of the above invoice site & the mention scope of work. The invoice amount will be paid 95% and balance 5% kept as retention and will be paid after defect liability period as per WO/Contract Order and Frame Order terms.

For M/s EXCEL ELECTRICALS

For, EXCEL ELECTRICALS


AUTH. SIGN.

Authorized Signatory

BOQ CIVIL / SITE I.D. WISE ABSTRACT SHEET

1 Contractor Name:		EXCEL ELECTRICALS									
2 Invoice No.:		MAY/22-23/12									
3 Invoice Dt.:		01-May-22									
4 WO No.:		P21/630186905									
5 Service Period From Date:		01-Apr-22									
6 Service Period To Date:		03-Apr-22									

Sr.	Site ID	WBS ID	Technical Parameter				Quantity	Civil Service & Provide Mat	Civil Service & Provide Mat	CHRG DIF RATE P/RCC	CHRG DIFF BOULDER SOLING	DIFFERENTIAL PAYMENT FOR RATE INCREASE	Amount	Total Amount	
			Tower Type	NON KTD	Building Height	Tower Height									Wind Speed
1	I-GJ-SAQE-ESC-0002	I-GJ-SAQE-ESC-0002	LATTICE	YES	NA	20M	39	1	65,959.00	6,196.23	616.40	6,004.57	78,776.20		
Total Abstract Value													65,959.00	6,004.57	78,776.20
CONTRACTOR Name For, EXCEL ELECTRICALS Sign Stamp Date EIC Name ANIL SHAH Sign Stamp Date QSD Name Sign Stamp Date CPH Name Sign Stamp Date															

Quantity Certification Summary (QCS)

WO No: P21/630186905

WO Date :- 27/04/2022

Site ID Count:-AS PER BELOW MENTION

This is to certify that following Sites along with Technical Parameter pertaining to ODESC for above mentioned Work Order and of M/s. Excel Electricals being invoiced as per details attached, has been completed the following works.

A) CIVIL WORK :- LATTICE

Site ID	WBS ID	Technical Parameter				
		Tower Type	KIT/NKIT	Tower Height	Building Height	Wind Speed
I-GJ-SAQE-ESC-0002	I-GJ-SAQE-ESC-0002	LATTICE	NONKTD	20M	NA	39

Certified By:-

Engineer In-Charge (EIC):-

Circle Project Head (CPH):-

For, EXCEL ELECTRICALS

AUTH. SIGN.


ANIL SHAH
MPCM-VADODARA-2
Mob. No. 9374710314



Work Completion Certificate

State	Gujarat		Maintenance Point		
Project Type	93 K ☐	Infill ☐	Growth ☐	Other (Specify) _____	
Site Type	Own Built ☒	IP Colo ☐	RP1 ☐	BSNL ☐	MAG1 ☐
Tower type	GBT ☒	RTT ☐	RTP ☐	GBM ☐	NBT ☐
	Other (Specify) _____				

This is to certify that work has been completed as per specification given in workorder on the sites mentioned

The required ITP / Checklists are available and verified in system

Site I.D.

I-GJ-SAQE-ESC-0002

SAP ID

I-GJ-SAQE-ESC-0002

W.O.Number

P21/630186905

Vendor Name

M/S. EXCEL ELECTRICALS

No of Sites

1

Completion Date

3-Apr-22

Vendor Representative

Name

For, EXCEL ELECTRICALS

Sign


AUTH. SIGN.

Date

RJIL Representative

Name


ANIL SHAH

Sign

MPCM-VADODARA-2

Date

Mob. No. 9374710314

Remarks, if any:

Note :

In case of Multiple sites, please attach applicable site details with this certificate

EXCEL ELECTRICALS

ESC LATTICE Civil Quantity Measurement Sheet

Reliance SAP I-GJ-SAQE-ESC-0002

Vendor Name:-Excel Electricals

TOWER HEIGHT:- 20M LATTICE

Opco Name:- Reliance -4G

District:- Vadodara-2

Circle Name:- Vadodara-2- Gujarat

Wo No :- P21/630186905

NO	Item Code	Item	Description	Quantity	UOM	Quantity
10	3338609	CHRG CVL ODSC 20M LT 50 NWT 5SBC	Charges for providing materials and services for execution of CIVIL work for ODSC 20M LATTICE TOWER ; 50m/s WS ; NO WATER TABLE ; 5SBC ; RAFT FOUNDATION. The scope of work includes site preparation & restoration, excavation for footing, disposal of surplus earth, backfilling with selected earth, providing and fixing/ laying of steel reinforcement, shuttering, and concrete, transportation, fixing and alignment of stubs/ foundation bolts/ CIP, construction of support wall, grouting related work etc., and other site specific works as per requirement. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge.	1.00	EA	1.00
10	3342847	CHRG DIF RATE P/RCC ESC LATTICE TOWER	Charges to compensate the additional cost incurred by vendor for providing and laying of PCC/ RCC for lattice tower works for ESC/ SOLAR works.	3.897	CUM	3.897
10	3342845	CHRG DIF BOULDER SOLING ESC WORKS	Charges to compensate the additional cost incurred by vendor BOULDER SOLING Works for ESC/ SOLAR works.	0.67	CUM	0.67
10	3243408	DIFFERENTIAL PAYMENT FOR RATE INCREASE	Differential Charges to be paid for the rate increase.	353.21	EA	353.21

Excel Engg	FE	AM/CDP
Name :- For, EXCEL ELECTRICALS	Name :- ANIL SHAIH	Name :-
Signature :-	Signature :- MO. No. 9662609867	Signature :- MPCM-VADODARA-2
Date :-	Date :- AUTH. SIGN.	Date :- Mob. No. 9374710314

EXCEL ELECTRICALS

ESC LATTICE Civil Quantity Abstract Sheet

Reliance SAP I-GJ-SAQE-ESC-0002			Vendor Name:-Exceal Electricals			
TOWER HEIGHT:- 20M LATTICE			Opco Name:- Reliance -4G			
District:- Vadodara-2			Wo No :- P21/630186905			
Circle Name:- Vadodara-2- Gujarat						
NO	Item Code	Item	Description	Quantity	UNIT RATE	Amount
10	3338609	CHRG CVL ODSC 20M LT 50 NWT 5SBC	Charges for providing materials and services for execution of CIVIL work for ODSC 20M LATTICE TOWER ; 50m/s WS ; NO WATER TABLE ; 5SBC ; RAFT FOUNDATION. The scope of work includes site preparation & restoration, excavation for footing, disposal of surplus earth, backfilling with selected earth, providing and fixing/ laying of steel reinforcement, shuttering, and concrete, transportation, fixing and alignment of stubs/ foundation bolts/ CIP, construction of support wall, grouting related work etc., and other site specific works as per requirement. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge.	1.00	65959.00	65,959.00
10	3342847	CHRG DIF RATE P/RCC ESC LATTICE TOWER	Charges to compensate the additional cost incurred by vendor for providing and laying of PCC/ RCC for lattice tower works for ESC/ SOLAR works.	3.897	1590.00	6,196.23
10	3342845	CHRG DIFF BOULDER SOLING ESC WORKS	Charges to compensate the additional cost incurred by vendor BOULDER SOLING Works for ESC/ SOLAR works.	0.67	920.00	616.40
10	3243408	DIFFERENTIAL PAYMENT FOR RATE INCREASE	Differential Charges to be paid for the rate increase.	353.21	17.00	6,004.57
						78776.20
Excel Engg			AM/CDP	CPH		
Name :- For, EXCEL ELECTRICALS			Name :-	Name :-		
Signature :-			Signature :-	Signature :-		
Date :-			Auth. SIGN.	Date :-		

Ag. Shah

ANIL SHAH

MPCM-VADODARA-2

Mob. No. 9374710314

[Signature]


AUTH. SIGN.

NOTE :





1. ALL DIMENSIONS ARE IN MM UNLESS OTHERWISE STATED.
2. LOCATION & LEVELS OF ODC FOUNDATION BASED ON THE RELATED ELECTRICAL EQUIPMENT LAYOUT DRAWING.
3. GRADE OF CONCRETE SHALL BE AS PER SITE EXPOSURE CONDITIONS AS IN IS:456-2000 BUT MINIMUM GRADE SHALL BE AS RCC-M20 & BUNDING-M10.
4. MATERIAL & CONSTRUCTION TO BE IN ACCORDANCE WITH CONCRETE SPECIFICATION SS-CS-03002.
5. GRADE OF REINFORCEMENT SHALL BE Fe415 AS PER IS:1786.
6. SOIL STRATA CORRESPONDS TO NET SBC OF 0/80MM APPROPRIATE COMPACTION TO BE CARRIED OUT BELOW FOOTING IN CASE OF LOW SBC/LOOSE SOIL.
7. SITE SPECIFIC DRAWING MAY BE PREPARED WITH ASSISTANCE OF CONSULTANT/SME FOR SPECIAL SITES & FLOOD PRONE AREAS.
8. FOUNDATION DESIGN DATA SBC NET 51/M² & WEIGHT OF ODC IS MAX 1100KGS.
9. IN CASE OF LOOSE SOIL SPECIAL CARE IS TO BE TAKEN FOR COMPACTION IN LAYERS OF 150mm TO 90% OF PROCTOR DENSITY.
10. ODC SHALL BE PLACED SYMMETRICALLY TO THE C OF FOUNDATION OR AS PER STANDARD GUIDELINES.
11. SOIL IS TO BE FILLED AND COMPACTED AROUND SLAB FOR WORKING.
12. FOR MFL & BASED FOUNDATION LVL. REFER DRAWING NO. 10070-CS3-XK-XXX-XXX-ENB-2006-044.
13. REFER RESPECTIVE DRAWINGS FOR ODC ARRANGEMENT.

MATERIAL QUANTITIES

S.NO	ITEM	1 BAY	2 BAY	3 BAY	4 BAY
1.	LENGTH M	1.2	2.8	4.0	2.0
2.	WIDTH M	1.05	1.05	1.05	0.1
3.	AREA SQ.M	1.26	1.80	2.84	4.2
4.	POC M ³	0.11	0.184	0.25	0.347
5.	M20 M ³	0.567	0.80	1.32	1.83
6.	STEEL KGS	28.21	36.15	55.55	76.36
7.	SOLING M ³	0.67	0.98	1.50	2.122



TYPICAL REINFORCEMENT DETAILS

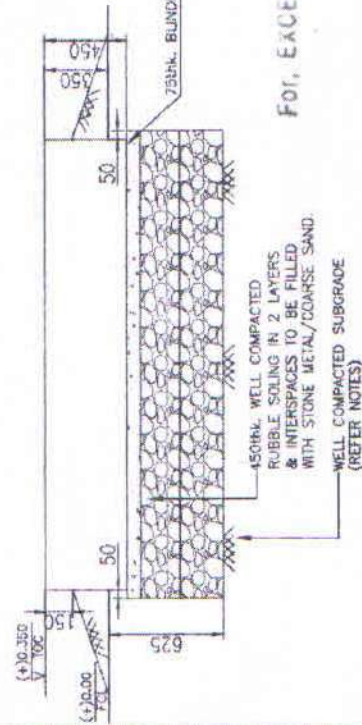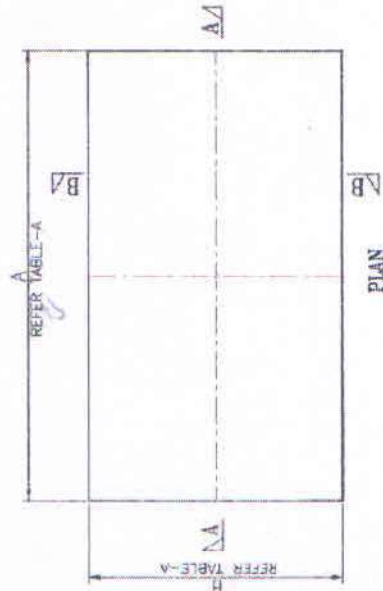

FOR, EXCEL ELECTRICALS

SECTION B-B

AUTH. SIGN.

SECTION A-A

For, EXCEL ELECTRICALS


AUTH. SIGN.

RELANCE JIC INFOCOMM LIMITED


BROADBAND WIRELESS ACCESS(BWA) SERVICES OUTSIDE PLANT(OSP) WORKS

CIVIL PLATFORM IN VIRGIN SOIL FOR ODC 2BAY & 3BAY

NTS:10070 10070-40-EP-CS3-PR-047 10

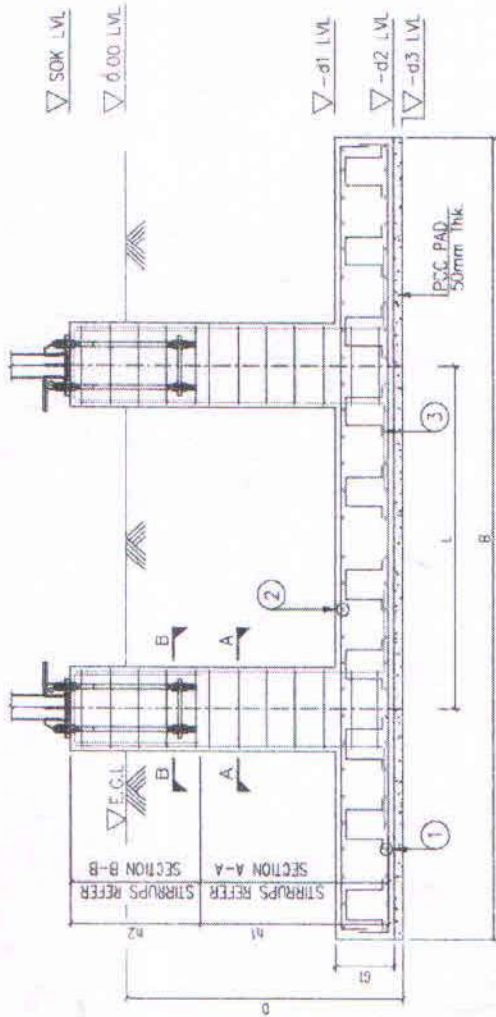

TOWER FOUNDATION

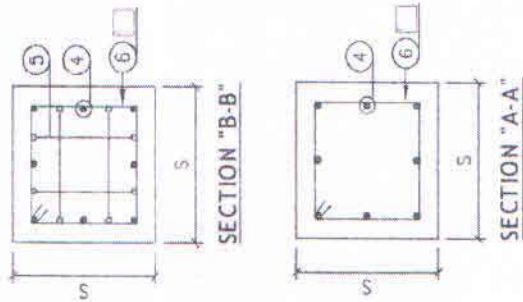

Dimensions	
B	2.750 m
L	0.800 m
L1	0.083 m
S	0.450 m
d1	1.200 m
d2	1.450 m
d3	1.500 m
G1	0.250 m
D	1.500 m
h1	1.076 m
h2	0.800 m
H1	0.950 m
H2	1.057 m
SOK W	0.500 m


Max. Foundation Forces:
 Compression = 233 kN
 Tension = 223 kN
 Shear = 4.4 kN

Soil:

Allowable Net soil bearing capacity = 5 T/m²
 Ground water level: Nil
 Depth of foundation: 1.5m
 Density of back filling material ≥ 1700 kN/m³
 Frustum angle ≥ 10 deg

For, EXCEL ELECTRICALS

AUTH. SIGN.

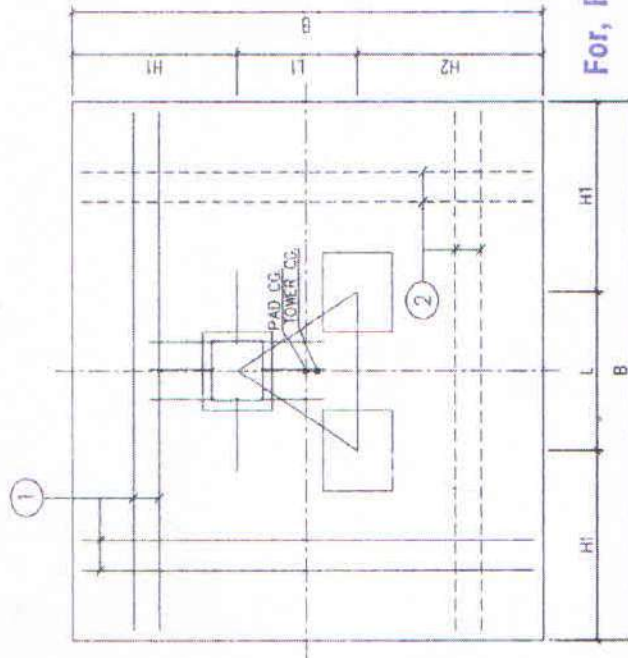

For, EXCEL ELECTRICALS

AUTH. SIGN.

IMPORTANT:

It is important that the cast-in part is placed in level and the cast-in part tube is filled with concrete up to the middle of the top hole as shown on drawings of cast-in parts.



Rev	Date	Prepared	Approved
0	21-08-2019	YPR	SSR
1	27-01-2020	YPR	SSR

Tower Type: 20m_DES-1 Mast

Square raft foundation Structural drawing

SBC : 5 T/m² No Water table

Wind Speed: 180 kmph

Dwg No: 19RIT-56_FD_20m_DES-1_MAST-SNWT

RELEASED FOR CONSTRUCTION

Sheet 1 of 3



Test Report on Compressive Strength of Concrete Cubes

8:\OM GEO TECH\20\TRF\9794\cc\cc Cube

Discipline/Group » Mechanical-Buildings Material
Sample ID No. » 01/20220418/CC Cube
Report Ref No » OGTS-2022-23/01/20220418/CC Cube

ULR-TC872622000001739F

Date of Report » 07-May-22

Customer » Reliance Jio
Name of Work » Site ID:- I-GJ-SAQE-ESC-0002
Agency » Excel Electricals, Jamnagar

Witness Person » Mr. Jayeshbhai Panchal
Date of Sample Received » 19-Apr-22
Material Received » Concrete Cubes
Method of Test » IS 516-1959 RA - 2018 Clause 5.0

Sr. No.	Sample ID	Date of Casting **	Date of Testing	Required Age of Test (days)	Grade of Concrete **	Length (mm)	Width (mm)	Height (mm)	Max.Load at Failure, (KN)	Weight of Spec. (Kg)	Comp. Strength, (N/mm ²)	Sample Density (Kg/m ³)
1	Cube 1	18-Apr-22	07-May-22	19	M 20	150.00	150.00	150.00	636.2	8.61	28.28	2550.8
2	Cube 2					150.00	150.00	150.00	506.8	8.52	22.52	2523.3
3	Cube 3					150.00	150.00	150.00	301.8	8.50	13.41	2518.2
Average											21.40	2530.8

» **Remark :-** The Average of Three Samples Values shall be taken as the Representative of the Batch provided the individual variation is not more than $\pm 15\%$ of the Average. Otherwise repeat tests shall be made as per IS 516-Clause-5.6

Requirements as per IS 456:2000-(Reaffirmed-2016)Table No.2 (Clause 6.1, 9.2.2, 15.1.1, and 36.1)

Grade of Concrete	M10	M15	M20	M25	M30	M35	M40	M45
Accepted Strength on 28 days of curing for Nominal Mix, N/mm ²	10	15	20	25	30	35	40	45

" M-10 is a Nominal Mix Concrete

•• End of Report ••

Note :-

1. The results are given only for the sample submitted by the Customer.
2. The test report shall not be reproduced except in full, without written approval of the laboratory.
3. Om Geo Tech Services is not responsible for any kind of interpretation of test results
4. The results/report is not used for publicity.
5. ** As informed by client



Doc ID: FMT-TST-01 / Page 1/1



Nadiad - Dabhan Road,
Nr. Bhutia Bunglow, Nr. MGVL Office,
NADIAD - 387 320



omgeotech18@gmail.com



94273 16024 , 99987 89919



Test Report on Compressive Strength of Concrete Cubes

E:\OM GEO TECH\2022\18/04/22\CC Cube

Discipline/Group » Mechanical-Buildings Material
Sample ID No. » 01/20220418/CC Cube
Report Ref No » OGTS-2022-23/01/20220418/CC Cube

ULR-TC872622000001938F

Date of Report » 20-May-22

Customer » Reliance Jio
Name of Work » Site ID:- I-GJ-SAQE-ESC-0002
Agency » Excel Electricals, Jamnagar

Witness Person » Mr. Abhijibhai
Date of Sample Received » 19-Apr-22
Material Received » Concrete Cubes
Method of Test » IS 516-1959 RA - 2018 Clause 5.0

Sr. No.	Sample ID	Date of Casting	Date of Testing	Required Age of Test (days)	Grade of Concrete **	Length (mm)	Width (mm)	Height (mm)	Max.Load at Failure, (KN)	Weight of Spec. (Kg)	Comp. Strength, (N/mm ²)	Sample Density (Kg/m ³)
1	Cube 1	18-Apr-22	20-May-22	32	M 20	150.00	150.00	150.00	641.4	8.53	28.51	2525.9
2	Cube 2					150.00	150.00	150.00	534.2	8.50	23.74	2519.7
3	Cube 3					150.00	150.00	150.00	778.1	8.49	34.58	2516.1
Average											28.94	2520.6

» **Remark :-** The Average of Three Samples Values shall be taken as the Representative of the Batch provided the individual variation is not more than $\pm 15\%$ of the Average. Otherwise repeat tests shall be made as per IS 516-Clause-5.6

Requirements as per IS 456:2000-(Reaffirmed-2016)Table No.2 (Clause 6.1, 9.2.2, 15.1.1, and 36.1)

Grade of Concrete	M10	M15	M20	M25	M30	M35	M40	M45
Accepted Strength on 28 days of curing for Nominal Mix, N/mm ²	10	15	20	25	30	35	40	45

** M-10 is a Nominal Mix Concrete

•• End of Report ••

Note :-

- The results are given only for the sample submitted by the Customer.
- The test report shall not be reproduced except in full, without written approval of the laboratory.
- Om Geo Tech Services is not responsible for any kind of interpretation of test results
- The results/report is not used for publicity.
- ** As informed by client



Doc ID : FMT-TST-01 / Page 1/1



Nadiad - Dabhan Road,
Nr. Bhutia Bunglow, Nr. MGVC Office,
NADIAD - 387 320



omgeotech18@gmail.com



94273 16024 , 99987 89919

Soil Investigation

Site Information	
Sap Id	I-GJ-SAQE-ESC-0002
Candidate Id	C2
Form No	R4G-70-CQM-FMT-PR-001
Site Name	Salun
Site Location	Block/Survey no. 204/1 , At. Salun, Ta. Nadiad, Dist. Kheda State Gujarat Indida,,
City	--
Latitude	22.729577
Longitude	72.918182
R4G State	Gujarat
Contractor	NA
Date	07 April 2022

For, EXCEL ELECTRICALS


AUTH. SIGN.

Inspection Report- Soil Investigation

Sr.No.	Description	Specifications	Observations	Remarks
Preliminary Checks				
1.1	Method of SI - Quadrant type(20mtr,69 city)		00	
1.2	Method of SI - SCPT(10 MTR),SPT (10MTR),Certification and Trial Pit Method for Isolated Raft/Open foundation		NA	
1.3	Method of SI - Advance SI in Multi pile and Micro pile		NA	
2	Availability of survey report for information of underground utility	Availability	Yes	
On Site Activities				
3	Trail Pit dimensions (As per SoW) wherever applicable	L*B*D/H	00	
4	Diameter of bore hole	100 mm/150 mm	100	
5	Depth of bore hole in soil	10 RMT/20 RMT	10	
6	Depth of bore hole in rock	As per drawing	00	
7	Sample collection as per specifications	No's	00	
Post Sampling Activity				
8	Back Filling bore hole/pit before removing barricades	Bore and Pit properly back-Filled	Yes	

9	Site cleanliness(Photographs of site " before and after soil sampling)		Yes		
10	Intimation to all stake holders of completion of work	Intimation sent to CML	Yes		
Observations and Comments: Water Table 00 Mtr SPT/SCPT N Value 00 at depth 00 Mtr Safe Bearing Capacity(SBC) of Soil 00 at depth 00 Mtr Sulphate content(%) 00 Chloride content(%) 00 Of soil					

CFQ details			
	Contractor's representative	Field Engineer	QC Engineer
Signature			
Name	bhaveshbhai	abhijit	
Date	07 April 2022	07 April 2022	--

Agreement
ANIL SHAH
MPCM-VADODARA-2
Mob. No. 98787814

For, EXCEL ELECTRICALS

AUTH. SIGN.

ODC Foundation

Site Information	
Sap Id	I-GJ-SAQE-ESC-0002
Candidate Id	C2
Form No	R4G-70-CQM-FMT-PR-040
Site Name	Salun
Site Location	Block/Survey no. 204/1 , At. Salun, Ta. Nadiad, Dist. Kheda State Gujarat Indida,,
City	
Latitude	22.729577
Longitude	72.918182
R4G State	Gujarat
Contractor	NA
Date	29 April 2022

Inspection Report- ODC Foundation

Sr.No.	Description	Specifications	Observations	Remarks
Preliminary Checks				
1.1	Site Name		Salun	
1.2	Site ID		I-GJ-SAQE-ESC-0002	
1.3	IFC Drawing No and Rev		10070-40-EP-C53-PR095-R00	
1.4	Availability of Drawing of ODC foundation	Site Specific	yes	
Materials				
2.1	Steel Re-bar	No rust/ no cracks	no rust and cracks	
2.2	Plain Cement Concrete below Raft	M 10	M10	
2.3.1	Grade of concrete for Raft	M 20	M20	
2.3.2	Grade of concrete for Pedstal	M 20	M20	
2.3.3	Grade of concrete for RCC Beam	M 20	NA	
2.3.4	Grade of concrete for RCC Slab	M 20	Na	
2.4.1	Cover blocks for Raft	mm	50	

For, EXCEL ELECTRICALS

 AUTH. SIGN.

2.4.2	Cover blocks for Column	mm	50	
2.4.3	Cover blocks for Beam	mm	0	
2.4.4	Cover blocks for Slab	mm	0	
Raft Foundation (Wherever applicable)				
3.1	Excavation for Foundation		1300*1050*625mm	
3.2	Plain Cement Concrete (PCC)		1300*1050*75mm	
3.3	Raft Size		1200*1050*450mm	
3.4.1	Reinforcement of Raft Spacing of bars	mm	200	
3.4.2	Reinforcement of Raft Diameter of bars	mm	10	
3.5.1	Check for Cover Foundation	mm	50	
3.5.2	Check for Cover Slab	mm	0	
3.5.3	Check for Cover Beam	mm,	0	
3.6	Check formwork and its supporting system	Check Support physically + Visually	ok	
3.7	Check for application of shuttering oil	Applied	yes applied	
3.8	Check for use of vibrator	Needle size 40/60/80, operational	40	

3.9	Ensure cubes taken for test		0	na
Column				
4.1	Reinforcement.	As Per drawing	10	y10 and y8
4.2.1	Check spacing of rings, stirrups, hooks and No's.of bars	Spacing of stirrups Y8 – 190 mm c/c	200	
4.2.2	Check spacing of rings, stirrups, hooks and No's.of bars	Diameter of bars in mm	8	
4.2.3	Check spacing of rings, stirrups, hooks and No's.of bars	No of bars	200	8nos and 200mm to cc
4.3	Check for size of Cover Block	mm	50	
4.4	Check formwork dimension and its supporting system	Dimensions as per drawing and Support physically + Visually	ok	
4.5	Check for application of shuttering oil	Applied	yes applied	
4.6	Check for use of vibrator	Needle size, Operational	40	
4.7	Ensure cubes taken for test		0	na
Beam				
5.1.1	Reinforcement Top Bars	mm	0	na
5.1.2	Reinforcement Bottom Bars	mm	0	na
5.1.3	Reinforcement Stirrups	mm c/c	0	na

5.2	Check for size of Cover Block	mm	0	na
5.3	Check formwork dimension and its supporting system	mm	0	na
5.4	Check for application of shuttering oil.	Oily Surface of shutter	na	
5.5	Check for use of vibrator	Needle size , Operational	0	na
5.6	Ensure cubes taken for test (Wherever applicable)		0	na

SLAB

6.1	Thickness of slab	mm	0	na
6.2	Reinforcement	MM , C/C	na	
6.3	Check for size of Cover Block	mm	0	na
6.4	Check formwork dimension and its supporting system	Dimensions as per drawing and Support physically + Visually	0	na
6.5	Check for application of shuttering oil	Applied	NA	
6.6	Check for use of vibrator	Needle size, Operational	0	na
6.7	Ensure cubes taken for test (Wherever applicable)		0	na



Post Casting


7.1	Visual check for cracks, bulging, honeycombing & exposed steel etc. in	No Damages	no damages	
-----	--	------------	------------	--

7.1	foundation	No Damages	no damages	
7.2	Check Curing/ Apply curing compound	7 days curing by water / Curing compound	7	by water
7.3	Ensure proper backfilling has been done	As Per Specification	ok	
7.4	28 Days Cube strength	100% and Above	NA	

Observations and Comments:

ok

CFQ details			
	Contractor's representative	Field Engineer	QC Engineer
Signature			
Name	BHAVESHBHAI	ABHIJIT	
Date	29 April 2022	29 April 2022	--


ANIL SHAH
 MPCM-VADODARA-2
 Mob. No. 9374710314

For, EXCEL ELECTRICALS

 AUTH. SIGN.

Foundation Bolt

Site Information	
Sap Id	I-GJ-SAQE-ESC-0002
Candidate Id	C2
Form No	R4G-70-CQM-FMT-PR-002
Site Name	Salun
Site Location	Block/Survey no. 204/1 , At. Salun, Ta. Nadiad, Dist. Kheda State Gujarat Indida,,
City	-
Latitude	22.729577
Longitude	72.918182
R4G State	Gujarat
Contractor	Excel Electrical
Date	18 April 2022

Inspection Report- Foundation Bolt

Sr.No.	Description	Specifications	Observations	Remarks
Document and Process Check				
1.1	IFC Drawing No. and Rev		10070-118-63510659-B05-060-R01	10070-118-63510659-B05-060-R0110070-118-63510659-B02-036-R02
1.2	Vendor Name		Excel electrical	
1.3	Bolt Size		M16 BOLTS	
1.4	Quantity		18 nos	
1.5	Raw Material Used (As per specifications)		FIM	
1.6	Material Test Report (check material test report as per specification)		FIM	
Physical and Visual Inspection				
2.1	Type of Foundation Bolt	A / B / C / D	anchor bolts FIM	
2.2	Total Length of the foundation bolt	mm	725	
2.3	Diameter of foundation bolt	mm	16	
2.4	Threaded Length of the bolt	mm	100	

2.5	Nut Thickness	mm	16	
2.6	Any Rust or damage/crack on bolt	No Rust , Cracks or damage	No	no rust and cracks
2.7	Free movement of Nut and Lock Nut	Free movement	Yes	
2.8	Galvanization Thickness (Wherever Applicable)	microns	FIM	
2.9	Galvanization done on threaded portion	Visual Inspection	FIM	


Observations and Comments:

ok

For, EXCEL ELECTRICALS

AUTH. SIGN.

CFQ details			
	Contractor's representative	Field Engineer	QC Engineer
Signature			
Name	BHAVESH	Abhijit	
Date	18 April 2022	18 April 2022	--


ANIL SHAH
MPCM-VADODARA-2
Mob. No. 9374710314

For, EXCEL ELECTRICALS

AUTH. SIGN.



Unnamed Road, Gujarat 387360, India

	Decimal	DMS
Latitude	22.718728	22°43'7" N
Longitude	72.921879	72°55'18" E



26°C

79°F

2022-04-19(Tue) 08:01

Google
IMPCM-VADODARA-2
Mob. No. 9374710314

Jm. Patel
JEVIN PATEL
Mo. No. 9882609867
FE-Vadodara-2

For, EXCEL ELECTRICALS

[Signature]
AUTH. SIGN.

From: Hardik1.Suthar@ril.com

To: project.gujarat@excelelectricals.com

Date: 5/9/2022 11:05:16 PM

Subject: RE: [External]RE: Material Reconciliation _ Excel Electricals

Attachments: RICCO-630186908_MAY-14 Electrical.pdf
RICCO-630150746_MAY-08 Electrical.pdf
RICCO-630150746_MAY-09 Electrical.pdf
RICCO-630163294_MAY-15 Electrical.pdf
RICCO-630164230_MAY-13 Electrical.pdf
RICCO-630170811_MAY-01 Electrical.pdf
RICCO-630170811_MAY-06 Electrical.pdf
RICCO-630170811_MAY-07 Electrical.pdf
RICCO-630180228_MAY-04 Civil.pdf
RICCO-630180228_MAY-05 Civil.pdf
RICCO-630186905_MAY-12 Civil.pdf

QTY in your Ricco found ok As per issued qty.

Pls validate Ricco Site material consumption qty through MPCM/PMO/SITE engineer for billing.

Thanks & Regards

Hardik Suthar

7043055098

From: Bhavesh Sadhu <project.gujarat@excelelectricals.com>

Sent: 05 May 2022 12:11

To: Akash Gandhi <Akash.Gandhi@ril.com>; Subhash1 Khimaniya <Subhash1.Khimaniya@ril.com>

Cc: ilsh.soni@excelelectricals.com; Hardik1 Suthar <Hardik1.Suthar@ril.com>; Chirag M Shah <Chirag.M.Shah@ril.com>

Subject: [External]RE: Material Reconciliation _ Excel Electricals

Caution: The e-mail below is from an external source. Please do not open attachments or click links unless this email comes from a known sender and you know the content is safe.

Dear Sir,

Please find attached Reco. for below sites for validation.

Kindly check & validate for further approval.

SR NO	MP	SAP ID	PROJECT	Material Reconciliation			SITE RFE1 DATE
				Civil	Erection	Electrical	

For, EXCEL ELECTRICALS


AUTH. SIGN.

1	Ahmedabad-1	I-GJ-AMBD-ENB-0498	5G	No	No	Yes	30-Apr-22
2	Ahmedabad-1	I-GJ-AMBD-ENB-0041	5G	No	No	Yes	21-Apr-22
3	Ahmedabad-2	I-GJ-BVLA-ESC-0024	ESC	No	Yes	Yes	28-Feb-22
4	Vadodara-2	I-GJ-KLAL-ESC-0025	ESC	No	Yes	Yes	8-Apr-22
5	Ahmedabad-1	I-GJ-AMBD-ENB-0871	5G	No	No	Yes	30-Apr-22
6	Ahmedabad-1	I-GJ-AMBD-ENB-0725	5G	No	No	Yes	30-Apr-22
7	Ahmedabad-1	I-GJ-AMBD-ENB-1109	5G	No	No	Yes	29-Mar-22
8	Vadodara-2	I-GJ-MTAR-ENB-9023	SOLAR	Yes	No	No	
9	Vadodara-2	I-GJ-VASO-ENB-9001	SOLAR	Yes	No	No	
10	Vadodara-2	I-GJ-SAQE-ESC-0002	ESC	Yes	No	No	28-Apr-22

Regards,

Bhavesh Sadhu

Excel Electricals

9979130791

From: Bhavesh Sadhu <project.gujarat@excelelectricals.com>

Sent: Monday, May 02, 2022 9:07 PM

To: 'Akash.Gandhi@ril.com' <Akash.Gandhi@ril.com>; 'Subhash1.Khimaniya@ril.com' <Subhash1.Khimaniya@ril.com>

Cc: 'ilesh.soni@excelelectricals.com' <ilesh.soni@excelelectricals.com>; 'Hardik1.Suthar@ril.com'

<Hardik1.Suthar@ril.com>; 'Chirag.M.Shah@ril.com' <Chirag.M.Shah@ril.com>

Subject: Material Reconciliation _ Excel Electricals

Dear Sir,

Please find attached Reco. for below sites for validation.

Kindly check & validate for further approval.

SR NO	MP	SAP ID	PROJECT	Material Reconciliation			SITE RFE1 DATE
				Civil	Erection	Electrical	
1	Ahmedabad-1	I-GJ-AMBD-ENB-0498	5G	No	No	Yes	30-Apr-22
2	Ahmedabad-1	I-GJ-AMBD-ENB-0041	5G	No	No	Yes	21-Apr-22
3	Ahmedabad-2	I-GJ-BVLA-ESC-0024	ESC	No	Yes	Yes	28-Feb-22
4	Vadodara-2	I-GJ-KLAL-ESC-0025	ESC	No	Yes	Yes	8-Apr-22
5	Ahmedabad-1	I-GJ-AMBD-ENB-0871	5G	No	No	Yes	30-Apr-22
6	Ahmedabad-1	I-GJ-AMBD-ENB-0725	5G	No	No	Yes	30-Apr-22
7	Ahmedabad-1	I-GJ-AMBD-ENB-1109	5G	No	No	Yes	29-Mar-22
8	Vadodara-2	I-GJ-MTAR-ENB-9023	SOLAR	Yes	No	No	
9	Vadodara-2	I-GJ-VASO-ENB-9001	SOLAR	Yes	No	No	
10	Vadodara-2	I-GJ-SAQE-ESC-0002	ESC	Yes	No	No	28-Apr-22

Regards,

Bhavesh Sadhu

For, EXCEL ELECTRICALS


AUTH. SIGN.

Excel Electricals

9979130791

"Confidentiality Warning : This message and any attachments are intended only for the use of the intended recipient(s), are confidential and may be privileged. If you are not the intended recipient, you are hereby notified that any review, re-transmission, conversion to hard copy, copying, circulation or other use of this message and any attachments is strictly prohibited. If you are not the intended recipient, please notify the sender immediately by return email and delete this message and any attachments from your system.

Virus Warning: Although the company has taken reasonable precautions to ensure no viruses are present in this email. The company cannot accept responsibility for any loss or damage arising from the use of this email or attachment."

For, EXCEL ELECTRICALS


AUTH. SIGN.

Material Reconciliation Statement

Contractor Name : M/s. Excel Electricals
Circle Name : Gujarat North
Site ID & Name : I-GJ-SAQE-ESC-0002
Site Count Billed : 01

Contractor Name : Mysri Enterprises Pvt. Ltd.										
Circle Name : Gujarat North										
Site ID & Name : I-GJ-SAQE-ESC-0002										
Site Count Billed : 01										
A	B	C	D	E	F	G	H	I	J	K
Material No	Material Description	UOM	Material Received from WH	Received BTN (IN)	Transfer BTN (OUT)	Material Return To WH (MRN)	Consumed & Invoiced Earlier	Consumed & Invoiced Currently	Total Consumption Till Date	Balance with Contractor / WIP
2002148773	ANCHOR,BOLT,WELD TOWR-20M,ODSC+UBR,50M/S	ST	1	0	0	0	0	1	1	0
5000032437	STOPPER PLATE FOR 20M UBR MAST	EA	1	0	0	0	0	1	1	0

Remarks If Any:-

>Material Net issuance verified by Material Coordinator(Column NO- "D" TO "G".)
>Site ID, Inv No + Previous and current bill quantities booking verify by MPCM/PMO

Verified & Signed By:-

MPCM :-  ANIL SHAH MPCM-VADODARA-2 Mob. No. 9374710314		Material Coordinator:- Hardik suthar Date : 10-05-2022	Contractor :- For, EXCEL ELECTRICALS  AUTH. SIGN.
--	--	--	---

For, EXCEL ELECTRICALS

AUTH. SIGN.

Site Wise Consumption				
Contractor Name : M/s. Excel Electricals Circle Name : Gujarat North Site Count in Contract : Site Count Billed : 01				
WO No. : 630186905 Invoice No. : MAY/22-23/12 Invoice Date: 01-May-2022				
Material No	Material Description	UOM	I-GJ-SAQE-ESC-0002	Total
2002148773	ANCHOR,BOLT,WELD TOWR-20M,ODSC+UBR,50M/S	ST	1	1
5000032437	STOPPER PLATE FOR 20M UBR MAST	EA	1	1
Remarks If Any :-				
>Material Net issuance verified by Material Coordinator >Site wise consumption QTY verify by MPCM/PMO.				
Verified & Signed By :-				
MPCM:-  ANIL SHAH MPCM-VADODARA-2 Mob. No. 9374710314		Material Coordinator:- 		
		Contractor :- 		
		For, EXCEL ELECTRICALS  AUTH. SIGN.		

For, EXCEL ELECTRICALS

AUTH. SIGN.



GOVT. APPROVED CIVIL, EHV - HT - LT ELECTRICALS,
TELECOM WORKS & LABOUR CONTRACTORS

Tel. : (0288) 2555750
M. : 97129 09040, 93774 58805
E-mail: excel19680@rediffmail.com
excel19680@gmail.com

116, Siddhinath Complex,
1st Floor, Near Indian Bank,
K. V. Road, Jamnagar - 361 001

This is to inform and certify that **M/S. Excel Electricals** will not be deploying 20 or more contract workmen/labour on any day during the execution of the contract work in the allotted vide Work Order No. P21/630186905

However, in future, if ever the number of contract workmen to be deployed exceeds the stipulated statutory number of 20 or more workmen, the contractor will immediately apply and obtain labour license for the required capacity from the concerned Licensing Authority under CL(R&A) Act, 1970/Central Rules, 1971.

Thanking You,

For, EXCEL ELECTRICALS


AUTH. SIGN.



GOVT. APPROVED CIVIL, EHV - HT - LT ELECTRICALS,
TELECOM WORKS & LABOUR CONTRACTORS

Tel. : (0288) 2555750
M. : 97129 09040, 93774 58805
E-mail: excet19680@rediffmail.com
excel19680@gmail.com

116, Siddhnath Complex,
1st Floor, Near Indian Bank,
K. V. Road, Jamnagar - 361 001

To,

Reliance Projects and Property Management Services Limited
5, TTS Industrial Area, Thane Belapur Road,
Ghansoli, Navi Mumbai - 400701

I/We/M/s. **EXCEL ELECTRICALS**. Hereby declare that we will not engage any child labour or Inter State Migrant Workmen on any day during the period of contract in the establishment of **M/s Reliance Digital Platform & Project Services Limited** for execution of the work awarded to us vide WO No. **P21/630186905**

We hereby indemnify M/s Reliance Corporate IT Park Limited against any legal hassles arising due to lapses on our part under **The Child Labour (Prohibition & Regulation) Act 1986 and Inter State Migrant Workmen (Regulation of Employment and Conditions of Services) Act, 1979.**

Thanking You,

(Authorized Signatory)

For, EXCEL ELECTRICALS


AUTH. SIGN.

Serial No. 454/2021

INDIA NON JUDICIAL NOTARY


Government of Gujarat

Certificate of Stamp Duty



सत्यमेव जयते

Certificate No.	IN-GJ26100522199170T
Certificate Issued Date	23-Sep-2021 05:36 PM
Account Reference	IMPACC (AC)/ gj13336711/ GULBAI TEKRA/ GJ-AH
Unique Doc. Reference	SUBIN-GJGJ1333671186961021756150T
Purchased by	EXCEL ELECTRICAL
Description of Document	Article 14 Bond
Description	Not Applicable
Consideration Price (Rs.)	0 (Zero)
First Party	EXCEL ELECTRICAL
Second Party	Not Applicable
Stamp Duty Paid By	EXCEL ELECTRICAL
Stamp Duty Amount(Rs.)	500 (Five Hundred only)



Signature

0015322762

For, EXCEL ELECTRICALS
AUTH. SIGN.

P131

Last Updationon :25.11.16

DECLARATION CUM INDEMNITY BOND

THIS DECLARATION CUM INDEMNITY BOND made at by M/s Excel Electrical their registered Office at 116, Siddhnath Complex, K.V. Road, Near Indian Bank, Jamnagar-361001 (hereinafter referred to as "**Contractor**") which expression shall unless it be repugnant to the context or meaning thereof, be deemed to mean and include their respective assigns, successors, executors and/or administrators) of the ONE PART in favor of the Company M/s. Reliance Projects And Property Management Service Limited

Registered under the Companies Act, 1956, and having its registered office at Auda TP Scheme, Bodakdev No 1/A F P No.5 2nd Floor, Opp. Drive-in Cinema, Drive-in Road Ahemdabad-380054 (hereinafter referred to as the "**Company**", which expression shall unless it be repugnant to the context or meaning thereof be deemed to mean and include its assigns, successors,) of the OTHER PART.

WHEREAS the Company has entered into a contract by issuing Work Order(s) to the Contractor for the

P21/54023589	P21/630132499	P21/630144520	P21/630144516
P21/630150017	P21/630150100	P21/630149196	P21/630149213
P21/630147145	P21/630143718	P21/630143719	P21/630152402
P21/630152403	P21/630150746	P21/630155636	P21/630155637
P21/630155650	P21/630155651	P21/630157110	P21/630157111
P21/630159071	P21/630159081	P21/630160651	P21/630160652
P21/630161205	P21/630162363	P21/630163207	P21/630163602
P21/630163292	P21/630163294	P21/630163603	P21/630163680
P21/630163207	P21/630162369	P21/630164228	P21/630164230
P21/630164338	P21/630164360	P21/630165881	P21/630165883
P21/630166047	P21/630166913	P21/630168426	P21/630168427
P21/630170776	P21/630169751	P21/630169585	P21/630169584
P21/630170205	P21/630170206	P21/630170809	P21/630170811
P21/630171733	P21/630173004	P21/630173001	P21/630172817
P21/630174759	P21/630174215	P21/630174208	P21/630173920
P21/630177304	P21/630177299	P21/630177208	P21/630177206
P21/630176190	P21/630174761	P21/630174759	P21/630177302
P21/630177300	P21/630179113	P21/630179110	P21/630178361
P21/630186317	P21/630186315	P21/630184297	P21/630180929
P21/630180926	P21/630180228		

For, EXCEL ELECTRICALS
AUTH. SIGN.

(Hereinafter called the "**Contract**")

PI31

Last Updationon :25.11.16

(Hereinafter called the "Contract")


AND WHEREAS it is one of these essential conditions of the Contract that the Contractor shall comply with all the provisions of the Labor & Industrial Laws, as may be applicable from time to time for the discharge and completion of the Works and/or Services covered under said Contract by the Contractor including but not limited to the observance and compliance of The Contract Labor (R & A) Act 1970, Child Labor (Prohibition and Regulation) Act 1986, The Employees Provident Funds & Miscellaneous Provisions Act, 1952, Employees State Insurance Act 1948, Minimum Wages Act, 1948, Payment of Bonus Act, 1965, Payment of Wages Act, 1936, Employees Compensation Act, 1923, and other Labor Laws applicable to the contractor (hereinafter referred as the 'Laws').

AND WHEREAS the Contractor has agreed to execute this Declaration cum Indemnity Bond to this effect and has agreed to indemnify and keep the Company, its directors and employees and representatives indemnified and hold harmless against all third party claims, charges, penalties, fines, expenses, losses, damages, costs, suits or any other levy against the Company and/or the management due to the failure of the Contractor to observe or follow any Laws.

NOW THIS DEED WITNESSETH AS UNDER:

1. In consideration of the Company awarding the Contract/ Work Order to the Contractor subject to the condition of execution of this Declaration cum Indemnity bond, the Contractor declares and represents to the Company that the Contractor has obtained all statutory registrations, certificates, licenses and approvals required under the Laws enabling the Contractor to execute the Contract in a legal and lawful manner.
2. That in the event of any liability arising out of non-compliance of any such 'Laws' by the Contractor in connection with the execution of the Contract, the Contractor shall bear all the resultant whatsoever liability(IES), if any arising out thereof and that the Company, its directors, employees, representatives, shall not be liable for any such liability(IES). The Contractor agrees to indemnify and keep the Company and its directors, employees, representatives indemnified, defend and hold harmless, against all losses, costs, damages, claims, penalties, interest, expenses, demands, fines, legal liability, causes of action, injury to persons suites which may be suffered, incurred, undergone and / or sustained by the Company including the costs and expenses that may be incurred in defending any such liability(ies) claim(s), proceeding(s) etc. that may be made or taken or arise on the same by any person, body, authority, government, judicial / quasi-judicial authority due to the failure or noncompliance of any such laws and rules there under (including any amendments in acts, laws, statutes & rules there under) of whatsoever kind and nature arising out of or in any way connected with, whether or not such acts or omissions are actual or alleged, active or passive with regard to the discharge of the said Contract.
3. The Contractor hereby agrees and undertakes to make good any loss, damage, penalties, interests, claims, suits, demands, decrees, expenses that the Company may suffer to the fullest satisfaction of the Company and if the Contractor fails to make good the same then the Company shall have the right to recover the same and or any other loss sustained, without any restriction or limitation, together with any other incidental expenses, costs, and all incidental logistic expenses etc. that may be suffered by the Company, from the Contractor.

For, EXCEL ELECTRICALS


AUTH. SIGN.

P131

Last Updationon :25.11.16

4. The Contractor hereby further confirms and declares that this Declaration cum Indemnity Bond, is irrevocable and shall be final and binding on it / him heirs, executors, administrators, legal representatives, successors and assigns, wherever the context applies. Any claims, demands, shall be adjusted against any amount due and payable to the Contractor and the Company shall have the right to withhold any amounts due and payable to the Contractor, till the settlement of such claims, disputes to the satisfaction of the Company or alternatively make demand sufficient security from the Contractor towards discharge of such claims, obligations etc.
5. The Declaration cum Indemnity Bond shall be applicable for any and all Work Orders issued to the Contractor in this regard.
6. This Declaration cum indemnity bond shall be in accordance with the laws of India and any dispute between the parties with regard to this Declaration cum Indemnity Bond shall be resolved through the dispute resolution process mentioned in the General Conditions of the Contract (GCC).
7. Any terms used in this indemnity bond, but not expressly defined herein shall have the meaning assigned to it in the General terms and Conditions (GTC) forming part of the Work Orders issued.


IN WITNESS WHEREOF, the said Contractor has hereunto set their hand the day and year first hereinabove written.

SIGNED SEALED AND DELIVERED
By the within named "CONTRACTOR")

For, EXCEL ELECTRICALS

[Signature]
AUTH. SIGN.
(Authorized Signatory)
Rubber Stamp of Firm/Company
Name:
Designation:
Date:

[Signature]
BEFORE ME
[Signature]
A. M. UJJAINI
NOTARY
GOVT. OF INDIA
23/9/21



For, EXCEL ELECTRICALS
[Signature]
AUTH. SIGN.

RELIANCE PROJECTS & PROPERTY MANAGEMENT SERVICES LIMITED

(FORMERLY RELIANCE DIGITAL PLATFORM & PROJECT SERVICES LTD)

AUDA TP SCHEME, BODAKDEV NO: 1/A,, F P NO.: 5, 2ND FLOOR,

OPP. DRIVE IN CINEMA, DRIVE IN ROAD, AHMEDABAD-380054, GUJARAT,

INDIA

Telephone : +91 79 -8879387831/40014190

**WORK CHANGE ORDER**

399452	Work Order No. : P21/630186905
EXCEL ELECTRICALS	Revision No. : 0001
116, SIDDHNATH COMPLEX,	Date : 27.04.2022
K. V. ROAD, NR. INDIAN BANK	
JAMNAGAR GUJARAT	GSTN Of Biller : 24AADFE1348L1ZJ
Pin Code: 361001	Bill From State : Gujarat
	Bill From : 399452

Attention : PARESH LUNAGARIYA
Tel.No. : +91-288-2555750
Fax.No. :
E-Mail : EXCEL19680@GMAIL.COM

WORK CHANGE ORDER - DO NOT DUPLICATE

This WORK CHANGE ORDER is issued to incorporate the following change(s) to the above noted Work Order:

Amendment to the Total Price as a result of this Revision	INR	0.00
Original/Previous Total Work Order Price :	INR	92955.92
Revised Total Work Order Price :	INR	92955.92
Revised Value in Words : Rs. Ninety Two Thousand Nine Hundred Fifty Five and Paise Ninety Two only		

ALL OTHER REQUIREMENTS, TERMS AND CONDITIONS SHALL REMAIN SAME AS PER THE ORIGINAL WORK ORDER AND ANY PREVIOUS CHANGE ORDER REVISION(S).

It is important that Contractor signs and returns the Work Change Order Copy within three (3) days of receipt. No other form of Order acceptance will be accepted. Failure to return the copy does not diminish responsibilities as set forth here in but may result in a delay to any payments that may be due.

FOR RELIANCE PROJECTS & PROPERTY MANAGEMENT SERVICES LIMITED

(FORMERLY RELIANCE DIGITAL PLATFORM & PROJECT SERVICES LTD)

BUYER : Pandey

Authorised Signatory

Contractor's Acceptance :

Engineer Incharge : Anil Shah

Validity From :30.03.2022 TO 31.05.2022

Contractor's Acceptance :

REGISTERED OFFICE : Office-101,Saffron, Nr.Centre Point Panchwati 5 Rasta,AmbawadiAhmedabad -380006

Agshah

ANIL SHAH
MPCM-VADODARA-2
Mob. No. 9774710314

For, EXCEL ELECTRICALS
[Signature]
AUTH. SIGN.



WORK CHANGE ORDER

W.O Number P21/630186905
Revision No : 0001 Dt. 27.04.2022
Page No: 1

WORK ORDER ISSUED FOR ODSC LATTICE ESC WORKS CIVIL 1 SITES AT NORTH GUJARAT

(Including Digital Conditions)

1. FIM - Applicable - Applicable
2. Indemnity Clause - Applicable
3. Performance Bank Guarantee(BG)- Applicable
4. Retension Clause - Applicable
5. DLP - 12 Months

No	Item Code	Material/Work Description	Quantity	UOM	Price Details	Unit Rate	Amount (INR)
1	IGJ-SAQE-ESC-0002	LATTICE 20	1	AU			
					Value of Work CGST SGST	INR/AU % %	65,959.00 5,936.31 5,936.31
		Service Accounting Number:	995428				

The item covers the following Work :

10 3332609 CHRG CVL ODSC 20M LT 50 NWT 5SBC

Charges for providing materials and services for execution of CIVIL work for ODSC 20M LATTICE TOWER : 50m/s WS : NO WATER TABLE : 5SBC : RAFT FOUNDATION. The scope of work includes site preparation & restoration, excavation for footing, disposal of surplus earth, backfilling with selected earth, providing and fixing/ laying of steel reinforcement, shuttering, and concrete, transportation, fixing and alignment of stubs/ foundation bolts/ CIP, construction of support wall, grouting related work etc., and other site specific works as per requirement. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge.#

1 EA - each
Net value of item
65,959.00

2	IGJ-SAQE-ESC-0002	RCC M-20 LATTICE	1	AU			
					Value of Work CGST SGST	INR/AU % %	6,196.23 557.66 557.66
		Service Accounting Number:	995428				

The item covers the following Work :

10 3342847 CHRG DIF RATE P/RCC ESC LATTICE TOWER

Charges to compensate the additional cost incurred by vendor for providing and laying of PCC/RCC for lattice tower works for ESC/ SOLAR works #

3.897 M3 - Cubic meter
Net value of item
1,590.00

3	IGJ-SAQE-ESC-0002	BOULDER SOALING	1	AU			
					Value of Work CGST SGST	INR/AU % %	616.40 55.48 55.48
		Service Accounting Number:	995428				

For, EXCEL ELECTRICALS

AUTH SIGN



WORK CHANGE ORDER

W.O Number **P21/630186905**
Revision No : 0001 Dt. 27.04.2022
Page No: 2

No	Item Code	Material/Work Description	Quantity	UOM	Price Details	Unit Rate	Amount (INR)
The item covers the following Work :							
10	3342845	CHRG DIFF BOULDER SOLING ESC WORKS	0.670	M3	- Cubic meter	920.00	616.40
Charges to compensate the additional cost incurred by vendor BOULDER SOLING Works for ESC/ SOLAR works.#							
4	I-GJ-SAQE-ESC-0002	STEEL	1	AU			
Service Accounting Number: 985428					Value of Work CGST SGST	INR/AU % %	6,004.57 540.41 540.41

The item covers the following Work :

10	3243408	DIFFERENTIAL PAYMENT FOR RATE INCREASE	353.210	EA	- each	17.00	6,004.57
Differential Charges to be paid for the rate increase.							

For, EXCEL ELECTRICALS

AUTH. SIGN.



WORK CHANGE ORDER

W.O. Number **P21/630186905**
Revision No : 0001 Dt. 27.04.2022
Page No: 3

Total Value of Work
Total CGST
Total SGST

INR 78,776.20
INR 7,089.86
INR 7,089.86

Revised Total Work Order Price:
Original/Previous Total Work Order Price:
Amendment to the Total Price as a result of this Revision

INR 92,955.92
INR 92,955.92
INR 0.00

Terms of payment :

Payment shall be made as per Detailed Payment Terms specified in the purchasing document.

Vendor Bank Details:

Bank Account No. : 917030011070652
Bank Name : AXIS BANK LTD
City : JAMNAGAR

Liquidated Damages :

0.5 % PER WEEK TO MAX OF 5%

Engineer-In-charge :

Anil Shah
Ankur Shah
Arvind Pipaliya
Chandrajeet Yadav
Girish Modi
Pavan Pandey
Nayan Patel
Saurabh Desai
Rakesh Shah
Kamal Patel
Pitar Simon
Ravi k verma
Satish Padhiyar
Kapil Gurubaxani
Alex Rao
Chirag Shah

Document Submission Bank:

Note(S): 1. It is essential that the Contractor shall mention Item No. & Item code along with corresponding Material/Work Description and W.O.No. as mentioned above, in the Delivery challan (On-Shore Order), Measurement sheet and invoice for ease of material Inwarding, Certification of work and Bill Processing. Failure to do so may be the grounds for the rejection(s) or delay in release of payment(s).

PLANT REGISTRATION NO. : 24AAJCR6636B1Z1

For, EXCEL ELECTRICALS

AUTH. SIGN.
