

GOVT. APPROVED CIVIL, EHV - HT - LT ELECTRICALS.
TELECOM WORKS & LABOUR CONTRACTORS

Tel. : (0288) 2555750
M. : 97129 09040, 93774 58805
E-mail : excel19680@rediffmail.com
excel19680@gmail.com

116, Siddhnath Complex,
1st Floor, Near Indian Bank,
K. V. Road, Jamnagar-361001

TAX INVOICE						
ORIGINAL FOR RECIPIENT						
Excel Electrical 116, Siddhnath Complex, 1st Floor, Near Indian Bank, K.V. Road, Jamnagar-361001				NA		
TO,				Invoice No	DEC/22-23/37	
Reliance Projects And Property Management Services Limited				Invoice Date	7-Dec-22	
First Floor 101, Saffron, Panchwati 5 Rasta, Nr Bank of Baroda, Ambawadi, Ahmedabad- Gujarat- 380006				Contract- WO No.	P21/630213338	
				Route Name	NA	
				Site ID	As Par Abstract	
				Site Name	As Par Abstract	
				Vendor Code	399452	
				Supplier's PAN No.	AADFE1348L	
				Supplier's GSTIN	24AADFE1348L1ZJ	
State - State Code as per GST : GUJARAT - 24				Period of Supply	02/11/2022 to 04/11/2022	
GSTIN / Unique ID : 24AAJCR6636B1ZJ				Nature of Supply	ESC RTP 6M CVL WORK	
PAN No. : AAJCR6636B				Place of supply of	GUJARAT	
Sr.	SAC : Code	Service Description	Qty (A)	UOM	Rate (Rs. / UoM) (B)	Amount (Rs.) (A*B*C)
1	995428	[3339785] CHRG CVL ODSC RT 6M STAY 2POLE 50	1.000	EA	15,625.00	15,625.00
2	995428	[3243408] DIFFERENTIAL PAYMENT FOR RATE INCREASE	41.910	EA	18.00	754.38
Total Supply Value of Milestone (Basic Value)						16,379.38
Less : Basic value of Advance Paid with Service Tax						
Balance Invoice Value (Net off Advance paid with Tax)						16,379.38
Central GST @ 9%						1,474.14
State GST @ 9%						1,474.14
Total GST Payable on Balance Invoice Value (Net off Advance paid with Service Tax)						2,948.29
Total Invoice Value with GST						19,327.67
Less - Advance paid without Service Tax						
Net Payable Amount						19,327.67
Round Off Net Amount						19,328.00
Amount in Words :- Nineteen Thousand Three Hundred Twenty Eight Rupees Only						
GST Amount in Words :- Two Thousand Nine Hundred Forty Eight Rupees & Twenty Nine Paise						
For:- Excel Electricals						
Authorised Signatory						
Declaration:						
a) Certified that all the particulars given above are true and correct.						



GOVT. APPROVED CIVIL, EHV - HT - LT ELECTRICALS.
TELECOM WORKS & LABOUR CONTRACTORS

Tel. : (0288) 2555750
M. : 97129 09040, 93774 58805
E-mail : excel19680@rediffmail.com
excel19680@gmail.com

116, Siddhnath Complex,
1st Floor, Near Indian Bank,
K. V. Road, Jamnagar-361001

NO CLAIM CERTIFICATE

WO/Contract Order and Frame Order no : P21/630213338

WO/Contract Order and Frame Order Date: 27/09/2022

Circle/State : North Gujarat

Site Name :-As Per Attached BOQ

Scope of Work :- ESC RTP 6M CIVIL WORK

Invoice no :- DEC/22-23/37

Invoice Date :- 07-12-2022

We hereby confirm that we have carried out above scope of work in accordance with the, w.o/Contract order and Frame Order scope, terms and instruction of EIC and RS/- (19,328=00) (Nineteen Thousand Three Hundred Twenty Eight Rupees Only) as our final claim. We confirm that there is no further claim by us in respect of the above invoice site & the mention scope of work. The invoice amount will be paid 95% and balance 5% kept as retention and will be paid after defect liability period as per WO/Contract Order and Frame Order terms.

For M/s EXCEL ELECTRICALS

For, EXCEL ELECTRICALS


AUTH. SIGN.

Authorized Signatory

BOQ CIVIL / SITE I.D. WISE ABSTRACT SHEET

EXCEL ELECTRICALS									
DEC/22-23/37									
7-Dec-22									
P21/630213338									
2-Nov-22									
4-Nov-22									

Sr.	Site ID	WBS ID	Tower Type	NON KTD	Building Height	Tower Height	Wind Speed	Quantity	CHRG CVL ODSC RT 6M STAY 2POLE 50	DIFFERENTIAL PAYMENT FOR RATE INCREASE	Amount	Total Amount
1	I-GJ-BLSN-ESC-0010	I-GJ-BLSN-ESC-0010	RTP	YES	G+3	6M	39 m/s	1	15,625.00	754.38	16,379.38	16,379.38
		Total Abstract Value							15,625.00	754.38	16,379.38	16,379.38

CONTRACTOR									
For, EXCEL ELECTRICALS									
Name	MPCM/PMO								
Sign	ANIL SHAH								
Stamp	MPCM-VADODARA-2								
Date	Mob. No. 9374710314								

(For And Gov on he are)

PMU - Vadodara - 2 mp

DILRAJ CHAVDA
MO. 9978573433
FE-VADODARA-2

Quantity Certification Summary (QCS)

WO No: P21/630213338

WO Date:- 27/09/2022

Site ID Count:-AS PER BELOW MENTION

This is to certify that following Sites along with Technical Parameter pertaining to **ODESC** for above mentioned Work Order and of **M/s. Excel Electricals** being invoiced as per details attached, has been completed the following works.

A) CIVIL WORK :- ESC RTP 6M CIVIL WORK

Site ID	WBS ID	Technical Parameter				
		Tower Type	KIT/NKIT	Tower Height	Building Height	Wind Speed
I-GJ-BLSN-ESC-0010	I-GJ-BLSN-ESC-0010	RTP	NONKTD	6M	G+3	39

Certified By:-

Engineer In-Charge (EIC):-

Circle Project Head (CPH):-

For, EXCEL ELECTRICALS

AUTH. SIGN.


DILRAJ CHAVDA
MO. 9978573433
FE-VADODARA-2


ANIL SHAH
MPCM-VADODARA-2
Mob. No. 9374710314

(Anil Sir on leave)
IMD - Vadodara-2



Work Completion Certificate

State Gujarat Maintenance Point Vadodara-2

Project Type ☐ 93 K ☐ Infill ☐ Growth ☒ Other (Specify) _____

Site Type ☐ Own Built ☐ IP Colo ☐ RP1 ☐ BSNL ☐ MAG1 ☐ NLD AG1

Tower type ☐ GBT ☐ RTT ☒ RTP ☐ GBM ☐ NBT ☐ Other (Specify) _____

This is to certify that work has been completed as per specification given in workorder on the sites mentioned

The required ITP / Checklists are available and verified in system

Site I.D. I-GJ-BLSN-ESC-0010

NEW SAP ID

I-GJ-BLSN-ESC-0010

W.O.Number P21/630213338

Vendor Name

M/S. EXCEL ELECTRICALS

No of Sites 1

Completion Date

4-Nov-22

Vendor Representative

Name

Sign

Date

For, EXCEL ELECTRICALS

AUTH. SIGN.

RJIL Representative

Name

Sign

Date

For Anil Sir
(Signature)
S.K.H.

ANIL SHAH
MPCM-VADODARA-2
Mob. No. 9374710314

(Anil Sir on leave)
PMO-Vadodara-2

Remarks, if any:

Note : In case of Multiple sites, please attach applicable site details with this certificate



ELECTRICALS

GOVT. APPROVED CIVIL, EHV, HT, LT ELECTRICALS,
TELECOM WORKS & LABOUR CONTRACTORS

Tel. : (0288) 2555750
M. : 97129 09040, 93774 58805
E-mail: excel19680@gmail.com
excel19680@rediffmail.com

116, Siddhnath Complex,
1st Floor, Near Indian Bank,
K. V. Road, Jamnagar - 361 001

Ref. No.

Date :

MATERIAL RECONCILIATION

Dear Sir,

This is to certify that we have not taken any material from the HFCL/RIL Warehouse for the completion civil work ODESC of site NAME-as below. SITE ID-as below against work order No: P21/630213338

[CIVIL WORK].

Site ID	Site Address
As Per Abstract	As Per Abstract

Name Of Contractor

Name Of Material Co-ordinator

Name of CPH

For, EXCEL ELECTRICALS


AUTH. SIGN.

Signature

Signature

Signature

Date

Date

Date

EXCEL ELECTRICALS

ESC RTP Civil Quantity Measurement Sheet

SAP ID : I-GJ-BLSN-ESC-0010		Vendor Name:-Excel Electricals				
TOWER HEIGHT:- RTP 6M		Opco Name:- Reliance -4G				
District:- Vadodara-2		Wo No :-P21/630213338				
Circle Name:- Gujarat North						
NO	Item Code	Item	Description	Quantity	UOM	Total
10	3339785	CHRG CVL ODSC RT 6M STAY 2POLE 50	Charges for providing materials and services for execution of CIVIL work for OUTDOOR SMALL CELL (ODSC) ROOF TOP WORKS 6M, WITH STAY; 2 Pole combination 50 m/s WIND SPEED. The scope of the work includes chipping / removal of water proofing/PCC, fixing of reinforcement dowels using chemical grouts; supply & installation of galvanized foundation bolts; construction of pedestals, and beams, cube test; supply and placement of non-shrink grout below base plate; shifting of materials to roof top and other misc. works. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge. #	1.00	EA	1.00
20	3243408	DIFFERENTIAL PAYMENT FOR RATE INCREASE	Differential Charges to be paid for the rate increase.	41.910	EA	41.910
EXCEL ELECTRICAL		FIELD ENGINEER		MPCM/PMO		
Name :-		Name :-		Name :-		
Signature :-		Signature :-		Signature :-		
Date :-		Date :-		Date :-		

For, EXCEL ELECTRICALS

Signature :-

Date :-

AUTH. SIGN.

MO. 9978573433

FE-VADODARA-2

DILRAJ CHAVDA

MO. 9978573433

FE-VADODARA-2

Name :-

Signature :-

Date :-

ANIL SHAH

MPCM-VADODARA-2

Mob. No. 9874710314

(Anil Sir on leave)

PMO-Vadodara-2MP

EXCEL ELECTRICALS

ESC RTP Civil Quantity Abstract Sheet

SAP ID : I-GJ-BLSN-ESC-0010		Vendor Name:- Excel Electricals				
TOWER HEIGHT:- RTP 6M		Opco Name:- Reliance -4G				
District:- Vadodara-2		Wo No :- P21/630213338				
Circle Name:- Gujarat North						
NO	Item Code	Item	Description	Quantity	Rate	Total
10	3339785	CHRG CVL ODSC RT 6M STAY 2POLE 50	Charges for providing materials and services for execution of CIVIL work for OUTDOOR SMALL CELL (ODSC) ROOF TOP WORKS 6M, WITH STAY; 2 Pole combination 50 m/s WIND SPEED. The scope of the work includes chipping / removal of water proofing/PCC, fixing of reinforcement dowels using chemical grouts; supply & installation of galvanized foundation bolts; construction of pedestals, and beams, cube test; supply and placement of non-shrink grout below base plate; shifting of materials to roof top and other misc. works. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge. #	1.00	15625.00	15625.00
20	3243408	DIFFERENTIAL PAYMENT FOR RATE INCREASE	Differential Charges to be paid for the rate increase.	41.910	18.00	754.38
EXCEL ELECTRICAL		MPCM / PMO		CPH		
Name :-		Name :-				
Signature :-		Signature :-				
Date :-		Date :-				

For, EXCEL ELECTRICALS

Signature :-

Date :-

AUTH. SIGN.

ANIL SHAH

MPCM-VADODARA-2

Mob. No. 9374710314

(Anil Sir in beam)
PMO - Vadodara-2

DILRAJ CHAVDA
MO. 9978573433
FE-VADODARA-2

Document Review Sheet

PROJECT TITLE:

R4G

VENDOR NAME:

STRUCON CONSULTANCY SERVICES

DOCUMENT TITLE:

Structural stability Report-site ID: I-GJ-BLSN-ESC-0010

VENDOR DOCUMENT NO.

RIL-2467

VENDOR REVISION NO:

DOCUMENT REVIEW FEEDBACK

Permission to proceed does not constitute acceptance or approval of Design Detail, Calculations, Analysis, Test Methods or Materials developed OR selected by Vendor, and does NOT relieve Vendor from FULL compliance with Contractual Obligations

- ☐ 1 Work may proceed.
- ☐ 2 Review not required, Work may proceed.
- ☐ 3 Revise & Resubmit at Final stage
- ☐ 4 Revise & Resubmit. Work may proceed, subject to incorporation of changes

- ☐ 5 Revise and Resubmit. Work may not proceed.
- ☐ 6 For Information Only
- ☐ ASB - As Built
- ☐ SUP - Superseded
- ☐ CAN - Cancelled / Not required.

By: _____ Date: _____

Discipline: SST Details for RTT Site

Equipment No.
(if applicable)

NA

MR Number
(if applicable)

N A

Project No

10070

Cat. Code

S S R

Service Area

G J

City Code

B L S N

Area Code

0 0 1 0

Facility Type

E S C

Seq. No. of Facility

X X X X

Seq. No.


0 0 1

Rev No

R 0

For, EXCEL ELECTRICALS


AUTH. SIGN.

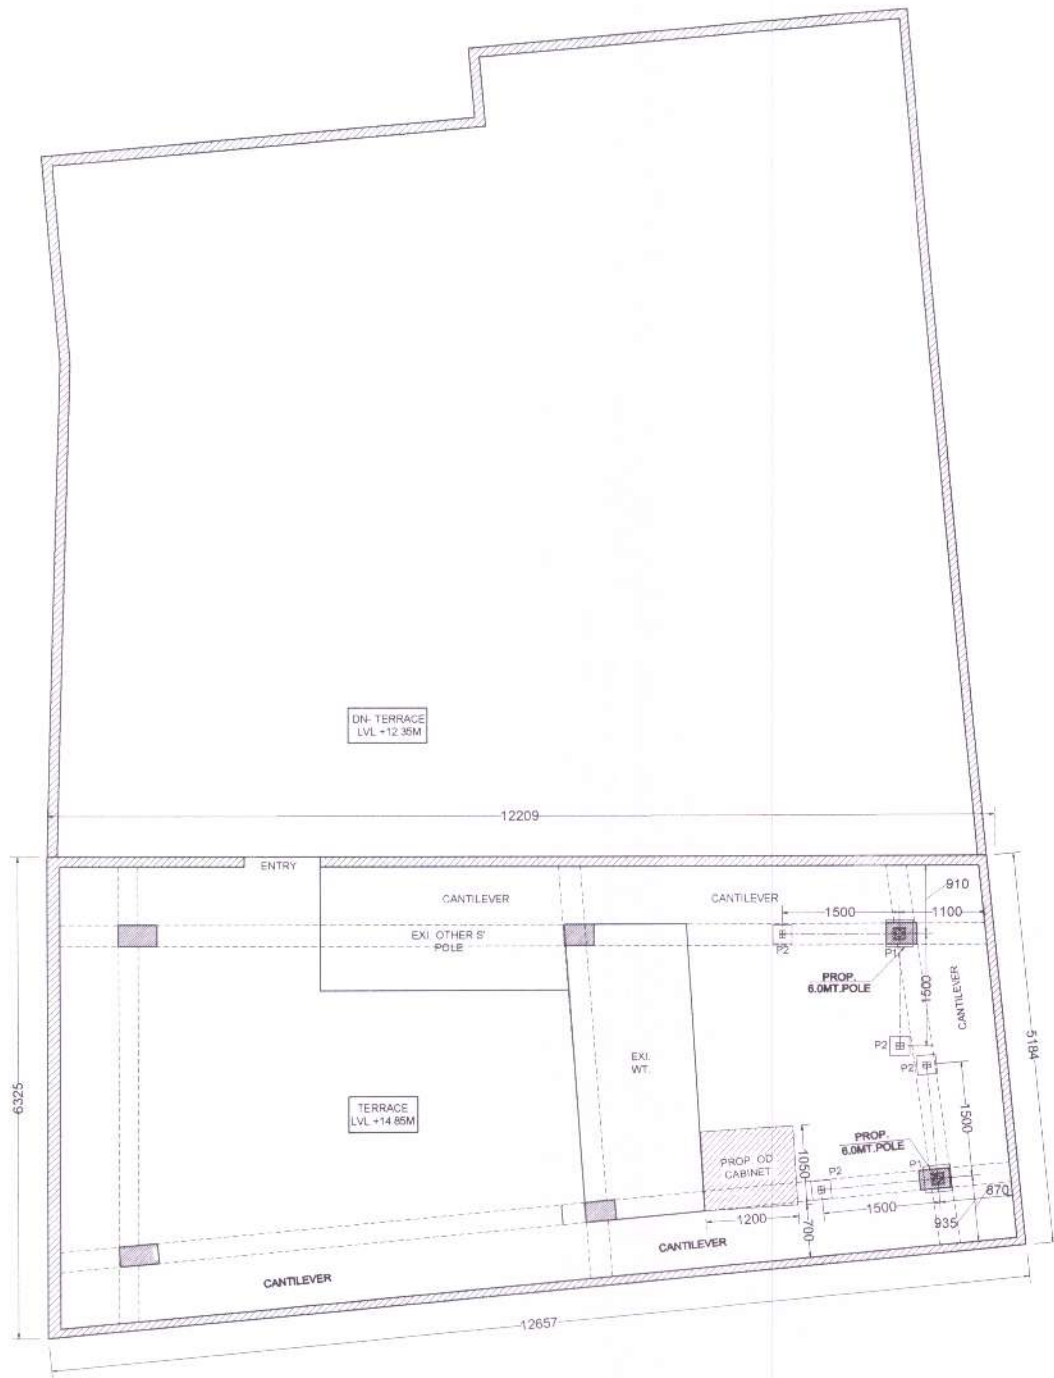


TERRACE LAYOUT PLAN FOR PROP. 6.0M R.T.P

		GENERAL NOTES 1. ALL DIMENSION ARE IN MM. UNLESS & OTHERWISE SPECIFIED 2. ALL DIMENSION SHALL BE VERIFY AT SITE WITH DRAWING BEFORE EXECUTION				BUILDING HT. :- 12.35MT. (G+3)	
						ROOM HT. :- 14.85MT. R.T.P. (G+4)	
						POLE HT. :- 6.00MT. R.T.P.	
						FINAL HT. :- 20.85MT.	
DESCRIPTION		REV NO	DATE	CLIENT NAME	RELIANCE	 STRUCON CONSULTANCY SERVICES CIVIL & STRUCTURAL CONSULTANT Corporate Office: 906, The Millennium, 150ft. Ring Road, Nana Mava Circle, Opp. Silver Height, Rajkot-360 005. Register Office: 206, Sorath Plaza, Bhakti Nagar Station Plot, Road-2, Rajkot-360002. mobile:-91 98796 16953 web site: www.strucon.co.in. Email id: strucon.rajkot@yahoo.com PRADIP KATHIRIYA (M.E.STR.), mobile +91 98796 16953	
TERRACE LAYOUT PLAN		0.00	22/09/22	DRAWING NO.	2467/2022		
TERRACE LAYOUT PLAN		R1	23/09/22	SITE NAME	Balasinor samaj		
				SITE ADDRESS :-			
				Open tarrece of Balasinor leva patidar seva samaj Milkat no 4463 Balasinor dist Kheda			
SCALE	DRAWN	CHK	SITE ID		Latitude: 23.015974, Longitude: 72.642199		
NTS	JIGNESH	PDK	1-GJ-BLSN-ESC-0010				


For, EXCEL ELECTRICALS

AUTH. SIGN.


NOTE: ALL DIMENSION SHALL BE VERIFY AT SITE WITH DRAWING BEFORE EXECUTION

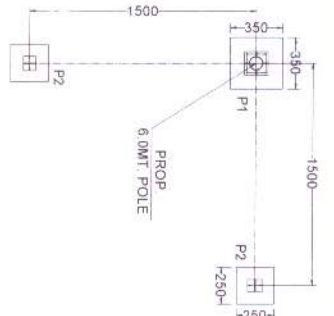


PROP R.T.P. 6.0M. POLE
(AS PER RIL DRG. NO. :- 10070-118-635/10659-B02-075)




BASE PLATE DETAILS FOR
3.0M. R.T.P. (TYP.) P1
(AS PER RIL DRG. NO. :- 10070-118-635/10659-B02-075)

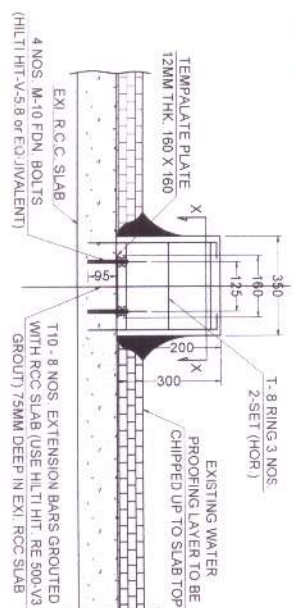


DETAILS OF PEDESTAL AT P1
(PEDESTAL HT. 300MM)
(PEDESTAL SHELL BE MADE AFTER POLE ERECTION)

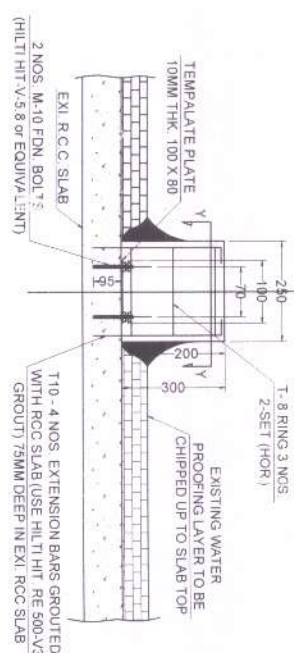


DETAILS OF PEDESTAL AT P2
(PEDESTAL HT. 300MM)
(PEDESTAL SHELL BE MADE AFTER POLE ERECTION)




TYPICAL SECTION AT "XX"
(PEDESTAL HT. 300MM)
(PEDESTAL SHELL BE MADE AFTER POLE ERECTION)




TYPICAL SECTION AT "YY"
(PEDESTAL HT. 300MM)
(PEDESTAL SHELL BE MADE AFTER POLE ERECTION)



WATER PROOFING DETAIL SECTION



DETAIL AT "A"

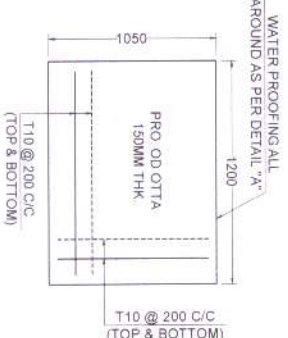

OD CABINET OTTA STR. DETAILS

GENERAL NOTES

1. ALL DIMENSIONS ARE IN MILLIMETERS, OTHERS ARE SPECIFIED.
2. ALL WORK SHALL BE DONE BY THE CONTRACTOR.
3. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
4. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
5. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
6. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
7. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
8. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
9. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
10. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
11. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
12. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
13. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
14. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.
15. ALL MATERIALS SHALL BE OF THE BEST QUALITY AND SHALL BE AS PER THE SPECIFICATION.

DESCRIPTION	REV. NO.	DATE
STRUCTURAL DETAILS FOR 6.0M RTP	0.00	26/09/22
SCALE	DRAWN	CHECKED
1:100	SANDIP	PDK

CLIENT NAME :-	RELANCE
DRAWING NO. 2467/2022	
SITE NAME	SITE ADDRESS :-
Balsinor samaj	Open tararee of Balsinor leva petidar seva samaj Milkat no 4463 Balsinor dist Kheda
	Latitude: 23.015974, Longitude: 72.642199

STRUCON CONSULTANCY SERVICES
CIVIL & STRUCTURAL CONSULTANT

Corporate Office: 906, The Millennium, 150ft. Ring Road,
Nana Maya Circle, Opp. Silver Height, Rajkot-360 005.
Register Office: 206, Sorath Plaza, Bhakti Nagar Station
Plot, Road-2, Rajkot-360002.
mobile: +91 98796 16953 web site: www.strucon.co.in
Email Id: strucon.rajkot@yahoo.com

PRADIP KATHIRIYA (M.E.STR.), mobile: +91 98796 16953

For, EXCEL ELECTRICALS
AUTH. SIGN.



STRUCON CONSULTANCY SERVICES




CIVIL & STRUCTURAL CONSULTANT

Corporate Office: 906, The Millennium, 150ft. Ring Road, Nana Mava Circle, Opp. Silver Height, Rajkot-360 005.

Register Office: 206, Sorath Plaza, Bhakti Nagar Station Plot, Road-2, Rajkot-360002.

mobile:+91 98796 16953, web site: www.strucon.co.in, Email Id: strucon.rajkot@yahoo.com

BAR BENDING SCHEDULE

MARK	DIA.	DESCRIPTION	LENGTH	NOS.	UNIT WT.	TOTAL WEIGHT (KG.)
GROUTING BAR Ped. P1	10		485	16	0.62	4.81
PEDESTAL STRRIUPS (HOR.) Ped. P1	8		1100	12	0.39	5.15
GROUTING BAR Ped. P2	10		485	16	0.62	4.81
PEDESTAL STRRIUPS (HOR.) Ped. P2	8		800	24	0.39	7.49
OD SLAB SHORT STEEL (TOP & BOTTOM)	10		1150	14	0.62	9.98
OD SLAB LONG STEEL (TOP & BOTTOM)	10		1300	12	0.62	9.67

TOTAL WEIGHT OF STEEL IN Kg

41.91

SITE ADDRESS:	SITE NAME:	SITE:	REV.NO.	DATE:
Open tarreche of Balasinor leva patidar seva samaj Milkat no 4463 Balasinor dist KhedA	Balasinor samaj	I-GJ-BLSN-ESC-0010	R0	26-Sep-22

For, EXCEL ELECTRICALS


AUTH. SIGN.



STRUCON CONSULTANCY SERVICES

CIVIL & STRUCTURAL CONSULTANT

Corporate Office: 906, The Millennium, 150ft. Ring Road, Nana Mava Circle, Opp. Silver Height, Rajkot-360 005.

Register Office: 206, Sorath Plaza, Bhakti Nagar Station Plot, Road-2, Rajkot-360002.

mobile:+91 98796 16953, web site: www.strucon.co.in, Email Id: strucon.rajkot@yahoo.com

Quantity Sheet

Sr. No.	Description	No.	Length	Width	Height	Total	Unit
1	PEDESTAL P1	2	0.350	0.350	0.300	0.074	cum
2	PEDESTAL P2	4	0.250	0.250	0.300	0.075	cum
3	OD otta SLAB	1	1.200	1.050	0.150	0.189	cum
Total=						0.338	cum
SITE ADDRESS:		SITE NAME:		SITE ID:		REV.NO.	DATE:
Open tarrece of Balasinor leva patidar seva samaj Milkat no 4463 Balasinor dist Kheda		Balasinor samaj		I-GJ-BLSN-ESC-0010		R0	26-Sep-22

For, EXCEL ELECTRICALS

AUTH. SIGN.



STRUCON CONSULTANCY SERVICES

CIVIL & STRUCTURAL CONSULTANT

Corporate Office: 905, The Millennium, 150M Ring Road, Nana Maya Circle, Opp. Silver Height, Rajkot-360 005.
Register Office: 206, Sorath Plaza, Bhadranagar Station Plot, Road No. 2, Rajkot - 360 032
☎ 0281 236 3347 ☎ +91 98796 16933 ☎ strucon@rajkot@yahoo.com ☎ www.strucon.co.in

REF: RIL/2467

DATE: 22/09/2022

STRUCTURAL STABILITY CERTIFICATE

PROJECT : Reliance Jio Infocom Ltd.,
SITE NAME : Balasinor samaj
SITE ID : I-GJ-BLSN-ESC-0010
SITE ADDRESS : Open tarrece of Balasinor leva patidar seva samaj Milkat no 4463
Balasinor dist Kheda
TOWER TYPE : 6.0m R.T.P.

Based on the detailed structural stability survey carried out by us, and on instructions by M/s. Reliance Jio Infocom Ltd., we here by certify that the existing load bearing structure of building will be capable of sustaining the additional load imposed by the **6.0m POLE** along with the loads of the equipments and their R.C.C. foundations indicated in the plan. The validity of this certificate is subjected to the execution and supervision carried out by M/s. Reliance Jio Infocom Ltd., at this site as per layout and structural design. As per the visual inspection and observations during the site visit, existing building does not show any signs of deterioration, no structural cracking and no foundation settlement hence we can say that the condition of building is good and stable to take the additional load.

STRUCON CONSULTANCY SERVICES

PRADIP KATHIRIYA (M.E.STRUCTURE)

For, EXCEL ELECTRICALS

AUTH. SIGN.



Pradip Kathiriya

Foundation Bolt

Site Information		
Sap Id	I-GJ-BLSN-ESC-0010	
Candidate Id	C1	
Form No	R4G-70-CQM-FMT-PR-002	
Site Name	Balasinor	
Site Location	Open tarreze of Balasinor leva patidar seva samaj Milkat no 4463 Balasinor dist Kheda,,	
City	--	
Latitude	22.956835	
Longitude	73.337164	
R4G State	Gujarat	
Contractor	Excel Electrical	
Date	04 November 2022	

ANIL SHAH
MPCM-VADODARA-2
Mob. No. 9374710314

(Anil Shah on Leave)
PMO- Vadodara-2

For, EXCEL ELECTRICALS


AUTH. SIGN.

Inspection Report- Foundation Bolt

Sr.No.	Description	Specifications	Observations	Remarks
Document and Process Check				
1.1	IFC Drawing No. and Rev		10070-SSR-GJ-BLSN-0010-ESC-XXXX-01	
1.2	Vendor Name		EXCEL ELECTRICAL	
1.3	Bolt Size		150	
1.4	Quantity		16	
1.5	Raw Material Used (As per specifications)		as per drawing	
1.6	Material Test Report (check material test report as per specification)		FIM USED	
Physical and Visual Inspection				
2.1	Type of Foundation Bolt	A / B / C / D	annechar	
2.2	Total Length of the foundation bolt	mm	150	
2.3	Diameter of foundation bolt	mm	10	
2.4	Threaded Length of the bolt	mm	150	
2.5	Nut Thickness	mm	19	

For, EXCEL ELECTRICALS


AUTH. SIGN.


2.6	Any Rust or damage/crack on bolt	No Rust , Cracks or damage	No		
2.7	Free movement of Nut and Lock Nut	Free movement	Yes		
2.8	Galvanization Thickness (Wherever Applicable)	microns	found ok		
2.9	Galvanization done on threaded portion	Visual Inspection	found ok		


Observations and Comments:

na

For, EXCEL ELECTRICALS


AUTH. SIGN.

CFQ details			
	Contractor's representative	Field Engineer	QC Engineer
Signature			
Name	jagdish	dilraj	
Date	04 November 2022	04 November 2022	--

for Anil Sir

 S. Khan

ANIL SHAH
 MPCM-VADODARA-2
 Mob. No. 9374710314

(Anil Sir on leave)
 PMO - Vadodara-2

For, EXCEL ELECTRICALS


 AUTH. SIGN.

RTP/RTT/Delta Foundation

Site Information	
Sap Id	I-GJ-BLSN-ESC-0010
Candidate Id	C1
Form No	R4G-70-CQM-FMT-PR-007
Site Name	Balasinor
Site Location	Open tarrece of Balasinor leva patidar seva samaj Milkat no 4463 Balasinor dist Kheda,,
City	--
Latitude	22.956835
Longitude	73.337164
R4G State	Gujarat
Contractor	Excel Electrical
Date	04 November 2022

ANIL SHAH
MPCM-VADODARA-2
Mob. No. 9374710314

(Anil Sir on leave)
PMO Vadodra-2

For, EXCEL ELECTRICALS

AUTH. SIGN.

Inspection Report- RTP/RTT/Delta Foundation

Sr.No.	Description	Specifications	Observations	Remarks
Preliminary Checks				
1.0	Drawing No and Rev		SSR-GJ-BLSN-0010-ESC-XXXX-001	
1.1	Availability of latest construction drawing (IFC) with revision as per tower height and wind speed	Availability	Available	
Materials				
2.1	Cement Grade		53	
2.2	Cement Brand		ultratect	
2.3	Cement Manufacturing Week		15-10-2022	
3	Grade of concrete	M 20	20	
4	Reinforcement steel	Fe 415 (Test Certificate)	Ok	
5	Anchor Bolt Length (in mm)		150	
6	Threaded portion of foundation bolt (in mm)		150	
7	Grouting Material	ISI Mark , Non Shrink Free Flow	Ok	
Pedestal				

For, EXCEL ELECTRICALS


AUTH. SIGN.

8	Layout Marking of Pedestal Foundation	L * B * D	350x350x300		
9	Check chipping of water proofing upto RCC Beam/Slab	Visual Inspection	Ok		
10.1	Hacking the RCC top slab	Visual Inspection	ok		
10.2	Apply concrete bonding agent	Nito bond,Equivalent ISI mark bond agent	ISI MARK BOND		
11.1	Check the spacing of rebars	Spacing	100		
11.2	Check the mark on slab	Dia of Bar	10		
12.1	Depth of Drilled Hole for rebars(Wherever Applicable)	As per Drawing	95		
12.2	Diameter of Drilled Hole for rebars(Wherever Applicable)	As per Drawing	10		
13	Grouting of rebars wherever applicable	As per Process / Specifications	Ok		
14	Check the rebars wherever applicable	As Per Drawing/ BBS	Ok		
15.1	Shuttering Dimension of Pedstal	Pedstal L*B*D/H	250*250*300		
15.2	Beam for RTT/RTP/Delta	Beam L*B*D/H	350*350*300		
16	Check for support and Shuttering oil	Application of oil	Ok		
17	Check on concrete operation	Visual Inspection	Ok		

For, EXCEL ELECTRICALS


AUTH. SIGN.

18	Ensure Cubes Taken	06 Nos	00		
19	Projection of Anchor bolt (in mm)		150		
20	Grout under baseplate (in mm)	Thickness	10		
Post casting					
21.1	De-shuttering & curing of pedestal	7 days Curing by water	7day		
21.2	Application of curing compound	curing compound	water		
22.1	Pedestal is made as per the drawing & specification	Pedestal L*B*D/H	250*250*300		
22.2	Beam is made as per the drawing & specification	Beam L*B*D/H	350*350*300		
23	Visual check in concrete pedestal	No Crack and Honeycomb	Ok		
24	Restoration of waterproofing membrane	Visual Inspection	Ok		
25	Making hauler/vatta	Visual Inspection	Ok		
26	Apply two coats of polymer based waterproofing paints as per consultant's recommendation	Visual Inspection	Ok		
27	Check for Pond Test	Test Certificate	Ok		
28	Check for leveling of pedestal for RTP/RTT erection	Check with Sprit level/Tube level	Ok		

For, EXCEL ELECTRICALS


AUTH. SIGN.


29	Overall Finishing of the site	Visual Inspection	Ok		
30	Cube strength for 7 days	60% & Above	00		
31	Cube strength for 28 days	100% & Above	00		

Observations and Comments:


Observations and Comments N/mm2

For, EXCEL ELECTRICALS


AUTH. SIGN.

CFQ details			
	Contractor's representative	Field Engineer	QC Engineer
Signature			
Name	jagdish	dilraj	
Date	04 November 2022	04 November 2022	--


For Anil Sir


ANIL SHAH
 MPCM-VADODARA-2
 Mob. No. 9374710314

(Anil Sir on Leave)
 PM - Vadodra-2 MO

For, EXCEL ELECTRICALS


 AUTH. SIGN.

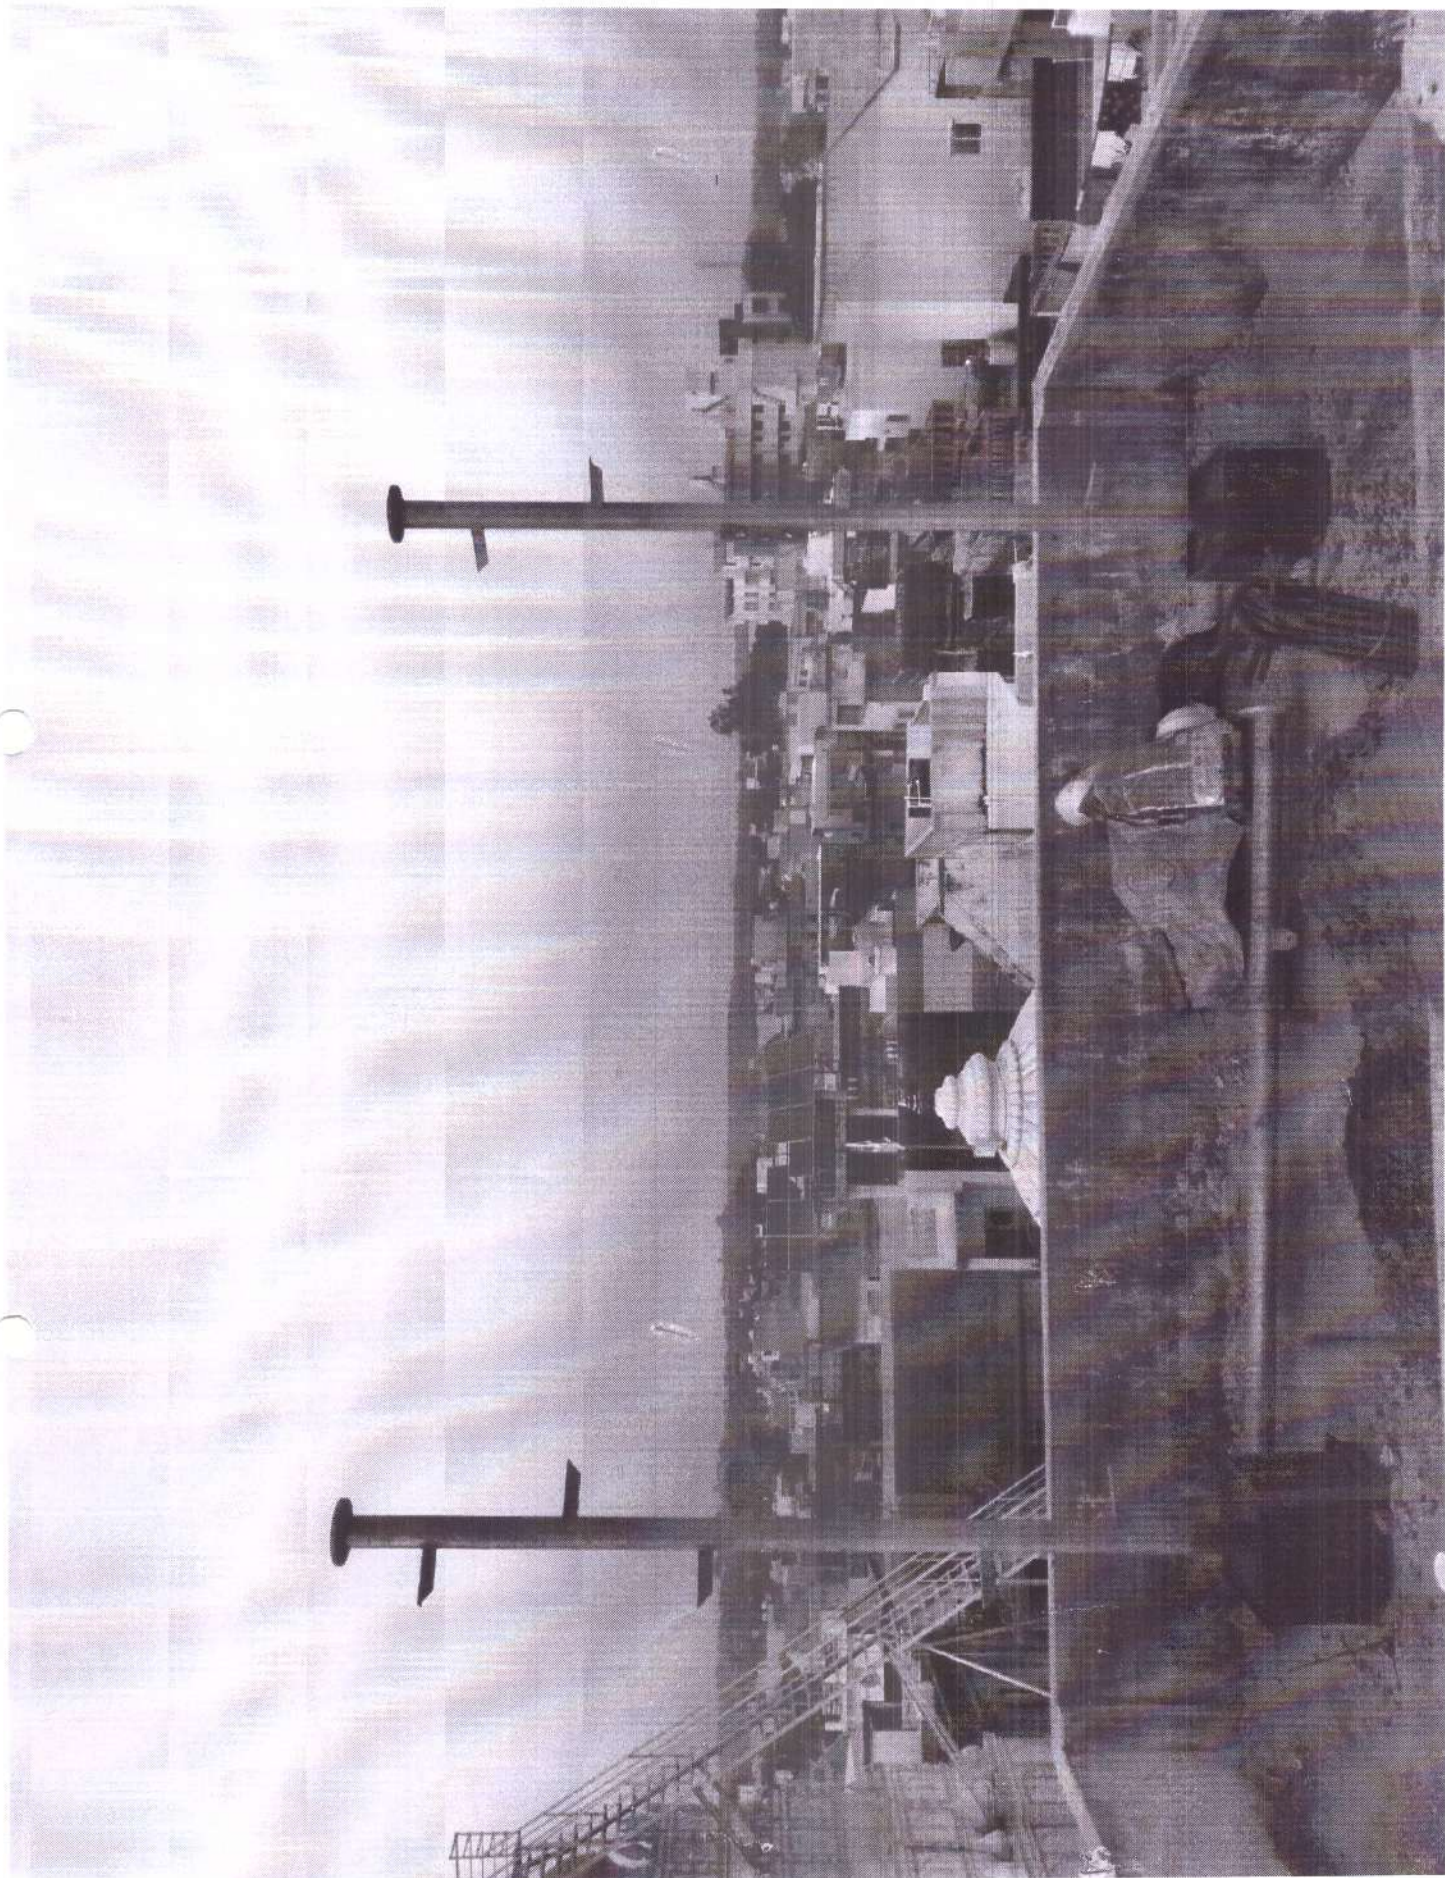

Dilraj
DILRAJ CHAVDA
MO. 9978573433
FE-VADODARA-2

For, EXCEL ELECTRICALS
[Signature]
AUTH. SIGN.

Ref. No.


Date :

This is to inform and certify that **M/S. Excel Electricals** will not be deploying 20 or more contract workmen/labour on any day during the execution of the contract work in the allotted vide Work Order No. P21/630213338

However, in future, if ever the number of contract workmen to be deployed exceeds the stipulated statutory number of 20 or more workmen, the contractor will immediately apply and obtain labour license for the required capacity from the concerned Licensing Authority under CL(R&A) Act, 1970/Central Rules, 1971.

Thanking You,

For, EXCEL ELECTRICALS



AUTH. SIGN.



GOVT. APPROVED CIVIL, EHV, HT, LT ELECTRICALS,
TELECOM WORKS & LABOUR CONTRACTORS

Ref. No.

Tel. : (0288) 2555750
M. : 97129 09040, 93774 58805
E-mail: excel19680@gmail.com
excel19680@rediffmail.com

116, Siddhnath Complex,
1st Floor, Near Indian Bank,
K. V. Road, Jamnagar - 361 001

Date :

To,

Reliance Projects and Property Management Services Limited

5, TTS Industrial Area, Thane Belapur Road,

Ghansoli, Navi Mumbai - 400701

I/We/M/s. **EXCEL ELECTRICALS**. Hereby declare that we will not engage any child labour or Inter State Migrant Workmen on any day during the period of contract in the establishment of **M/s Reliance Digital Platform & Project Services Limited** for execution of the work awarded to us vide WO No. **P21/630213338**

We hereby indemnify M/s Reliance Corporate IT Park Limited against any legal hassles arising due to lapses on our part under **The Child Labour (Prohibition & Regulation) Act 1986 and Inter State Migrant Workmen (Regulation of Employment and Conditions of Services) Act, 1979.**

Thanking You,

(Authorized Signatory)

For, EXCEL ELECTRICALS


AUTH. SIGN.

Serial No. 454/202

23-9-21



सत्यमेव जयते

INDIA NON JUDICIAL NOTARY

Government of Gujarat

Certificate of Stamp Duty

Certificate No. : IN-GJ26100522199170T
Certificate Issued Date : 23-Sep-2021 05:36 PM
Account Reference : IMPACC (AC)/ gj13336711/ GULBAI TEKRA/ GJ-AH
Unique Doc. Reference : SUBIN-GJGJ1333671186961021756150T
Purchased by : EXCEL ELECTRICAL
Description of Document : Article 14 Bond
Description : Not Applicable
Consideration Price (Rs.) : 0
(Zero)
First Party : EXCEL ELECTRICAL
Second Party : Not Applicable
Stamp Duty Paid By : EXCEL ELECTRICAL
Stamp Duty Amount(Rs.) : 500
(Five Hundred only)



Abuzar

KC 0015322762

For, EXCEL ELECTRICALS

AUTH. SIGN.

P131

Last Updationon :25.11.16

DECLARATION CUM INDEMNITY BOND


THIS DECLARATION CUM INDEMNITY BOND made at by M/s Excel Electrical their registered Office at **116, Siddhnath Complex, K.V. Road, Near Indian Bank, Jamnagar-361001** (hereinafter referred to as “**Contractor**” which expression shall unless it be repugnant to the context or meaning thereof, be deemed to mean and include their respective assigns, successors, executors and/or administrators) of the ONE PART in favor of the Company M/s. **Reliance Projects And Property Management Service Limited**

Registered under the Companies Act, 1956, and having its registered office at **Auda TP Scheme, Bodakdev No 1/A F P No.5 2nd Floor, Opp. Drive-in Cinema, Drive-in Road Ahemdabad-380054** (hereinafter referred to as the “**Company**”, which expression shall unless it be repugnant to the context or meaning thereof be deemed to mean and include its assigns, successors,) of the OTHER PART.

WHEREAS the Company has entered into a contract by issuing Work Order(s) to the Contractor for the

P21/54023589	P21/630132499	P21/630144520	P21/630144516
P21/630150017	P21/630150100	P21/630149196	P21/630149213
P21/630147145	P21/630143718	P21/630143719	P21/630152402
P21/630152403	P21/630150746	P21/630155636	P21/630155637
P21/630155650	P21/630155651	P21/630157110	P21/630157111
P21/630159071	P21/630159081	P21/630160651	P21/630160652
P21/630161205	P21/630162363	P21/630163207	P21/630163602
P21/630163292	P21/630163294	P21/630163603	P21/630163680
P21/630163207	P21/630162369	P21/630164228	P21/630164230
P21/630164338	P21/630164360	P21/630165881	P21/630165883
P21/630166047	P21/630166913	P21/630168426	P21/630168427
P21/630170776	P21/630169751	P21/630169585	P21/630169584
P21/630170205	P21/630170206	P21/630170809	P21/630170811
P21/630171733	P21/630173004	P21/630173001	P21/630172817
P21/630174759	P21/630174215	P21/630174208	P21/630173920
P21/630177304	P21/630177299	P21/630177208	P21/630177206
P21/630176190	P21/630174761	P21/630174759	P21/630177302
P21/630177300	P21/630179113	P21/630179110	P21/630178361
P21/630186317	P21/630186315	P21/630184297	P21/630180929
P21/630180926	P21/630180228	P21/630195709	P21/630195708
P21/630195706	P21/630195705	P21/630195703	P21/630194522
P21/630191437	P21/630191436	P21/630188716	P21/630188720
P21/630187840	P21/630186905	P21/630186908	

For, EXCEL ELECTRICALS


AUTH. SIGN.

(Hereinafter called the “**Contract**”)

P131

Last Updationon :25.11.16

(Hereinafter called the "**Contract**")

AND WHEREAS it is one of these essential conditions of the Contract that the Contractor shall comply with all the provisions of the Labor & Industrial Laws, as may be applicable from time to time for the discharge and completion of the Works and/or Services covered under said Contract by the Contractor including but not limited to the observance and compliance of The Contract Labor (R & A) Act 1970, Child Labor (Prohibition and Regulation) Act 1986, The Employees Provident Funds & Miscellaneous Provisions Act, 1952, Employees State Insurance Act 1948, Minimum Wages Act, 1948, Payment of Bonus Act, 1965, Payment of Wages Act, 1936, Employees Compensation Act.1923, and other Labor Laws applicable to the contractor (hereinafter referred as the '**Laws**').

AND WHEREAS the Contractor has agreed to execute this Declaration cum Indemnity Bond to this effect and has agreed to indemnify and keep the Company, its directors and employees and representatives indemnified and hold harmless against all third party claims, charges, penalties, fines, expenses, losses, damages, costs, suits or any other levy against the Company and/or the management due to the failure of the Contractor to observe or follow any Laws.

NOW THIS DEED WITNESSETH AS UNDER:

1. In consideration of the Company awarding the Contract/ Work Order to the Contractor subject to the condition of execution of this Declaration cum Indemnity bond, the Contractor declares and represents to the Company that the Contractor has obtained all statutory registrations, certificates, licenses and approvals required under the Laws enabling the Contractor to execute the Contract in a legal and lawful manner.
2. That in the event of any liability arising out of non-compliance of any such 'Laws' by the Contractor in connection with the execution of the Contract, the Contractor shall bear all the resultant whatsoever liability(IES), if any arising out thereof and that the Company, its directors, employees, representatives, shall not be liable for any such liability(IES). The Contractor agrees to indemnify and keep the Company and its directors, employees, representatives indemnified, defend and hold harmless, against all losses, costs, damages, claims, penalties, interest, expenses, demands, fines, legal liability, causes of action, injury to persons suites which may be suffered, incurred, undergone and / or sustained by the Company including the costs and expenses that may be incurred in defending any such liability(ies) claim(s), proceeding(s) etc. that may be made or taken or arise on the same by any person, body, authority, government, judicial / quasi-judicial authority due to the failure or noncompliance of any such laws and rules there under (including any amendments in acts, laws, statutes & rules there under) of whatsoever kind and nature arising out of or in any way connected with, whether or not such acts or omissions are actual or alleged, active or passive with regard to the discharge of the said Contract.
3. The Contractor hereby agrees and undertakes to make good any loss, damage, penalties, interests, claims, suits, demands, decrees, expenses that the Company may suffer to the fullest satisfaction of the Company and if the Contractor fails to make good the same then the Company shall have the right to recover the same and or any other loss sustained, without any restriction or limitation, together with any other incidental expenses, costs, and all incidental logistic expenses etc that may be suffered by the Company, from the Contractor.

For, EXCEL ELECTRICALS

AUTH. SIGN.

P131

Last Updationon :25.11.16

4. The Contractor hereby further confirms and declares that this Declaration cum Indemnity Bond is irrevocable and shall be final and binding on it / him heirs, executors, administrators, legal representatives, successors and assigns, wherever the context applies. Any claims, demands, shall be adjusted against any amount due and payable to the Contractor and the Company shall have the right to withhold any amounts due and payable to the Contractor, till the settlement of such claims, disputes to the satisfaction of the Company or alternatively make demand sufficient security from the Contractor towards discharge of such claims, obligations etc.
5. The Declaration cum Indemnity Bond shall be applicable for any and all Work Orders issued to the Contractor in this regard.
6. This Declaration cum indemnity bond shall be in accordance with the laws of India and any dispute between the parties with regard to this Declaration cum Indemnity Bond shall be resolved through the dispute resolution process mentioned in the General Conditions of the Contract (GCC).
7. Any terms used in this indemnity bond, but not expressly defined herein shall have the meaning assigned to it in the General terms and Conditions (GTC) forming part of the Work Orders issued.

IN WITNESS WHEREOF, the said Contractor has hereunto set their hand the day and year first hereinabove written.

SIGNED SEALED AND DELIVERED
By the within named "CONTRACTOR")

For, EXCEL ELECTRICALS

Chit

AUTH. SIGN.

(Authorized Signatory)
Rubber Stamp of Firm/Company
Name:
Designation:
Date:

Contractor

BEFORE ME

Signature

A. M. UJJAINI
NOTARY
GOVT. OF INDIA

23/9/21

For, EXCEL ELECTRICALS

Signature
AUTH. SIGN.



RELIANCE PROJECTS & PROPERTY MANAGEMENT SERVICES LIMITED

(FORMERLY RELIANCE DIGITAL PLATFORM & PROJECT SERVICES LTD)

AUDA TP SCHEME, BODAKDEV NO: 1/A,, F P NO.: 5, 2ND FLOOR,

OPP. DRIVE IN CINEMA, DRIVE IN ROAD, AHMEDABAD-380054, GUJARAT, INDIA

Telephone : +91 79 -8879387831/40014190

Email: SUNILKUMAR.LIMBACHIA@RIL.COM

**WORK ORDER**

To 399452 EXCEL ELECTRICALS 116, SIDDHNATH COMPLEX, K. V. ROAD, NR. INDIAN BANK JAMNAGAR GUJARAT Pin Code : 361001 INDIA Phone : +91-288-2555750 Fax : E-Mail : EXCEL19680@GMAIL.COM Attention : PARESH LUNAGARIYA	Work Order No. : P21/630213338 Date : 27.09.2022 Contractor's Quot. Ref : Date : Our Ref : 6000 GSTN Of Biller : 24AADFE1348L1ZJ Bill From State : Gujarat Bill From : 399452
--	---

This WORK ORDER, the SPECIAL CONDITIONS OF CONTRACT, the GENERAL CONDITIONS OF CONTRACT, the annexures enclosed to each of the foregoing, including any other document forming part of CONTRACT DOCUMENTS contain all the express terms and conditions of contract of supply of SERVICES ordered pursuant to this WORK ORDER and confirms and supersedes the LETTER OF COMMITMENT (if any) issued by COMPANY. CONTRACTOR agrees to supply the SERVICES, including all DELIVERABLES in full accordance with the foregoing terms and conditions. Capitalized terms used in this WORK ORDER but not defined in the WORK ORDER shall have the meaning ascribed to such terms in the foregoing SPECIAL CONDITIONS OF CONTRACT and GENERAL CONDITIONS OF CONTRACT. CONTRACTOR shall sign and return this WORK ORDER acknowledging the acceptance of this WORK ORDER within three (3) days of receipt at the communication address mentioned in this WORK ORDER. If acknowledgement is not received within three (3) days, this WORK ORDER will be deemed accepted by the CONTRACTOR. No other form of acceptance shall be binding on the PARTIES. For all future correspondence please quote this WORK ORDER NUMBER.

WO Period From DT : 27.09.2022 To DT : 31.12.2022	Value of Work CGST SGST	INR 16,379.38 INR 1,474.14 INR 1,474.14
TOTAL ORDER VALUE		INR 19,327.66
Value in Words : (Rs. Nineteen Thousand Three Hundred Twenty Seven and Paise Sixty Six only) For other details, please refer line items.		
Delivery Terms : N/A . Engineer in Charge : Anil Shah		
Payment Terms : See Page Inside		
BUYER : Shah	for RELIANCE PROJECTS & PROPERTY MANAGEMENT SERVICES LIMITED (FORMERLY RELIANCE DIGITAL PLATFORM & PROJECT SERVICES LTD) Authorised Signatory	CONTRACTOR'S Acceptance Signature Title Date

REGISTERED OFFICE : Office-101, Saffron, Nr. Centre Point, Panchwati Rasta, Ambawadi, Ahmedabad - 380006

ANIL SHAH
MPCM-VADODARA-2
Mob. No. 9374710314

(Anil for in leave)
Vadoder- 2 MP

For, EXCEL ELECTRICALS**AUTH. SIGN.**



WORK ORDER

W.O.Number
Page No: 1

P21 / 630213338 Dt.27.09.2022

WORK ORDER ISSUED FOR ODSC LATTICE_ESC WORKS_CIVIL_1 SITES AT NORTH GUJARAT

(Including Digital Conditions)

1. FIM - Applicable
2. Indemnity Clause - Applicable
3. Performance Bank Guarantee(BG)- Applicable
4. Retention Clause - Applicable
5. DLP - 12 Months

No	Item Code	Material/Work Description	Quantity	UOM	Price Details	Unit Rate	Amount (INR)
1	I-GJ-BLSN-ESC-0010	RTP 6 39	1	AU			
					Value of Work	INR/AU	15,625.00
					CGST	9.00 %	1,406.25
					SGST	9.00 %	1,406.25
		Service Accounting Number:	995428				

The item covers the following Work :

10 3339785 CHRG CVL ODSC RT 6M STAY 2POLE 50

Charges for providing materials and services for execution of CIVIL work for OUTDOOR SMALL CELL (ODSC) ROOF TOP WORKS 6M, WITH STAY, 2 Pole combination 50 m/s WIND SPEED. The scope of the work includes chipping / removal of water proofing/PCC, fixing of reinforcement dowels using chemical grouts, supply & installation of galvanized foundation bolts, construction of pedestals, and beams, cube test, supply and placement of non-shrink grout below base plate, shifting of materials to roof top and other misc. works. The site work shall be completed in all respects as per approved drawings, specifications, scope of work, and as per directions of Engineer In Charge. #

Net value of item 15,625.00

2	I-GJ-BLSN-ESC-0010	STEEL	1	AU			
					Value of Work	INR/AU	754.38
					CGST	9.00 %	67.89
					SGST	9.00 %	67.89
		Service Accounting Number:	995428				

The item covers the following Work :

10 3243408 DIFFERENTIAL PAYMENT FOR RATE INCREASE

Differential Charges to be paid for the rate increase.

41.910 EA - each
Net value of item 18.00

754.38

For, EXCEL ELECTRICALS

AUTH. SIGN.



WORK ORDER

W.O.Number P21 / 630213338 Dt.27.09.2022
Page No: 2

Total Value of Work	16,379.38
Total CGST	1,474.14
Total SGST	1,474.14

Total Order Value:	19,327.66
--------------------	-----------

Terms of payment :

Payment shall be made as per Detailed Payment Terms specified in the purchasing document.

Vendor Bank Details:

Bank Account No. : 5291462239
Bank Name : CENTRAL BANK OF INDIA
City : JAMNAGAR

Liquidated Damages :

0.5 % PER WEEK TO MAX OF 5%

Engineer-In-charge :

Anil Shah
Ankur Shah
Arvind Pipaliya
Chandrajeet Yadav
Girish Modi
Pavan Pandey
Nayan Patel
Saurabh Desai
Rakesh Shah
Kamal Patel
Pitar Simon
Jignesh Bhayani
Satish Padhiyar
Kapil Gurubaxani
Alex Rao
Chirag Shah

Document Submission Bank:

Note(S): 1. It is essential that the Contractor shall mention ItemNo. & Item code along with corresponding Material/Work Description and W.O.No. as mentioned above, in the Delivery challan (On-Shore Order), Measurement sheet and invoice for ease of material Inwarding, Certification of work and Bill Processing. Failure to do so may be the grounds for the rejections(s) or delay in release of payment(s).

PLANT REGISTRATION NO. : 24AAJCR6636B1ZI

For, EXCEL ELECTRICALS

AUTH. SIGN.
